

RESOLUTION NO. 2012 - 62

**A RESOLUTION BY THE BOARD OF COUNTY COMMISSIONERS OF ST. JOHNS COUNTY, FLORIDA, AUTHORIZING THE COUNTY ADMINISTRATOR, OR DESIGNEE, TO AWARD BID NO. 12-31 AND TO EXECUTE AN AGREEMENT FOR INNLET BEACH WTP HIGH SERVICE PUMPS UPGRADE.**

**RECITALS**

**WHEREAS**, the County desires to enter into a contract with Sawcross, Inc. to provide services for Innlet Beach WTP High Service Pumps Upgrade; and

**WHEREAS**, the scope of the project shall generally include furnishing all labor, materials, equipment and other items necessary for providing a new fire pump and total turnkey installation; and

**WHEREAS**, through the County's formal bid process, Sawcross, Inc. was selected as the most qualified respondent to enter into a contract with the County to perform the work referenced above; and

**WHEREAS**, the County has reviewed the terms, provisions, conditions and requirements of the Contract (attached hereto, an incorporated herein) and finds that entering into the Contract serves a public purpose.

**NOW, THEREFORE BE IT RESOLVED BY THE BOARD OF COUNTY COMMISSIONERS OF ST. JOHNS COUNTY, FLORIDA**, as follows:

Section 1. The above Recitals are incorporated by reference into the body of this Resolution and such Recitals are adopted as finds of fact.

Section 2. The County Administrator, or designee, is hereby authorized to award Bid No. 12-31 Innlet Beach WTP High Service Pumps Upgrade to Sawcross, Inc.

Section 3. The County Administrator, or designee, is further authorized to execute the attached Contract with Sawcross, Inc. on behalf of the County for the completion of the Innlet Beach WTP High Service Pumps Upgrade specifically provided in Bid No 12-31.

Section 4. To the extent that there are typographical and/or administrative errors that do not change the tone, tenor, or concept of this Resolution, then this Resolution may be revised without subsequent approval by the Board of County Commissioners.

**PASSED AND ADOPTED** by the Board of County Commissioners of St. Johns County, Florida, this 21 day of February, 2012.

**BOARD OF COUNTY COMMISSIONERS  
OF ST. JOHNS COUNTY, FLORIDA**


By: [Signature]  
Chair

ATTEST: Cheryl Strickland, Clerk

By: [Signature]  
Deputy Clerk

RENDITION DATE 2/23/12





**ST. JOHNS COUNTY  
PURCHASING DEPARTMENT**

2446 Dobbs Road  
St. Augustine, Florida 32086

---

**I N T E R O F F I C E   M E M O R A N D U M**

---

**TO:** Scott Triggs, P.E., Engineer II *ST*  
**FROM:** Sharon Haluska, Contract Administrator *SH*  
**SUBJECT:** Transmittal of Bids Received for Bid No. 12.31; Innlet Beach Water Treatment Plant  
High Service Pumps Upgrade  
**DATE:** January 18, 2012

Attached are copies of the bid proposals received for the above mentioned along with a copy of the Bid Tabulation Sheet.

Please review, evaluate and make a written recommendation for this project. Also, indicate the budgeted amount for this item along with the appropriate charge code and return at your earliest convenience. We will prepare the agenda item and contract.

Please let me know if I can assist your department in any other way.

Dept. Approval *ST*

Date 1/19/12

Budget Amount \$550,000.00

Account Funding Title 4459-56302-6689

Funding Charge Code Innlet WTP Upgrades

Award to Sawcross, Inc.

Award Amount \$547,400.00

JAN 19 2012

Approved: *Initial & Date*  
Prepared By: \_\_\_\_\_  
Approved By: \_\_\_\_\_

**STANDARD AGREEMENT  
BETWEEN  
OWNER AND CONTRACTOR**

1992 EDITION  
(REVISED 5/19/11)

These Contract Documents should be used only after consultation with counsel. The documents are not intended as legal advice appropriate to any specific situation, nor do they purport to address all issues which may arise between the contracting parties. The documents should be amended or supplemented where appropriate in order to address contractual concerns.

This Agreement is made \_\_\_\_\_, 2012 by and between **St. Johns County, 500 San Sebastian View, St. Augustine, Florida 32084** (hereafter referred to as the "Owner") and **Sawcross, Inc., 10970 New Berlin Road, Jacksonville, FL 32226 (904) 751-7500 (p) (904) 751-0600 (f)** hereinafter referred to as the "Contractor") under seal for Construction of **Bid No.: 12-31 Inlet Beach WTP High Service Pumps Upgrade** hereinafter referred to as the "Project"), the Owner and the Contractor hereby agreeing as follows:

**ARTICLE I  
THE CONTRACT AND THE CONTRACT DOCUMENTS**

**1.1 The Contract**

1.1.1 The Contract between the Owner and the Contractor, of which this Agreement is a part, consists of the Contract Documents. It shall be effective on the date this Agreement is executed by the last party to execute it.

**1.2 The Contract Documents**

1.2.1 The Contract Documents consist of this Agreement, the Bid Documents and Bid Forms, Specifications, all Change Orders and Field Orders issued hereafter and executed by the parties and the Engineers, any other amendments hereto executed by the parties hereafter, together with the following (if any): Sawcross, Inc.'s Bid Proposal dated 1/18/21; Addendum 1; Bonds & Insurances.

(Here list any additional Contract Documents such as addenda special conditions, supplemental conditions, etc.)

Documents not enumerated in this Paragraph 1.2.1 are not Contract Documents and do not form part of this Contract.

**1.3 Entire Agreement**

1.3.1 This Contract, together with the Contractor's Public Construction Bond (if applicable) for the Project, constitutes the entire and exclusive agreement between the Owner and the Contractor with reference to the Project. Specifically, but without limitation, this Contract supersedes any Bid Documents

not listed among the Contract Documents described above and all prior written or oral communications, representations and negotiations, if any, between the Owner and Contractor.

#### **1.4 No Privity with Others**

1.4.1 Nothing contained in this Contract shall create, or be interpreted to create, privity or any other contractual agreement between the Owner and any person or entity other than the Contractor.

#### **1.5 Intent and Interpretation**

1.5.1 The intent of this Contract is to require complete, correct and timely execution of the Work. Any work that may be required implied or inferred by the Contract Documents, or any one or more of them, as necessary to produce the intended result shall be provided by the Contractor for the Contract Price.

1.5.2 This Contract is intended to be an integral whole and shall be interpreted as internally consistent. What is required by any one Contract Document shall be considered as required by the Contract.

1.5.3 When a word, term or phrase is used in this Contract, it shall be interpreted or construed, first, as defined herein; second, if not defined, according to its generally accepted meaning in the construction industry; and third, if there is no generally accepted meaning in the construction industry, according to its common and customary usage.

1.5.4 The words "include," "includes" or "including," as used in this Contract, shall be deemed to be followed by the phrase "without limitation."

1.5.5 The specification herein of any act, failure, refusal, omission, event, occurrence, or condition as constituting a material breach of this Contract shall not imply that any other, non-specified act, failure, refusal, omission, event, occurrence, or condition shall be deemed not to constitute a material breach of this Contract.

1.5.6 Words or terms used as nouns in this Contract shall be inclusive of their singular and plural forms, unless the context of their usage clearly requires a contrary meaning.

1.5.7 The Contractor shall have a continuing duty to read, carefully study and compare each of the Contract Documents, the Shop Drawings and the Product Data and shall give written notice to the Engineer and the Owner of any inconsistency, ambiguity, error or omission which the Contractor may discover with respect to these documents before proceeding with the affected Work. The issuance, or the express or implied approval by the Owner or the Engineer of the Contract Documents, Shop Drawings, or Product Data shall not relieve any such approval by evidence of the Contractor's compliance shall any such approval be evidence of the Contractor's compliance with this Contract. The Owner has requested the Engineer to only prepare documents for the Project, including the Drawings and Specifications for the Project, which are accurate, adequate, consistent, coordinated, and sufficient for construction. **HOWEVER, THE OWNER MAKES NO REPRESENTATION OR WARRANTY OF ANY NATURE WHATSOEVER TO THE CONTRACTOR CONCERNING SUCH DOCUMENTS.** By the execution hereof, the Contractor acknowledges and represents that it has received, reviewed and carefully examined such documents, has found them to be complete, accurate, adequate, consistent, coordinated and sufficient for construction, and that the Contractor has not, does not, and shall not rely upon any representation or warranties by the Owner concerning such documents as no such representation or warranties have been or are hereby made.

1.5.8 As between numbers and scaled measurements on the Drawings and in the Design, the numbers shall govern; as between larger scale and smaller scale drawings, the larger scale shall govern.

1.5.9 Neither the organization of any of the Contract Documents into divisions, sections, paragraphs, articles, (or other categories), nor the organization or arrangement of the Design, shall control the Contractor in dividing the Work or in establishing the extent or Scope of Work to be performed by Subcontractors.

## **1.6 Ownership of Contract Documents**

1.6.1 The Contract Documents, and each of them, shall remain the property of the Owner. The Contractor shall have the right to keep one record set of the Contract Documents upon completion of the Project; provided, however, that in no event shall Contractor use, or permit to be used, any or all of such Contract Documents on other projects without Owner's prior written authorization.

## **ARTICLE II THE WORK**

2.1 The Contractor shall perform all of the Work required, implied, or reasonably inferable from, this Contract.

2.2 The term "Work" shall mean whatever is done by or required of the Contractor to perform and complete its duties under this Contract, including the following: construction of the whole or a designated part of the Project in the manner set forth in the Contract Documents; furnishing of any required Surety Bonds and insurance; and the provision or furnishing of labor, supervision, services, materials, supplies, equipment, fixtures, appliances, facilities, tools, transportation, storage, power, permits and licenses required of the Contractor, fuel, heat, light, cooling and all other utilities as required by this Contract. The Work to be performed by the Contractor is generally described as follows:

*The Scope of Work for this project shall generally include furnishing all labor, materials, equipment and other items necessary construct the upgrades. The scope of work shall include but not necessarily be limited to the following:*

1. *Mobilization/Demobilization, General Requirements, Bonds and Insurance*
2. *Site Work and Above Grade Yard Piping*
  - a. *Erosion and sedimentation control*
  - b. *Site restoration including grassing, and other restoration*
  - c. *Installation and testing of 16-inch pipe and valves between the existing GST and existing pump station building*
  - d. *Sidewalk installation between the existing pavement and electrical building*
  - e. *Seeding*
3. *High Service Pumps Upgrade*
  - a. *Removal of the existing four (4) high service pumps*
  - b. *Installation of four (4) new horizontal split-case centrifugal pumps supplied by the OWNER*
  - c. *Installation and testing of 10-inch suction pipe and valves, and upgraded connection tees to suction of pumps No. 2, 3 and 4*
  - d. *Installation of prefabricated concrete electrical building and associated mechanical and electrical equipment*
4. *Coordination with DCR on instrumentation programming*
5. *Pump Station startup*

6. *Permits including Notice of Intent, St. Johns River Water Management District dewatering permit, St. Johns County building permit for prefabricated electrical building, and other which are necessary. ENGINEER and OWNER have secured FDEP permit modification. All work shall be bid and performed specifically in accordance with the specifications and drawings. as provided as part of the bid documents.*

### ARTICLE III CONTRACT TIME

#### 3.1 Time and Liquidated Damages

3.1.1 The Contractor shall commence the Work within ten (10) days upon receipt of the Notice to Proceed and shall Substantially Complete all Work within Ninety (90) consecutive calendar days. Final Completion shall be Fifteen (15) consecutive calendar days after Substantial Completion.

The number of calendar days from the date on which the Work is permitted to proceed, through the date set forth for Final Completion, shall constitute the "Contract Time."

3.1.2 The Contractor shall pay the Owner the sum of \$ 1,423.00 per day for each and every calendar day of unexcused delay in achieving Substantial Completion beyond the date set forth herein for Substantial Completion of the Work. Any sum's due and payable hereunder by the Contractor shall be payable, not as a penalty, but as liquidated damages representing an estimate of delay damages likely to be sustained by the Owner, estimated at or before the time of executing this Contract. When the Owner reasonably believes that Substantial Completion shall be inexcusably delayed the Owner shall be entitled, but not required, to withhold from any amounts otherwise due the Contractor an amount then believed by the Owner to be adequate to recover liquidated damages applicable to such delays. If and when the Contractor overcomes the delay in achieving Substantial Completion, or any part thereof, for which the Owner has withheld payment, the Owner shall promptly release to the Contractor those funds withheld, but no longer applicable, as liquidated damages.

#### 3.2 Substantial Completion

3.2.1 "Substantial Completion" shall mean that stage in the progression of the Work when the Work is sufficiently complete in accordance with this Contract that the Owner can enjoy beneficial use or occupancy of the Work and can utilize the Work for its intended purpose.

#### 3.3 Time is of the Essence

3.3.1 All limitations of time set forth in the Contract Documents are of the essence of this Contract.

### ARTICLE IV CONTRACT PRICE

#### 4.1 The Contract Price

4.1.1 The Owner shall pay, and the \$ Five Hundred & Forty-Seven Thousand Four Hundred Dollars & XX/Cents (\$547,400.00). The sum set forth in the Paragraph 4.1 shall constitute the Contract Price, which shall not be modified except by Change Order as provided in this Contract.

**ARTICLE V  
PAYMENT OF THE CONTRACT PRICE**

**5.1 Schedule of Values**

5.1.1 Within ten (10) calendar days of the effective date hereof, the Contractor shall submit to the Owner and to the Project Director a Schedule of Values allocating the Contract Price to the various portions of the Work. The Contractor's Schedule of Values shall be prepared in such form, with such detail, and supported by such data as the Project Director or the Owner may require to substantiate its accuracy. The Contractor shall not imbalance its Schedule of Values nor artificially inflate any element thereof. The violation of this provision by the Contractor shall constitute a material breach of this Contract. The Schedule of Values shall be used only as a basis for the Contractor's Applications for Payment and shall only constitute such basis after it has been agreed upon in writing by the Project Director and the Owner. The Owner may terminate this Contract without liability of any kind if the Schedule of Values is not agreed upon within fifteen (15) calendar days of the effective date hereof.

**5.2 Payment Procedure**

5.2.1 The Owner shall pay the Contract Price to the Contractor as provided below.

5.2.2 Progress Payments - Based upon the Contractor's Applications for Payment submitted to the Project Director and upon Certificates for Payment subsequently issued to the Owner by the Project Director, the Owner shall make progress payments to the Contractor on account of the Contract Price. Retainage in the amount of ten percent (10%) will be withheld from each progress payment until Owner has issued Final Acceptance.

5.2.3 On or before the fifteen (15) day of each month after commencement of the Work, the Contractor shall submit an Application for Payment for the period ending the thirtieth (30th) day of the previous month to the Project Director in such form and manner, and with such supporting data and content, as the Project Director may require. Therein, the Contractor may request payment for ninety percent (90%) of that portion of the Contract Price properly incorporated in the Work less the total amount of previous payments received from the Owner.

Such Application for Payment shall be signed by the Contractor and shall constitute the Contractor's representation that the Work has progressed to the level for which payment is requested that the Work has been properly installed or performed in full accordance with this Contract, and that the Contractor knows of no reason why payment should not be made as requested. Thereafter, the Project Director and Engineer shall review the Application for Payment and may also review the Work at the project site or elsewhere to determine whether the quantity and quality of the Work is as represented in the Application for Payment and is as required by this Contract. The Project Director shall determine and certify to the Owner the amount properly owing to the Contractor. The Owner shall make partial payments on accounts of the Contract Price within thirty (30) days following the Project Director's receipt of each Application for Payment. The amount of each partial payment shall be the amount certified for payment by the Project Director less such amounts, if any, otherwise owing by the Contractor to the Owner or which the Owner shall have the right to withhold as authorized by this Contract. The Project Director's certification of the Contractor's Application for Payment shall not preclude the Owner from the exercise of any of its rights as set forth in Paragraph 5.3 herein below.

5.2.4 The Contractor warrants that title to all Work covered by an Application shall pass to the Owner no later than time of payment. The Contractor further warrants that upon submittal of an Application for Payment, all Work for which payments have been received from the Owner shall be free and clear of liens, claims, security interest or other encumbrances in favor of the Contractor or any other person or entity whatsoever.

5.2.5 The Contractor shall promptly pay each Subcontractor out of the amount paid to the Contractor on account of such Subcontractor's Work, the amount to which such Subcontractor is entitled. In the event the Owner becomes informed that the Contractor has not paid a Subcontractor as herein provided, the Owner shall have the right, but not the duty, to issue future checks in payment to the Contractor of amounts otherwise due hereunder naming the Contractor and such Subcontractor as joint hereunder naming the Contractor and such Subcontractor as joint payees. Such joint check procedure, if employed by the Owner, shall create no rights in favor of any person or entity beyond the right of the named payees to payment of the check and shall not be deemed to commit the Owner to repeat the procedure in the future.

5.2.6 No progress payment, nor any use or occupancy of the Project by the Owner, shall be interpreted to constitute an acceptance of any Work not in strict accordance with this Contract.

### **5.3 Withheld Payment**

5.3.1 Owner may decline to make payment, may withhold funds and, if necessary, may demand the return of some or all of the amounts previously paid to the Contractor, to protect the Owner from loss because of:

- a) defective Work not remedied by the Contractor and, in the opinion of the Owner, not likely to be remedied by the Contractor;
- b) claims of third parties against the Owner or the Owner's property;
- c) failure by the Contractor to pay Subcontractors or others in a prompt and proper fashion;
- d) evidence that the balance of the Work cannot be completed in accordance with the Contract for unpaid balance of the Contract Price;
- e) evidence that the Work shall not be completed in the time required for Substantial or Final Completion;
- f) persistent failure to carry out the Work in accordance with the Contract;
- g) damage to the Owner or a third party to whom the Owner is, or may be, liable.

In the event that the Owner makes written demand upon the Contractor for amounts previously paid by the Owner as contemplated in this Subparagraph 5.3.1, the Contractor shall promptly comply with such demand.

### **5.4 Unexcused Failure to Pay**

5.4.1 If within ten (10) days after the date established herein for payment to the Contractor by the Owner, the Owner, without cause or basis hereunder, fails to pay the Contractor any amount due and payable to the Contractor, then the Contractor may after seven (7) additional days, written notice to the Owner and the Project Director, and without prejudice to any other available rights or remedies it may have, stop the Work until payment of those amounts due from the Owner have been received. Any payment not made within ten (10) days after the date due shall bear interest at the rate of 12 percent (12%) per annum.

### **5.5 Substantial Completion**

5.5.1 When the Contractor believes the Work is Substantially Complete, the Contractor shall submit to the Project Director a list of items to be completed or corrected. When the Project Director on the basis of an inspection determines that the Work is in fact Substantially Complete, he shall prepare a Certificate of Substantial Completion which shall establish the date of Substantial Completion, shall state the responsibilities of the Owner and the Contractor for Project security, maintenance, heat, utilities, damage



to the Work, and insurance, and shall fix the time within which the Contractor shall complete the items listed therein. Guarantees required by the Contract shall commence on the date of Substantial Completion of the Work. The Certificate of Substantial Completion shall be submitted to the Owner and the Contractor for their written acceptance of the responsibilities assigned to them in such certificate.

Until Final Completion and acceptance of the Work by the Owner, the Owner shall pay the Contractor an amount equal to ninety percent (90%) of the Contract price. Ten Percent (10%) of the Contract Price shall be retained until Final Completion, acceptance of the Work by the Owner and Final Payment to the Contractor.

## **5.6 Final Completion and Final Payment**

5.6.1 When all the Work is finally complete and the Contractor is ready for a Final Inspection, it shall notify the Owner and the Project Director thereof in writing. Thereupon, the Project Director shall make Final Inspection of the Work and, if the Work is complete in full accordance with this Contract and this Contract has been fully performed, the Project Director shall promptly issue a Final Certificate for Payment and if required to repeat its Final Inspection of the Work, the Contractor shall bear the cost of such repetition of the Work, the Contractor shall bear the cost of such repeat Final Inspection(s) which cost may be deducted by the Owner and all other Authorities having jurisdiction under Florida Laws or regulations.

5.6.1.1 If the Contractor fails to achieve Final Completion within the time fixed therefore by the Engineer in its Certificate of Substantial Completion, the Contractor shall pay the Owner liquidated damages at the sum shown in Paragraph 3.1.2, per day for each and every calendar day of unexcused delay in achieving Final Completion beyond the date set forth herein for Final Completion of the Work. Any sum's due and payable hereunder by the Contractor shall be payable, not as penalty, but as liquidated damages representing an estimate of delay damages likely to be sustained by the Owner, estimated at or before the time of executing the Contract. When the Owner reasonably believes that Final Completion shall be inexcusably delayed, the Owner shall be entitled, but not required, to withhold from any amounts otherwise due the Contractor an amount then believed by the Owner to be adequate to recover liquidated damages applicable to such delays. If and when the Contractor overcomes the delay in achieving Final Completion, or any part thereof, for which the Owner has withheld payment, the Owner shall promptly release to the Contractor those funds withheld, but no longer applicable, as liquidated damages.

5.6.2 The Contractor shall not be entitled to Final Payment unless and until it submits to the Project Director its affidavit that all payrolls, invoices for materials and equipment, and other liabilities connected with the Work for which the Owner, or the Owner's property might be responsible, have been fully paid or otherwise satisfied; releases and waivers of claims and lien from all Subcontractors of the Contractor and of any and all other parties required by the Project Director or the Owner; consent of Surety, if any, to Final Payment. If any third party fails or refuses to provide a release of claim or waiver of a lien as required by Owner the Contractor shall furnish a bond satisfactory to the Owner to discharge any such lien or indemnify the Owner from liability.

5.6.3 The Owner shall make Final Payment of all sums, due the Contractor within thirty (30) days of the Project Director's execution of a Final Certificate for Payment.

5.6.4. Acceptance of Final Payment shall constitute a waiver of all claims against the Owner by the Contractor except for those claims previously made in writing against the Owner by the Contractor, pending at the time of Final Payment, and identified in writing by the Contractor as unsettled at the time of its request for Final Payment.

## **ARTICLE VI THE OWNER**

## **6.1 Information, Services and Things Required from Owner**

6.1.1 The Owner shall furnish to the Contractor, at the time of executing this Contract, any and all written and tangible material in its possession concerning conditions below ground at the site of the Project. Such written and tangible material is furnished to the Contractor only in order to make complete disclosure of such material and for no other purpose. By furnishing such material, the Owner does not represent, warrant, or guarantee its accuracy either in whole, in part, implicitly, or at all, and shall have no liability therefore. The Owner shall also furnish surveys, legal limitations and utility locations (if known), and a legal description of the Project site. Copies may be provided instead of originals.

6.1.2 Excluding permits and fees normally the responsibility of the Contractor, the Owner shall obtain all approvals, easements, and the like required for construction.

6.1.3 The Owner shall furnish the Contractor, free of charge, 5 copies of the Contract Documents for execution of the Work. The Contractor shall be charged, and shall pay the Owner \$25.00 per additional set of Contract Documents which it may require.

## **6.2 Right to Stop Work**

6.2.1 If the Contractor persistently fails or refuses to perform the Work in accordance with this Contract, the Owner may order the Contractor to stop the Work, or any described portion thereof, until the cause for stoppage has been corrected, no longer exists, or the Owner orders that Work be resumed. In such event, the Contractor shall immediately obey such order.

## **6.3 Owner's Right to Perform Work**

6.3.1 If the Contractor's Work is stopped by the Owner under Paragraph 6.2, and the Contractor fails within seven (7) days of such stoppage to provide adequate assurance to the Owner that the cause of such stoppage shall be eliminated or corrected, the Owner may, without prejudice to any other rights or remedies the Owner may have against the Contractor, proceed to carry out the subject Work.

In such a situation, an appropriate Change Order shall be issued deducting from the Contract Price the cost of correcting the subject deficiencies, and compensation for the Owner's additional services and expenses necessitated thereby, if any. If the unpaid portion of the Contract Price is insufficient to cover the amount due the Owner, the Contractor shall pay the difference to the Owner.

## **ARTICLE VII THE CONTRACTOR**

7.1 The Contractor is again reminded of its continuing duty set forth in Subparagraph 1.5.7. The Contractor shall perform no part of the Work at any time without adequate Contract Documents or, as appropriate, approved Shop Drawings, Product Data or Samples for such portion of the Work. If the Contractor performs any of the Work where Contractor knows or should know such work involves a recognized error, inconsistency or omission in the Contract Documents without such notice to the Project Director and the Owner, the Contractor shall bear responsibility for such performance and shall bear the cost of correction.

7.2 The Contractor shall perform the Work strictly in accordance with this Contract.

7.3 The Contractor shall supervise and direct the Work using the Contractor's best skill, effort and attention. The Contractor shall be responsible to the Owner for any and all acts or omissions of the

Contractor, its employees and other engaged in the Work on behalf of the Contractor.

**7.4. Warranty**

7.4.1 The Contractor warrants to the Owner that all labor furnished to progress the Work under this Contract shall be competent to perform the tasks undertaken, that the product of such labor shall yield only first-class results, that materials and equipment furnished shall be of good quality, free from faults and defects and in strict conformance with this Contract. This warranty shall survive termination of this Contract and shall not be affected by Final Payment hereunder. All Work not conforming to these requirements may be considered defective.

7.5 Contractor shall obtain and pay for all permits, fees and licenses necessary and ordinary for the Work. The Contractor shall comply with all lawful requirements applicable to the Work and shall give and maintain any and all notices required by applicable law pertaining to the Work.

**7.6 Supervision**

7.6.1 The Contractor shall employ and maintain at the Project site only competent supervisory personnel. Absent written instruction from the Contractor to the contrary, the superintendent shall be deemed the Contractor's authorized representative at the site and shall be authorized to receive and accept any and all communications from the Owner or Assignees.

7.6.2 Key supervisory personnel assigned by the Contractor to this Project are as follows:

Name	Function
_____	_____
_____	_____
_____	_____

So long as the individuals named above remain actively employed or retained by the Contractor, they shall perform the functions indicated next to their names unless the Owner agrees to the contrary in writing. In the event one or more individuals not listed above subsequently assume one or more of those functions listed above, the Contractor shall be bound by the provisions of this Subparagraph 7.6.2 as though such individuals have been listed above.

7.7 The Contractor, prior to commencing the Work, shall submit to the Project Director for his information, the Contractor's schedule for completing the Work. The Contractor's schedule shall be revised no less frequently than monthly (unless the parties otherwise agree in writing) and shall be revised to reflect conditions encountered from time to time and shall be related to the entire Project. Each sum revision shall be furnished to the Project Director. Failure by the Contractor to strictly comply with the provisions of this Paragraph 7.7 shall constitute a material breach of this Contract.

7.8 The Contractor shall continuously maintain at the site, for the benefit of the Project Director, one record copy of this Contract marked to record on a current basis changes, selections and modifications made during construction. Additionally, the Contractor shall maintain at the site for the Project Director

the approved Product Data, Samples and other similar required submittals. Upon Final Completion of the Work, all of these record documents shall be delivered to the Owner.

**7.9 Product Data and Samples**

7.9.1 Product Data, Samples and other submittals from the Contractor do not constitute Contract Documents. Their purpose is merely to demonstrate the manner in which the Contractor intends to implement the Work in conformance with the information received from the Contract Documents. All Product Data, Samples and other submittals shall belong to the Owner and shall be delivered, or returned to Owner, as applicable, prior to Submittals shall belong to Owner and shall be delivered, or returned to Owner, as applicable, prior to Substantial Completion.

#### **7.10 Cleaning the Site and the Project**

7.10.1 The Contractor shall keep the site reasonably clean during performance of the Work. Upon Final Completion of the Work, the Contractor shall clean the site and the Project and remove all waste, together with all of the Contractor's property therefrom.

#### **7.11 Access to Work**

7.11.1 The Owner and the Project Director shall have access to the Work at all times from commencement of the Work through Final Completion. The Contractor shall take whatever steps necessary to provide access when requested.

#### **7.12 Indemnity**

7.12.1 To the fullest extent permitted by law, the Contractor shall indemnify and hold harmless the Owner, employees and officials from, and against, any, and all, administrative/legal/equitable liability, claims, damages, losses and expenses, including attorneys' fees, arising out of or resulting from performance of the work, noted in either the Scope of Work, or the Contract Documents, that are referenced and considered a part of this Contract. It is specifically noted that such liability, claims, damages, loss or expense includes any of those referenced instances attributable to bodily injury, sickness, disease, or death, or to injury to, or destruction of, personal and/or real property, including the loss of use resulting therefrom or incident to, connected with, associated with or growing out of direct and/or indirect negligent or intentional acts or omissions by the Contractor, a Subcontractor, or anyone directly, or indirectly employed by them, or anyone for whose acts the Contractor or Subcontractor may be liable, regardless of whether or not such liability, claim, damage, loss or expense is caused in part by a party indemnified hereunder.

7.12.2 In claims against any person or entity indemnified under this Paragraph 7.12 by an employee of the Contractor, a Subcontractor, any one directly or indirectly employed by them or anyone for whose acts they may be liable, the indemnification obligation under this Paragraph 7.12 shall not be limited by a limitation on amount or type of damages, compensation or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefits acts or other employee benefit acts.

#### **7.13 Safety**

7.13.1 The Contractor shall be responsible for supervising all safety precautions, including initiating and maintaining such programs in connection with the performance of the Contract and for adequate maintenance of traffic.

7.13.2 The Contractor shall designate a member of the on site construction team whose duty shall be the prevention of accidents. Unless notified otherwise in writing by the Contractor to the Owner and the Engineer, this person shall be the Contractor's Superintendent.

## **ARTICLE VIII**

### **CONTRACT ADMINISTRATION**

#### **8.1 Project Director**

8.1.1 The Project Director, unless otherwise directed by the Owner shall perform those duties and discharge those responsibilities allocated to the Project Director as set forth in this Contract. The Project Director shall be the Owner's representative from the effective date of this Contract until Final Payment has been made. The Project Director shall be authorized to act on behalf of the Owner only to the extent provided in this Contract.

8.1.2 The Owner and the Contractor shall communicate with each other in the first instance through the Project Director.

8.1.3 The Project Director shall be the initial interpreter of the requirements of the drawings and specifications and the judge of the performance there under by the Contractor. The Project Director shall render written or graphic interpretations necessary for the proper execution or progress of the Work with reasonable promptness on request of the Contractor.

8.1.4 The Project Director shall review the Contractor's Applications for Payment and shall certify to the Owner for payment to the Contractor, those amounts then due to the Contractor as provided in this Contract.

8.1.5 The Project Director shall have authority to reject Work, which is defective or does not conform to the requirements of this Contract. If the Project Director deems it necessary or advisable, the Project Director shall authority to require additional inspection or testing of the Work for compliance with Contract requirements at Contractor's expense.

8.1.6 The Project Director shall review and approve, or take other appropriate action as necessary, concerning the Contractor's submittals including Product Data and Samples. Such review, approval or other action shall be for the sole purpose of determining conformance with the design concept and information given through the Contract Documents.

8.1.7 The Project Director shall prepare Change Orders and may authorize minor changes in the Work by field order as provided elsewhere herein.

8.1.8 The Project Director shall, upon written request from the Contractor, conduct inspections to determine the date of Substantial Completion and the date of Final Completion, shall receive and forward to the Owner for the Owner's review and records, written warranties and related documents required by this Contract and shall issue a Final Certificate for Payment upon compliance with the requirements of this Contract.

8.1.9 The Project Director's decision in matters relating to aesthetic effect shall be final if consistent with the intent of this Contract.

#### **8.2 Claims by the Contractor**

8.2.1 All Contractor claims shall be initiated by written notice and claim to the Project Director. Such written notice and claims must be furnished within seven (7) days after occurrence of the event, or the first appearance of the condition, giving rise to the claim.

8.2.2 Pending final resolution of any claim of the Contractor, the Contractor shall diligently proceed with performance of this Contract and the Owner shall continue to make payments to the Contractor in accordance with this Contract. The resolution of any claim under this Paragraph 8.2 shall be reflected by a Change Order executed by the Project Director and the Contractor.

8.2.3 Claims for Concealed and Unknown Conditions - Should concealed and unknown conditions encountered in the performance of the Work (a) below the surface of the ground or (b) in an existing structure be at variance with the conditions indicated by this Contract, or should unknown conditions of an usual nature differing materially from those ordinarily encountered in the area and generally recognized as inherent in Work of the character provided for in this Contract, be encountered, wherein the Contract Documents or Standard Construction industry practices have not placed the responsibility of discovering such concealed and unknown conditions upon the Contractor prior to the Contractor submitting his Bid for the Work, the Contract Price shall be equitably adjusted by Change Order upon the written notice and claim by either party made within seven (7) days after the first observance of the condition. As a condition precedent to the Owner having any liability to the Contractor for concealed or unknown conditions, the Contract must give the Project Director written notice of, and an opportunity to observe, the condition prior to disturbing it. The failure by the Contractor to make the written notice and claim as provided in this Subparagraph shall constitute a waiver by the Contractor of any claim arising out of or relating to such concealed or unknown condition.

8.2.4 Claims for Additional Costs - If the Contractor wishes to make a claim for an increase in the Contract Price, as a condition precedent to any liability of the Owner therefore, the Contractor shall give the Project Director written notice of such claim within seven (7) days after the occurrence of the event, or the first appearance of the condition, giving rise to such claim. Such notice shall be given by the Contractor before proceeding to execute any additional or changed Work. The failure by the Contractor to give such notice prior to executing the Work shall constitute a waiver of any claim for additional compensation.

8.2.4.1 In connection with any claim by the Contractor against the Owner for compensation in excess of the Contract Price, any liability of the Owner for the Contractor's costs shall be strictly limited to direct costs incurred by the Contractor and shall in no event include indirect costs or consequential damages of the Contractor.

The Owner shall not be liable to the Contractor for claims of third parties, including Subcontractors, unless and until liability of the Contractor has been established therefore in a court of competent jurisdiction.

8.2.5 Claims for Additional Time - If the Contractor is delayed in progressing any task which at the time of the delay is then critical or which during the delay becomes critical, as the sole result of any act or neglect to act by the Owner or someone acting in the Owner's behalf, or by changes ordered in the Work, unusual delay in transportation, unusually adverse weather conditions not reasonably anticipated, fire or any causes beyond the Contractor's control, then the date for achieving Substantial Completion of the Work shall be extended upon the written notice and claim of the Contractor to the Project Director, for such reasonable time as the Project Director may determine.

Any notice and claims for an extension of time by the Contractor shall be made not more than seven (7) days after the occurrence of the event or the first appearance of the condition giving the rise to the claim and shall set forth in detail the Contractor's basis for requiring additional time in which to complete the Project. In the event the delay to the Contractor is continuing one, only one notice and claim for additional time shall be necessary. If the Contractor fails to make such claim for an extension shall be waived. This paragraph shall not be deemed to waive any damages for delay that are covered by insurance.

8.2.5.1 Delays and Extensions of Time - An extension of Contract Time shall not be given due to weather conditions unless such weather conditions more severe than average have caused a delay. In requesting extension of time for weather conditions; Contractor shall present complete records and such requests shall document how weather conditions delayed progress of Work.

### **8.3 Field Orders**

8.3.1 The Project Director shall have authority to order minor changes in the Work not involving a change in the Contract Price or in Contract Time and not inconsistent with the intent of the Contract. Such changes shall be effected by field order and shall be binding upon the Contractor. The Contractor shall carry out such field orders promptly.

## **ARTICLE IX SUBCONTRACTORS**

### **9.1 Definition**

9.1.1 A Subcontractor is an entity, which has a direct Contract with the Contractor to perform a portion of the Work.

### **9.2 Award of Subcontracts**

9.2.1 Upon execution of the Contract, the Contractor shall furnish the Project Director, in writing, the names of persons or entities proposed by the Contractor to act as a Subcontractor on the Project (See Attachment B attached to this agreement). The Project Director shall promptly reply to the Contractor, in writing, stating any objections the Project Director may have to such proposed Subcontractor. The Contractor shall not enter into a Subcontract with a proposed Subcontractor with reference to whom the Project Director has made a timely objection.

9.2.2 All subcontracts shall afford the Contractor rights against the Subcontractor, which correspond to those rights afforded to the Owner by Subparagraph 12.2.1 below.

## **ARTICLE X CHANGES IN THE WORK**

### **10.1 Changes Permitted**

10.1.1 Changes in the Work within the general scope of this Contract, consisting of additions, deletions, revisions, or any combination thereof, may be ordered without invalidating this Contract, by Change Order or by Field Order.

10.1.2 Changes in the Work shall be performed under applicable provisions of this Contract and the Contractor shall proceed promptly with such changes.

## **10.2 Change Order Defined**

10.2.1 Change Order shall mean a written order to the Contractor executed by the Project Director, issued after execution of this Contract, authorizing and directing a change in the Work or an adjustment in the Contract Price or the Contract Time, or any combination thereof. Only the Change Order may change the Contract Price and the Contract Time.

## **10.3 Changes in the Contract Price**

10.3.1 Any change in the Contract Price resulting from a Change Order shall be determined as follows: (a) by mutual agreement between the Owner and the Contractor as evidenced by (1) the change in the Contract Price being set forth in the Change Order, (2) such change in the Contract Price, together with any conditions or requirements related thereto, being initialed by both parties and (3) the Contractor's execution of the Change Order, or (b) if no mutual agreement occurs between the Owner and the Contractor, then, as provided in Subparagraph 10.3.2 below.

10.3.2 If no mutual agreement occurs between the Owner and the Contractor as contemplated in Subparagraph 10.3.1 above, the change in the Contract Price, if any, shall than be determined by the Project Director on the basis of the reasonable expenditures or savings of those performing, deleting or revising the Work attributable to the change, including, in the case of an increase or decrease in the Contract Price, a reasonable allowance for direct job site overhead and profit. In such case, the Contractor shall present, in such form and with such content as the Owner or the Project Director requires, an itemized accounting of such expenditures or savings shall be limited to the following: reasonable costs of materials, supplies, or equipment including delivery costs, reasonable costs of labor, including social security, old age and unemployment insurance, fringe benefits required by a pre-existing agreement or by custom, and workers' compensation insurance, reasonable costs of premiums for all Bonds and insurance, permit fees, and sales, use or other taxes related to the Work and paid by the Contractor, and reasonable costs of directly attributable to the change. In no event shall any expenditure or savings associated with the Contractor's home office or other non-jobsite overhead expenses be included in any change in the Contract Price. Pending final determination of reasonable expenditures or savings to the Owner, payments on account shall be made to the Contractor on the Owner's Certificate of Payment.

10.3.3 If Unit Prices are provided in the Contract, and if the quantities contemplated are so changed in proposed Change Order that application of such Unit Prices to the quantities of Work proposed shall cause substantial inequity to the Owner or to the Contractor, that applicable Unit Prices shall be equitable adjusted.

## **10.4 Minor Changes**

10.4.1 The Project Director shall have authority to order minor changes in the Work not involving a change in the Contract Price or an extension of the Contract Time and not inconsistent with the intent of this Contract. Such minor changes shall be made by written Field Order, and shall be binding upon the Owner and the Contractor. The Contractor shall promptly carry out such written Field Orders.

## **10.5 Effect of Executed Change Order**

10.5.1 The execution of a Change Order by the Contractor shall constitute conclusive evidence of the Contractor's agreement to the ordered changes in the Work, this Contract as thus amended, the Contract Price and the Contract Time. The Contractor, by executing the Change Order, waives and forever releases any claim against the Owner for additional time or compensation for matters relating to or arising out or resulting from the Work included within or affected by the executed Change Order.



## **10.6 Notice to Surety; Consent**

10.6.1 The Contractor shall notify and obtain the timely consent and approval of the Contractor's surety with reference to all Change Orders if such notice, consent or approval is required by the Contractor's surety or by law. The Contractor's warranty to the Owner that the surety has been notified of and consents to, such Change Order and the surety shall be conclusively deemed to have been notified of such Change Order and to have expressly consented thereto.

## **ARTICLE XI UNCOVERING AND CORRECTING WORK**

### **11.1 Uncovering Work**

11.1.1 If any of the Work is covered contrary to the Project Director's request or to any provision of this Contract, it shall, if required by the Project Director, be uncovered for the Project Director's inspection and shall be properly replaced at the Contractor's expense without change in the Contract Time.

11.1.2 If any of the Work is covered in a manner not described in Subparagraph 11.1.1 above, it shall, if required by the by the Project Director or Owner, be uncovered for the Project Director's inspection. If such Work conforms strictly to this Contract, costs of uncovering and proper replacement shall by Change Order be charged to the Owner. If such Work does not strictly conform to this Contract, the Contractor shall pay the costs of uncovering and proper replacement.

### **11.2 Correcting Work**

11.2.1 The Contractor shall immediately proceed to correct Work rejected by the Project Director as defective or failing to conform to this Contract. The Contractor shall pay all costs and expenses associated with correcting such rejected Work, including any additional testing and inspections, and reimbursement to the Owner for the Project Director's services and expenses made necessary thereby.

11.2.2 If within one (1) year after Substantial Completion of the Work, if any of the Work is found to be defective or not in accordance with this Contract, the Contractor shall correct it within seven (7) days at the Contractor's expense upon receipt of written notice from the Owner. This obligation shall survive Final Payment by the Owner and termination of this Contract. With respect to Work first performed and completed after Substantial Completion, this one (1) year obligation to specifically correct defective and nonconforming Work shall be extended by the period of time which elapses between Substantial Completion and completion of the subject Work.

11.2.3 Nothing contained in this Paragraph 11.2 shall establish any period of limitation with respect to other obligations, which the Contractor has under this Contract. Establishment of the one (1) year time period in Subparagraph 11.2.2 relates only to the duty of the Contractor to specifically correct the Work, and has no relationship to the time which the obligation to comply with the Contract Documents may be sought to be enforced.

### **11.3 Owner May Accept Defective or Nonconforming Work**

11.3.1 If the Owner chooses to accept defective or nonconforming Work, the Owner may do so. In such events, the Contract Price shall be reduced by the greater of (a) the reasonable cost of removing and correcting the defective or nonconforming Work, and (b) the difference between the fair market value of the Project had it not been constructed in such manner as to include defective

or nonconforming Work. If the remaining portion of the unpaid Contract Price, if any, is insufficient to compensate the Owner for its acceptance or defective or nonconforming Work, the Contractor shall, upon written demand from the Owner, pay the Owner such remaining compensation for accepting defective or nonconforming Work.

## **ARTICLE XII CONTRACT TERMINATION**

### **12.1 Termination by the Contractor**

12.1.1 If the Work is stopped for a period of ninety (90) days by an order of any court or as a result of an act of the Government, through no fault of the Contractor or any person or entity working directly or indirectly for the Contractor, the Contractor may, upon ten (10) days written notice to the Owner, terminate performance under this Contract and recover from the Owner payment for the actual reasonable expenditures of the Contractor (as limited in Subparagraph 10.3.2 above) for all Work executed and for materials, equipment, tools, construction equipment and machinery actually purchased or rented solely for the Work, less any salvage value of any such items.

12.1.2 If the Owner shall persistently or repeatedly fail to perform any material obligation to the Contractor for a period of fifteen (15) days after receiving written notice from the Contractor of its intent to terminate if such failure is not substantially corrected within fifteen (15) days, the Contractor may terminate performance under this Contract by written notice to the Project Director. In such event, the Contractor shall be entitled to recover from the Owner as though the Owner had terminated the Contractor's performance under this Contract for convenience pursuant to Subparagraph 12.2.1 hereunder.

### **12.2 Termination by the Owner**

#### **12.2.1 For Convenience**

12.2.1.1 The Owner may for any reason whatsoever terminate performance under this Contract by the Contractor for convenience. The Owner shall give written notice of such termination to the Contractor specifying when termination becomes effective.

12.2.1.2 The Contractor shall incur no further obligations in connection with the Work and the Contractor shall stop Work when such termination becomes effective. The Contractor shall also terminate outstanding orders and subcontracts. The Contractor shall settle liabilities and claims arising out of the termination of subcontracts and orders. The Owner may direct the Contractor to assign the Contractor's right, title and interest under terminated orders or subcontracts to the Owner or its designee.

12.2.1.3 The Contractor shall transfer title and deliver to the Owner such completed or partially completed Work and materials, equipment, parts, fixtures, information and Contract rights as the Contractor has.

12.2.1.4 (a) The Contractor shall submit a termination claim to the Project Director specifying the amounts due because of the termination for convenience together with costs, pricing or other data required by the Project Director. If the Contractor fails to file a termination claim within one (1) year from the effective date of termination, the Owner shall pay the Contractor, an amount derived in accordance with subparagraph (c) below.

(b) The Owner and the Contractor may agree to compensation, if any, due to the

Contractor hereunder.

- (c) Absent agreement to the amount due to the Contractor, the Owner shall pay the Contractor the following amounts;
- (d) Contract prices for labor, materials, equipment, and other services accepted under this Contract;
- (e) Reasonable costs incurred in preparing to perform and in performing a portion of the Work prior to termination and not included in (d) or (e), and in terminating the Contractor's performance, plus a fair and reasonable allowance for overhead and profit thereon (such profit shall not include anticipated profit or consequential damages); provided, however, that if it appears that the Contractor would have not profited or would have sustained a loss if the entire Contract had been completed, no profit shall be allowed or included and the amount of compensation shall be reduced to reflect the anticipated rate of loss, if any;
- (f) Reasonable costs of settling and paying claims arising out of the termination of Subcontracts or orders pursuant to Subparagraph 12.2.1.2 of this Paragraph. These costs shall not include amounts paid in accordance with other provisions hereof.

The total sum to be paid the Contractor under this Subparagraph 12.2.1 shall not exceed the total Contract Price, as properly adjusted, reduced by the amount of payments otherwise made, and shall in no event include duplication of payment.

#### **12.2.2 For Cause**

12.2.2.1 If the Contractor persistently or repeatedly refuses or fails to prosecute the Work in a timely manner, supply enough properly skilled Workers, supervisory personnel or proper equipment or materials, or if it fails to make prompt payment to Subcontractors, or for materials or labor, or persistently disregards laws, ordinances, rules, regulations or orders of any public authority having jurisdiction, or otherwise is guilty of a substantial violation of a material provision of this Contract, then the Owner may, by written notice to the Contractor, without prejudice to any other right or remedy, terminate the employment of the Contractor and take possession of the site and of all materials, equipment, tools, construction equipment and machinery thereon owned by the Contractor and may finish the Work by whatever methods it may deem expedient. In such case, the Contractor shall not be entitled to receive any further payment until the Work is finished.

12.2.2.2 If the unpaid balance of the Contract Price less any liquidated damages due under this Contract, exceeds the cost of finishing the Work, including compensation for the Project Director's additional services and expenses made necessary thereby, such exceed the unpaid balance, the Contractor shall pay the difference to the Owner. This obligation for payment shall survive the termination of the Contract.

12.2.2.3 In the event the employment of the Contractor is terminated by the Owner for cause pursuant to Subparagraph 12.2.2 and it is subsequently determined by a Court of competent jurisdiction that such termination was without cause, such termination shall thereupon be deemed a Termination for Convenience under Subparagraph 12.2.1 and the provisions of Subparagraph 12.2.1 shall apply.

### **ARTICLE XIII INSURANCE**

#### **13.1 Contractor's Insurance:**

13.1.1 The successful Bidder shall indemnify and hold the Owner harmless against all loss, damage, or expense by reason of injury to person or damage to property arising out of the use of or activities on any said premises by the successful Bidder, its agents, representatives, Contractors, Subcontractors, or employees. Prior to commencement of services under this Contract the successful Bidder's insurance coverage shall comply with the following insurance requirements:

- a) Workers' compensation – to meet statutory limits in compliance with the Workers Compensation Law of Florida. This policy must include Employer Liability with a limit of \$100,000 for each accident, \$500,000 disease policy limit and \$100,000 disease each employee limit. Longshoreman's insurance, if applicable, must meet statutory limits.
- b) Commercial general liability – coverage shall provide minimum limits of liability of \$1,000,000 per occurrence, \$2,000,000 Aggregate, for bodily injury and property damage. This shall include coverage for:
  - a. Premises/operations
  - b. Products/complete operations
  - c. Contractual liability
  - d. Independent contractors
  - e. Broad form property damage
  - f. X, C, U and personal injury with employment exclusion deleted
- c) Business auto liability – coverage shall provide minimum limits of liability of \$1,000,000 per occurrence, \$2,000,000 aggregate for bodily injury and property damage. This shall include coverage for:
  - a. Owned autos
  - b. Hired autos
  - c. Non-owned autos
- d) Umbrella or Excess Liability Insurance covering workers compensation, commercial general liability and business auto liability with minimum limits of liability of \$3,000,000.

#### Special Requirements

- a) Prior to execution of a contract, a certificate of insurance will be provided that shall provide for the following:
  - a. **St. Johns County will be named as additional insured on the commercial general liability, business auto liability, umbrella or excess liability policies.**
  - b. St. Johns County will be given thirty (30) days notice prior to cancellation or modification of any stipulated insurance.
  - c. **Certificate of Insurance shall note "Bid No.: 12-31 – Inlet Beach WTP High Service Pump Upgrade" in the description block of the certificate.**
- b) It is the responsibility of the contractor to insure that all subcontractors comply with all insurance requirements.
- c) It should be remembered that these are minimum requirements which are subject to modification in response to high hazard operations.

#### Property Insurance

Property insurance will be provided by the prime contractor:

- a) Property Insurance shall be in an amount equal to the full replacement cost of the project.
- b) Property Insurance is to insure against the perils of fire and extended coverage and is to include "all risk" insurance to insure for physical loss or damage due to theft, vandalism and malicious mischief, collapse, water damage, and/or all other risks against which coverage is obtainable.

## Special Requirements

- d) Prior to execution of a contract, a certificate of insurance will be provided that shall provide for the following:
  - d. **St. Johns County, the Contractor and all subcontractors will be named as insured or additional insured on the property insurance policies.**
  - e. St. Johns County will be given thirty (30) days notice prior to cancellation or modification of any stipulated insurance.
- e) It is the responsibility of the contractor to insure that all subcontractors comply with all insurance requirements.
- f) It should be remembered that these are minimum requirements which are subject to modification in response to high hazard operations.

## **ARTICLE XIV MISCELLANEOUS**

### **14.1 GOVERNING LAW AND VENUE**

14.1.1 The Contract shall be governed by the laws of the State of Florida. Venue for any administrative and/or legal action arising under this Agreement shall be St. Johns County, Florida.

### **14.2 Successors and Assigns**

14.2.1 The Owner and Contractor bind themselves, their successors, assigns and legal representatives to the other party hereto and to successors, assigns and legal representatives of such other party in

respect to covenants, agreements and obligations contained in this Contract. The Contractor shall not assign this Contract without written consent of the Owner.

### **14.3 Surety Bonds**

14.3.1 The Contractor shall furnish a separate Public Construction Bond to the Owner. Such Bonds shall set forth a penal sum in an amount not less than the Contract Price. The Bond furnished by the Contractor shall incorporate by reference the terms of this Contract as fully as though they were set forth verbatim in such Bonds. The Public Construction Bond shall provide that in the event the Contract Price is adjusted by Change Order executed by the Contractor. The Public Construction Bond furnished by the Contractor shall be in form suitable to the Owner and shall be executed by a Surety, or Sureties, reasonably suitable to the Owner.

### **14.4. Safety of Persons and Property**

14.4.1 When existing utility lines shown on the Drawings are to be removed or relocated, the Contractor shall notify the Engineer in ample time for taking measures for prevention of the interruption of any required services prior to the beginning of operations. In the event that the Contractor damages any existing utility lines not shown on the Drawings, the location of which is not known to the Contractor, report thereof shall be made immediately to the Engineer.

14.4.2 Locations of existing utility lines shown on the Drawings are based on the best information available to the Engineer, but shall not be considered exact either as to location or number of such lines.

14.4.3 Contractor shall protect utility lines constructed under terms of the agreement and those discovered or shown on Drawings to be existing. Damage occurring to utility lines due to

Contractor's operations shall be repaired at no cost to the Owner.

## **ARTICLE XV EQUAL EMPLOYMENT OPPORTUNITY**

### **15.1 Contractor's Employment Opportunity**

15.1.1 The Contractor and all Subcontractors shall not discriminate against any employee or applicant for employment because of race, religion, color, sex, national origin or age.

The Contractor shall take affirmative action to insure that applicants are employed, and that employees are treated during employment without regard to their race, religion, color, sex, national origin or age. Such action shall include, but not be limited to, the following: employment, upgrading, demotion or transfer, recruitment or recruitment advertisement, layoff or termination, rates of pay or other forms of compensation, and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices setting forth the policies of non-discrimination.

15.1.2 The Contractor and all Subcontractors shall, in all solicitations or advertisements for employees placed by them or on their behalf, state that all qualified applicants shall receive consideration for employment without regard to race, religion, color, sex, national origin or age.

## **ARTICLE XVI APPRENTICESHIP LAW REQUIREMENTS**

### **16.1 Apprenticeship Law (Chapter 446, Florida Statutes)**

16.1.1 The Contractor shall make a diligent effort to hire for Performance of the Contract a number of apprentices in each occupation which bears to the average number of journeyman in that occupation to be employed in the performance of the Contract, the ratio of at least one (1) apprentice or trainee to every five (5) journeymen.

16.1.2 The Contractor shall, when feasible and except when the number of apprentices or trainees to be hired is fewer than four (4), assure that twenty-five (25) percent of such apprentices or trainees are in their first year of training. Feasibility here involves a consideration of the availability of training opportunities for first year apprentices or trainees, the hazardous nature of the Work for beginning workers, and excessive unemployment of apprentices or trainees in their second or subsequent years of training.

16.1.3 The Contractor, during the performance of the Contract, shall make diligent efforts to employ the number of apprentices or trainees necessary to meet requirements of Subparagraphs a. and b. However, on-the-job training programs shall only be established in non-apprenticable trades or occupations to meet the requirements of this section.

16.1.4 The Contractor agrees to return records of employment, by trade, of the number of apprentices or trainees by first year of training, and the number of journeymen and the wages paid, and hours of work, of such persons on a form as prescribed by the Bureau of Apprenticeship of the Division of Labor at three (3) month intervals. Submission of duplicate copies of forms submitted to the United States Department of Labor shall be sufficient compliance with the provisions of the section.

16.1.5 The Contractor agrees to supply the Bureau of Apprenticeship of the Division of Labor, at three (3) months intervals, a statement describing steps taken toward making diligent effort and containing a breakdown by craft or hours worked and wages paid for first year apprentices or

trainees, other apprentices or trainees and journeymen.

16.1.6 The Contractor agrees to insert in any Subcontract under this Contract the requirements contained in this section. "The term Contractor" as used in such clauses and any Subcontract shall mean the Subcontractor.

16.1.7 Anything herein to the Contrary notwithstanding, Contractor agrees to comply with all of the provisions of Florida Statutes 446 and all regulations prescribed by the Bureau of Apprenticeship of the Division of Labor.

#### **ARTICLE XVII** **ACCESS TO RECORDS**

##### **17.1 Access To Records (Chapter 119, Florida Statutes)**

The access to, disclosure, non-disclosure, or exemption of records, data, documents, and/or materials associated with this Agreement/Contract shall be subject to the applicable provisions of the Florida Public Records Law (Chapter 119, Florida Statutes). Access to such public records may not be blocked, thwarted, or hindered by placing the public records in the possession of a third party, or an unaffiliated party.

#### **ARTICLE XVIII** **REVIEW OF RECORDS**

##### **18.1 Review of Records**

As a conditions of entering into this Agreement/Contract, and to ensure compliance, especially as it relates to any applicable law, rule, or regulation, the (insert name of other party) authorizes the County to examine, review, inspect, and/or audit the books and records, in order to determine whether compliance has been achieved with respect to the terms, conditions, provisions, rights, and responsibilities noted in this Agreement. It is specifically noted that (insert name of party) is under no duty to provide access to documentation not related to this Agreement, and/or is otherwise protected by County, State, or Federal law.

**{Remainder of page intentionally left blank}**

**Contract No.: 12-31 Innlet Beach WTP High Service Pumps Upgrade**

**Owner**  
St. Johns County (Seal)

(Typed Name)

By: \_\_\_\_\_

Signature

Joe Burch, Purchasing Director  
Printed Name & Title

\_\_\_\_\_  
Date of Execution

**Cheryl Strickland, Clerk of Courts**

By:  
Deputy Clerk

\_\_\_\_\_  
Date of Execution

**Legally Sufficient:**

\_\_\_\_\_  
Assistant County Attorney

Date: \_\_\_\_\_

**Contractor**  
Sawcross, Inc. (Seal)

(Typed Name)

By: \_\_\_\_\_

Signature

\_\_\_\_\_  
Printed Name & Title

\_\_\_\_\_  
Date of Execution



TECHNICAL  
SPECIFICATIONS


ISSUED FOR BID

Innlet Beach WTP High  
Service Pumps Upgrade



St. Johns County

December 2011



**CDM**

**BID NO.: 12-31**

**NOTICE TO BIDDERS – CONSTRUCTION**

Notice is hereby given that sealed bids will be received until 2:00 P.M. on January 18, 2012, by Sharon Haluska, Contract Administrator, St. Johns County Purchasing Department located at 2446 Dobbs Road, St. Augustine, Florida 32086 for Innlet Beach Water Treatment Plant High Service Pumps Upgrade. Bids will be opened promptly after the 2:00 P.M. deadline. **Note:** Bids delivered or received in the Purchasing Department after the 2:00 P.M. deadline shall not be give consideration and shall be returned to the sender unopened.

**Scope of Work:**

The construction of the Innlet Beach Water Treatment Plant High Service Pumps Upgrade project requires Contractor to furnish all labor, materials, equipment, and incidentals required to construct the upgrades. The scope of work shall include but not necessarily be limited to the following:

1. Mobilization/Demobilization, General Requirements, Bonds and Insurance
2. Site Work and Above Grade Yard Piping
  - a. Erosion and sedimentation control
  - b. Site restoration including grassing, and other restoration
  - c. Installation and testing of 16-inch pipe and valves between the existing GST and existing pump station building
  - d. Sidewalk installation between the existing pavement and electrical building
  - e. Seeding
3. High Service Pumps Upgrade
  - a. Removal of the existing four (4) high service pumps
  - b. Installation of four (4) new horizontal split-case centrifugal pumps supplied by the OWNER
  - c. Installation and testing of 10-inch suction pipe and valves, and upgraded connection tees to suction of pumps No. 2, 3 and 4
  - d. Installation of prefabricated concrete electrical building and associated mechanical and electrical equipment

4. Coordination with DCR on instrumentation programming
5. Pump Station startup
6. Permits including Notice of Intent, St. Johns River Water Management District dewatering permit, St. Johns County building permit for prefabricated electrical building, and other which are necessary. ENGINEER and OWNER have secured FDEP permit modification.

Prime Bidders must be fully licensed to do business in the State of Florida and hold a current Certified General Contractor license at the time that the bid is submitted, must have successfully constructed, as a prime contractor or subcontractor, at least two (2) projects of the type, size, and dollar value of the construction proposed for this project in the past five (5) years, and must have been in business as a contractor for at least five (5) years. Bidder's must complete Attachment "E" – License/Certification List and attach a copy of each license and certificate shown and submit the with their Bid Proposal.

There will be a **Mandatory** Pre-Bid Conference on January 4, 2012, at 10:00 am at Sawgrass Wastewater Treatment Plant Conference Room, located at 10052 Sawgrass Drive West, Ponte Vedra, Florida 32092, with a mandatory site visit to follow. **Anyone arriving after the scheduled time will not be allowed admittance. Any company not in attendance and signed in at this meeting will not be allowed to submit a bid. Bidders must attend both the meeting and site visit to be eligible to submit a bid for this project. The deadline for questions for this bid shall be January 10, 2012 at 4:00 pm.**

Copies of Bidding Documents may be obtained from Cheryl Gullotto, CDM, 8381 Dix Ellis Trail, Suite 400, Jacksonville, Florida 32256, 904-731-7109, [GullottoCA@cdm.com](mailto:GullottoCA@cdm.com), for the sum of \$50.00 per set, which is non-refundable. Electronic copies (CD) would be available to those bidders purchasing hard copy sets for an additional cost of \$10.00. Make checks payable to CDM.

Any and all technical questions relative to this project shall be directed to Scott Trigg, P.E., St. Johns County Utility Department, 904-209-2622, [strigg@sjcfl.us](mailto:strigg@sjcfl.us). Any and all procurement or bid process questions shall be directed to Sharon Haluska, Contract Administrator, St. Johns County Purchasing Department, 904-209-0156, [shaluska@sjcfl.us](mailto:shaluska@sjcfl.us). The deadline for all questions shall be January 10, 2012.

Additional available information that is not part of the Contract Documents includes Geotechnical Report (Report issued December 13, 2011) and St. Johns County Manual of Water, Wastewater, and Reuse Design Standards and Specifications. The Geotechnical Report can be viewed at CDM (8381 Dix Ellis Trail, Suite 400, Jacksonville, Florida 32256) or an electronic copy can be obtained from CDM (904-731-7109) for the sum of \$10 per set, which is non-refundable. Make checks payable to CDM. The St. Johns County Manual of Water, Wastewater, and Reuse Design Standards and Specifications is available online: ([http://www.co.st-johns.fl.us/BCC/Utility\\_Department/Development\\_Group/index.aspx](http://www.co.st-johns.fl.us/BCC/Utility_Department/Development_Group/index.aspx)).

Additionally, document orders may be facilitated through Onvia DemandStar, Inc. These requests will be forwarded to the party responsible for bid document distribution via email. For technical assistance with this Website please contact Onvia Supplier Services at 1-800-711-1712. A link to Onvia DemandStar is also available through the St. Johns County Website at [www.sjcfl.us/BCC/Purchasing/Open\\_Bids.aspx](http://www.sjcfl.us/BCC/Purchasing/Open_Bids.aspx). Check the County's site for download availability and any applicable fees. Vendors registered with Onvia DemandStar.com may visit [www.demandstar.com](http://www.demandstar.com) to electronically download some documents.

Any bidder, proposer or person substantially and adversely affected by an intended decision or by an term, condition, procedure or specification with respect to any bid, invitation, solicitation of proposals or requests

for qualifications, shall file with the Purchasing Department for St. Johns County, a written notice of intent to protest no later than 72 hours (excluding Saturdays, Sundays and legal holidays for employees of St. Johns County) after the posting either electronically or by other means of the notice of intended action, not of intended award, bid tabulation, publication by posting electronically or by other means of a procedure, specification, term or condition which the person intends to protest, or the right to protest such matter shall be waived. The protest procedures may be obtained from the Purchasing Department and are included in the County's Purchasing Manual. All of the terms and conditions of the County Purchasing Manual are incorporated by reference and are fully binding.

Vendors shall not contact, lobby, or otherwise communicate with any SJC employee, including any member of the Board of County Commissioners, other than the above referenced individual from the point of advertisement of the Bid until contract(s) are executed by all parties, per SJC Purchasing Code 304.6.5 "Procedures Concerning Lobbying". According to SJC policy, any such communication shall disqualify the vendor, contractor, or consultant from responding to the subject invitation to bid, request for quote, request for proposal, invitation to negotiate, or request for qualifications.

St. Johns County reserves the right to accept or reject any or all bids/proposals, waive minor formalities, and to award the bid/proposal that best serves the interests of St. Johns County. St. Johns County also reserves the right to award the base bid and any alternate bids in any combination that best suits the needs of the County.


BOARD OF COUNTY COMMISSIONERS  
OF ST. JOHNS COUNTY, FLORIDA  
CHERYL STRICKLAND, CLERK

BY: \_\_\_\_\_  
Deputy Clerk


**CONTRACT DOCUMENTS AND SPECIFICATIONS  
INNLET BEACH WATER TREATMENT PLANT HIGH SERVICE PUMPS  
UPGRADE**

**FOR**

**ST. JOHNS COUNTY UTILITY DEPARTMENT**



Leslie Samel, P.E. \_\_\_\_\_ Date  
Florida Registered P.E. No. 68763  
General/Civil/Mechanical  
Specification Sections: Division 1, Division 2,  
Division 9, Division 10, Division 11, Division  
15 (Except Sections 15500, 15520)



Tim Verwey, P.E. \_\_\_\_\_ Date  
Florida Registered P.E. No. 50947  
Structural  
Florida Building Code 2007 with 2009  
Supplements, Chapter 16, 19, 21 and 22  
Specification Sections: Division 3

**CDM  
8381 Dix Ellis Trail Suite 400  
Jacksonville, FL 32256  
Phone: (904) 731-7109  
Fax: (904) 519-7090  
FL COA No. EB-0000020**

**ST. JOHNS COUNTY  
BID TABULATION**

*JAC*

**BID TITLE** INLET BEACH WATER TREATMENT PLANT  
HIGH SERVICE PUMPS UPGRADE

**BID NUMBER** 12-31

**OPENING DATE/TIME** January 18, 2012 2:00 PM

**POSTING DATE/TIME** 01/18/12 3:00 PM

**FROM** 01/18/12 3:00 PM **UNTIL** 01/23/12 3:00 PM

**ANY BIDDER AFFECTED ADVERSELY BY AN INTENDED DECISION WITH RESPECT TO THE AWARD OF ANY BID, SHALL FILE WITH THE PURCHASING DEPARTMENT FOR ST. JOHNS COUNTY, A WRITTEN NOTICE OF INTENT FILE A PROTEST NOT LATER THAN SEVENTY-TWO (72) HOURS (EXCLUDING SATURDAY, SUNDAY AND LEGAL HOLIDAYS) AFTER THE POSTING OF THE BID TABULATION PROTEST PROCEDURES MAY BE OBTAINED IN THE PURCHASING DEPARTMENT.**

**OPENED BY** LEIGH DANIELS

**TABULATED BY** Barbara Beauchamp

**VERIFIED BY** [Signature]

**PAGE (S)** 1 **of 1**

BIDDERS	BASE BID TOTAL LUMP SUM PRICE	BID BOND	ATTENDED MANDATORY PRE-BID MEETING	ADDENDUM # 1			
TB LANDMARK CONSTRUCTION, INC.	\$609,997.00	YES	YES	YES			
GRUDEN MAY, INC.	\$600,623.00	YES	YES	YES			
C&S COMPANIES	\$592,088.00	YES	YES	YES			
SAWCROSS, INC.	\$547,400.00	YES	YES	YES			
AC GENERAL, INC.	\$559,000.00	YES	YES	YES			
ACON CONSTRUCTION CO., INC.	\$584,341.00	YES	YES	YES			

**BID AWARD DATE -** \_\_\_\_\_

**ST. JOHNS COUNTY  
BID TABULATION**

**BID TITLE**

INLET BEACH WATER TREATMENT PLANT  
HIGH SERVICE PUMPS UPGRADE

ANY BIDDER AFFECTED ADVERSELY BY AN INTENDED

DECISION WITH RESPECT TO THE AWARD OF ANY BID,

SHALL FILE WITH THE PURCHASING DEPARTMENT FOR

ST. JOHNS COUNTY, A WRITTEN NOTICE OF INTENT

FILE A PROTEST NOT LATER THAN SEVENTY-TWO (72)

HOURS (EXCLUDING SATURDAY, SUNDAY AND LEGAL


HOLIDAYS) AFTER THE POSTING OF THE BID TABULATION

PROTEST PROCEDURES MAY BE OBTAINED IN THE

PURCHASING DEPARTMENT.

**OPENED BY  
TABULATED BY  
VERIFIED BY**

LEIGH DANIELS  
Barbara Beauchamp



**BID NUMBER**

12-31

**OPENING DATE/TIME**

January 18, 2012 2:00 PM

FROM

**POSTING DATE/TIME**

01/18/12 3:00 PM

UNTIL

01/23/12 3:00 PM

PAGE (S) 1 of 1

BIDDERS	BASE BID TOTAL LUMP SUM PRICE	BID BOND	ATTENDED MANDATORY PRE- BID MEETING	ADDENDUM # 1			
RTD CONSTRUCTION, INC.	\$605,626.00	YES	YES	YES			
TLC DIVERSIFIED, INC.	\$588,700.00	YES	YES	YES			

BID AWARD DATE - \_\_\_\_\_





BID NO.: 12-31

OFFICIAL COUNTY BID FORM  
ST. JOHNS COUNTY, FLORIDA  
LUMP SUM BID PROPOSAL

PROJECT: INNLET BEACH WATER TREATMENT PLANT HIGH SERVICE PUMPS  
UPGRADE

TO: THE BOARD OF COUNTY COMMISSIONERS OF ST. JOHNS COUNTY,  
FLORIDA

DATE SUBMITTED: January 18, 2012

BID PROPOSAL OF

Sawcross, Inc.

FULL LEGAL COMPANY NAME

10970 New Berlin Road, Jacksonville, FL. 32226 (904) 751-7500 fax (904) 751-7500  
Address Telephone No.

Gentlemen: Having become familiar with site conditions of the project, and having carefully examined the Bidding requirements, including the Advertisement, Instructions to Bidders, and Contract Documents, including the General Conditions, Supplementary Conditions, Specifications, and Drawing entitled for Innlet Beach Water Treatment Plant High Service Pumps Upgrade, in St. Johns County, Florida. The undersigned proposes to furnish all materials, labor and equipment, supervision and all other requirements necessary to comply with the Contract Documents for the following base bids quoted in this Bid Proposal summarized as follows:

BASE BID:

FOR: Construction of Innlet Beach Water Treatment Plant High Service Pumps Upgrade as per plans and specifications.

\$ 547,400  
Total Lump Sum Price (Numerical)

Five Hundred Forty-Six Thousand Four Hundred 100 Dollars  
(Amount written or typed in words)

Bidder will enter written (in words) and numerically by the Lump Sum Price in the space provided above. In the event of a conflict, the written Lump Sum Price shall be considered as the Bidder correct bid.

Time of Substantial Completion to be ninety (90) consecutive calendar days from receipt of Notice to Proceed from Owner.

Note: The listing order of bid items reflects a construction sequence in general terms for bidding purposes only and is not a specific construction schedule.

During the preparation of the Bid, the following addenda, if any, were received:

No.: 1 Date Received: 1/11/12

No.: \_\_\_\_\_ Date Received:

No.: \_\_\_\_\_ Date Received:

We, the undersigned, hereby declare that no person or persons, firm or corporation, other than the undersigned are interested, in this proposal, as principals, and that this proposal is made without collusion with any person, firm or corporation, and we have carefully and to our satisfaction examined the Project Specifications and form of Contract and Public Construction Bonds, together with the Plans.

We have made a full examination of the location of the proposed work and the sources of supply of materials, and we hereby agree to furnish all necessary labor, and equipment and materials, fully understanding that any quantities shown therewith are approximate only, and that we will fully complete all requirements therein as prepared by Architect, within the same time limit specified in the Contract Documents for the following total sum price as indicated above.

If the Undersigned is notified of the acceptance of this Bid Proposal by the Board within sixty (60) calendar days for the time set for the opening of Bids, the Undersigned further agrees, to execute a contract for the above work within ten (10) days after notice that his Bid has been accepted for the above stated compensation in the form of a Contract presented by the Owner.

The Undersigned agrees, if awarded the Contract, to Substantially Complete all work within ninety (90) consecutive calendar from receipt of NOTICE TO PROCEED. Undersigned further agrees that from the compensation otherwise to be paid, the Owner may retain the liquidated damages as provided in the Contract, which sum is agreed upon as the proper measure of liquidated damages which the Owner will sustain each day by the failure of the Undersigned to complete the work in the time stipulated, and this sum is not to be construed as penalty.

The Undersigned further agrees that security in the form of a Bid Bond, certified or cashier's check in the amount of not less than five percent (5%) total Bid Price, payable to the Owner, accompanies this Bid; that the amount is not to be construed as a penalty, but as liquidated damages which said Owner will sustain by failure of the Undersigned to execute and deliver the Contract and Bond within ten (10) days of the written notification of the Award of the Contract to him; thereupon, the security shall become the property of the Owner, but if this Bid is not accepted within sixty (60) days of the time set for the submission of Bids, or if the Undersigned delivers the executed Contract and Public Construction Bond upon receipt, the Security shall be returned to the Bidder within seven (7) working days.

**CORPORATE/COMPANY**

Full Legal Company Name: Sawcross, Inc. (Seal)

By: [Signature] Mark Hickinbotham, President  
(Name & Title typed or printed)

By: \_\_\_\_\_  
(Name & Title typed or printed)

Address: 10970 New Berlin Road, Jacksonville, FL. 32226

Telephone No.: (904) 751-7500 Fax No.: (904) 751-0600

Email Address for Authorized Company Representative: markh@sawcross.com

Federal I.D. Tax Number: 59-3136689 DUNS #: 79-130-9834

**INDIVIDUAL**

Name: N/A \_\_\_\_\_  
(Signature) (Name typed or printed) (Title)

Address: \_\_\_\_\_

Telephone No.: (\_\_\_\_) \_\_\_\_\_ Fax No.: \_\_\_\_\_

Email Address: \_\_\_\_\_

Federal I.D. Tax Number: \_\_\_\_\_

- Bid Proposal Attachments:
- "A" - Affidavit
  - "B" - List of Proposed Subcontractors
  - "C" - Certificate as to Corporate Principal
  - "D" - Certificate of Compliance with Florida Trench Safety Act
  - "E" - License/Certification List
  - "F" - Unit Prices for Adjustment/Schedule of Values
  - "G" - Qualifications Statement
  - "H" - Certification of Compliance with FDEP Generic Permit Requirements

Bid Bond  
Fully Acknowledged Addenda Applicable to this bid

Attachments "A", "B", "C", "D", "E", "F", "G", "H", and Bid Bond must be completed and attached to Bidder's bid proposal along with a fully acknowledged copy of each Addendum applicable to this Bid.

Bid No.: 12-31

ATTACHMENT "A"

**ST. JOHNS COUNTY, BOARD OF COUNTY COMMISSIONERS AFFIDAVIT**

TO: ST. JOHNS COUNTY, BOARD OF COUNTY COMMISSIONERS, ST. JOHNS COUNTY, ST. AUGUSTINE, FLORIDA.

At the time the proposal is submitted, the Bidder shall attach to his Bid a sworn statement.

This sworn statement shall be an affidavit in the following form, executed by an officer of the firm, association, or corporation submitting the proposal, and shall be sworn to before a person who is authorized by law to administer oaths.

STATE OF FLORIDA, COUNTY OF ST. JOHNS

Before me, the Undersigned authority, personally appeared Mark Hickinbotham who being duly sworn, deposes and says he is President (Title) of the firm of Sawcross, Inc. Bidder submitting the attached proposal for the services covered by the bid documents for Bid # 12-31, for Innlet Beach Water Treatment Plant High Service Pumps Upgrade, in St. Johns County, Florida.

The affiant further states that no more that one proposal for the above-referenced project will be submitted from the individual, his firm or corporation under the same or different name, and that such Bidder has no financial interest in the firm of another bidder for the same work. That he, his firm, association or corporation has neither directly, nor indirectly entered into any agreement, participated in any collusion, or otherwise taken any action in restraint of free competitive bidding in connection with this firm's Bid on the above-described project. Furthermore, neither the firm nor any of its officers are barred from participating in public contract lettings in the State of Florida or any other state.

Sawcross, Inc.  
(Bidder)


By: [Signature]  
Mark Hickinbotham, President  
(Title)

Sworn and subscribed to me this 18th day of January, 2012.

[Signature]  
Notary Public  
Signature  
Sherry L. Winkelmann  
Printed

My commission Expires: January 29, 2016

BIDDER ON ALL COUNTY PROJECTS MUST EXECUTE AND ATTACH THIS AFFADAVIT TO EACH BID.



Bid No.: 12-31

ATTACHMENT "B"

**LIST OF PROPOSED SUBCONTRACTORS**

All subcontractors and major materials suppliers are subject to approval of Owner. The following are subcontractors and manufacturers of materials and/or equipment that are proposed to be utilized by the Contractor in the performance of this work:


<u>DIVISION OF WORK or DESCRIPTION/NAME OF EQUIPEMENT</u>	<u>NAME AND ADDRESS OF SUBCONTRACTOR or EQUIPMENT VENDOR</u>
Electrical	Cogburn Bros. Jacksonville, FL.
Pre-fab Building	Concrete Modular St. Petersburg, FL.

Bid No.: 12-31

ATTACHMENT "C"

**CERTIFICATES AS TO CORPORATE PRINCIPAL**

I, Frances Hickinbotham, certify that I am the Secretary of the Corporation named as Principal in the attached bond; that Mark Hickinbotham who signed the said bond on behalf of the Principal, was then Sawcross, Inc. of said Corporation; that I know his signature, and his signature hereto is genuine; and that said bond was duly signed, sealed, and attested for and in behalf of said Corporation by authority of it's governing body.

  
Secretary Corporate Seal  
Frances Hickinbotham

(STATE OF FLORIDA  
COUNTY OF ST. JOHNS)

Before me, a Notary Public duly commissioned, qualified and acting, personally appeared James J. Pedoulas to me well known, who being by me first duly sworn upon oath, says that he is the Attorney-In-Fact, for the Western Surety Company and that he has been authorized by Western Surety Company to execute the foregoing bond on behalf of the surety named therein in favor of St. Johns County, Florida.

Subscribed and sworn to me this 16th day of January, 20 12, A.D.

*Michelle E Bartlett*

NOTARY PUBLIC  
State of Florida-at-large



**MICHELLE E. BARTLETT**  
Notary Public, State of Florida  
My Comm. Expires July 28, 2015  
Commission No. EE 116717

My Commission Expires: July 28, 2015

(Attach Power of Attorney to original Bid Bond and Financial Statement of Surety Company)

Bid No.: 12-31

ATTACHMENT "D"


CERTIFICATE OF COMPLIANCE  
WITH FLORIDA TRENCH SAFETY ACT

Bidder acknowledges that he is solely responsible for complying with the Florida Trench Safety Act (ACT) and Occupational Safety and Health Administrations excavation safety standard 29 CFR 1926.650 (Subpart P as amended) and the St. Johns County Trenching and Excavation Safety Program. If there is a conflict between the ACT and the St. Johns County Trenching and Excavation Safety Program, the more stringent requirement would apply. Bidder further acknowledges that included in the various items of the proposal and in the Total Bid Price are costs for complying with the Florida Trench Safety Act (90-96, Laws of Florida) effective October 1, 1990 and the Occupational Safety and Health Administrations excavation safety standard.

By: Mark Hickinbotham, President

Sawcross, Inc.

Bidder



Authorized Signature

January 18, 2012

Date

Bid No.: 12-31

**ATTACHMENT "E"**

*License/Certification List*

In the space below, the Bidder shall list all **current** licenses and certifications held.

*The bidder shall attach a copy of each current license or certification listed below to this form.*

License Name	License #	Issuing Agency	Expiration Date
CGC	036203	State of Florida	8/31/2012
CMC	056728	State of Florida	8/31/2012
CUC	056787	State of Florida	8/31/2012
CFC	1427748	State of Florida	8/31/2012
PCC	1256908	State of Florida	8/31/2012



**ATTACHMENT "F"**  
**UNIT PRICES FOR ADJUSTMENT/SCHEDULE OF VALUES**

The following unit prices, if approved by the Owner, will be used for adjusting the Contract Price for changes in the work (additions or deletions) in accordance with the provisions of an approved change order and any other modifications of the Contract. Unit prices shall include all labor, materials, equipment, transportation, supervision, insurance cost, bond cost, overhead and profit representing an in-place price for each item. Scope or size of each item not otherwise indicated is as described in the construction specifications and drawings.

ITEM DESCRIPTION		UNIT MEASURE	UNIT PRICE
1	16-inch Ductile Iron Flanged Pipe	LF	\$ 185. <sup>00</sup>
2	16-inch Ductile Iron Gate Valve	EA	\$ 1,500. <sup>00</sup>
3	10-inch Ductile Iron Gate Valve	EA	\$ 3,700. <sup>00</sup>
4			
5			
6			
7			
8			
9			
10			
11			
12			
13			

**ATTACHMENT "G"**  
**QUALIFICATIONS STATEMENT**

Bidder acknowledges that he is licensed to perform utility work in the STATE OF FLORIDA and has successfully completed similar projects as shown below.

By: Sawcross, Inc.

January 18, 2012

Bidder Date

\_\_\_\_\_  
Authorized Signature

Provide a brief description of at least two (2) similar jobs completed within the last 5 years

Date	Job Name	Description: Type, Length, Size, Material	Owner Contact Info
<i>Example</i> April-Nov. 2005	SR207 FM Extension	FM Extension, 10,000 ft. of 10" PVC and services. 2,000 ft. of 12" HDPE Dir. Drill.	St. Johns Co. Utility Scott Trigg, P.E. (904) 471-8486
	Please see attached		




SAWCROSS, INC.  
CONTRACTORS  
and ENGINEERS

10970 New Berlin  
Road  
Jacksonville, FL  
32226

904-751-7500  
904-751-0600 (fax)

[www.sawcross.com](http://www.sawcross.com)

## JEA Woodmere Pump Station

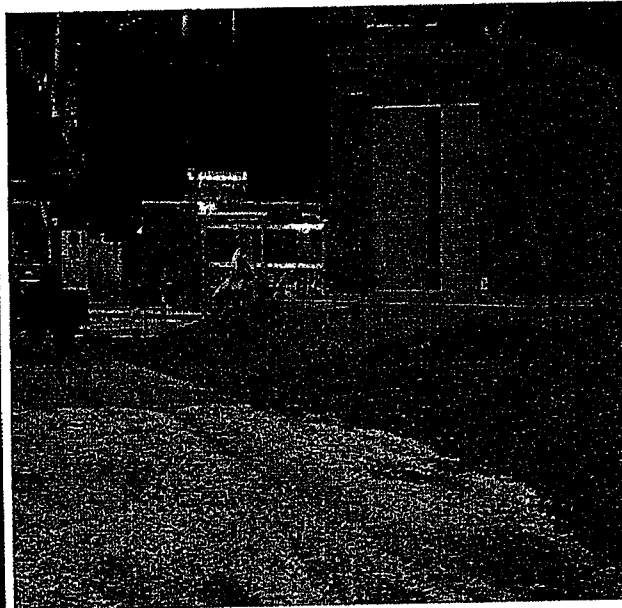

New 12'-0" diameter 30'-0" deep triplex sewage pump station. Spectrashield coatings, new precast electrical building, HVAC, plumbing, instrumentation, generator, fuel tank, pumps, piping, sheet piling, deep well dewatering, grading and grassing.

**Owner:** Jacksonville Electric  
Authority  
21 West Church Street  
Jacksonville, FL 32202  
Mr. Mark Cooley  
(904) 655-7872 cell

**Engineer:** Jacksonville Electric  
Authority  
21 West Church Street  
Jacksonville, FL 32202  
Mr. Mark Cooley  
(904) 655-7872 cell

**Original Contract Amount:** \$1,307,000  
**Final Contract Amount:** \$1,387,463  
**Final Completion Date:** 11/2008  
**Original Contract Time:** 427 days  
**Final Contract Time:** 396 days

## Nocatee Reclaim Water Pump Station




SAWCROSS, INC.  
CONTRACTORS  
and ENGINEERS

10970 New Berlin  
Road  
Jacksonville, FL  
32226

904-751-7500  
904-751-0600 (fax)

[www.sawcross.com](http://www.sawcross.com)

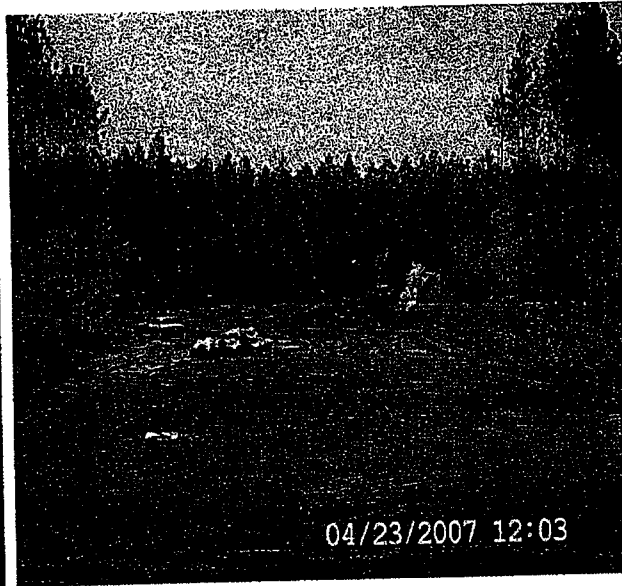

Construction of complete new reclaim water pumping station. Work included extensive clearing and grubbing, hauling in fill dirt and compacting, excavation, water lines, reuse transmission line, all site piping, 1 mg reuse storage tank, concrete pump pads, crush crete paving, drainage, finish grading and landscaping

**Owner:** Jacksonville Electric  
Authority  
21 West Church Street  
Jacksonville, FL 32202  
Mr. Steve Wiggins  
[wiggsc@jea.com](mailto:wiggsc@jea.com)  
(904) 665-6314

**Engineer:** CH2M Hill  
9428 Baymeadows Road,  
Suite 300  
Jacksonville, FL 32256  
Mr. Joe Hall, P.E.  
(904) 733-9119

Original Contract Amount: \$2,207,202  
Final Contract Amount: \$2,394,000  
Final Completion Date: 3/2008  
Original Contract Time: 365 days  
Final Contract Time: 340 days

## JEA Fury Drive Pump Station



SAWCROSS, INC.  
CONTRACTORS  
and ENGINEERS

10970 New Berlin  
Road  
Jacksonville, FL  
32226

904-751-7500  
904-751-0600 (fax)

[www.sawcross.com](http://www.sawcross.com)



New regional master pump station cast in place with coatings, generator, pumps, piping, electrical building, HVAC, plumbing, extensive instrumentation, sitework, sheet piling, deep well dewatering, grading and grassing.

**Owner:** Jacksonville Electric Authority  
21 West Church Street  
Jacksonville, FL. 32202  
Mr. Mark Cooley  
(904) 655-7872 cell

**Engineer:** Jacksonville Electric Authority  
21 West Church Street  
Jacksonville, FL. 32202  
Mr. Mark Cooley  
(904) 655-7872 cell

Original Contract Amount: \$1,556,000  
Final Contract Amount: \$1,756,000  
Final Completion Date: 5/2008  
Original Contract Time: 458 days  
Final Contract Time: 427 days

## State Road 207 Pump Station St Johns County



SAWCROSS, INC.  
CONTRACTORS  
and ENGINEERS

10970 New Berlin  
Road  
Jacksonville, FL  
32226

904-751-7500  
904-751-0600 (fax)

[www.sawcross.com](http://www.sawcross.com)



This project included all clearing, grubbing, water lines, sewer lines, paving, drainage, an electrical building, a pump building, sludge storage tank, site finish grading and grassing.

**Owner:** St. Johns County Utility  
Department  
2175 Mizell Street  
St. Augustine, FL. 32085  
Mr. Scott Trigg, P.E.  
(904) 209-2622

**Engineer:** St. Johns County Utility  
Department  
2175 Mizell Street  
St. Augustine, FL. 32085  
Mr. Scott Trigg, P.E.  
(904) 209-2622

Original Contract Amount: \$1,198,000  
Final Contract Amount: \$1,250,859  
Final Completion Date: 6/2007  
Original Contract Time: 270 days  
Final Contract Time: 255 days

## St. Johns County Utilities Northwest Pump Station




SAWCROSS, INC.  
CONTRACTORS  
and ENGINEERS

10970 New Berlin  
Road  
Jacksonville, FL  
32226

904-751-7500  
904-751-0600 (fax)

[www.sawcross.com](http://www.sawcross.com)

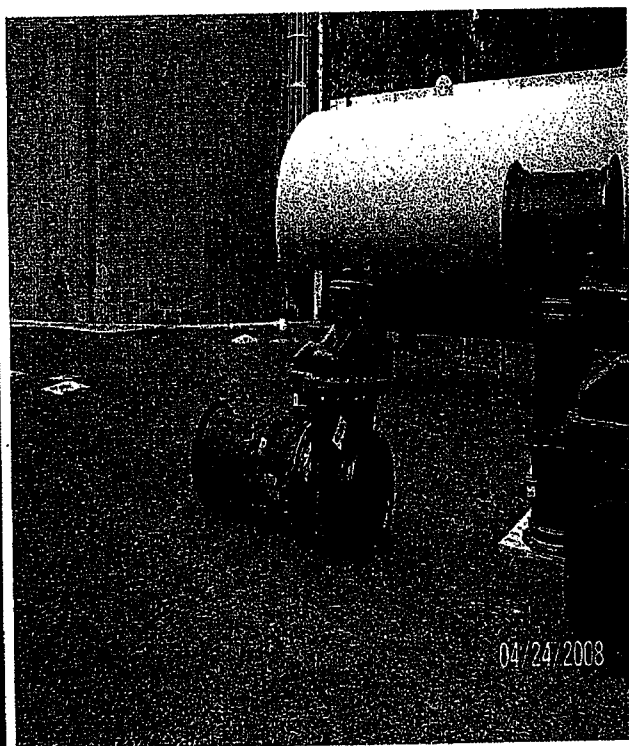

Relocate existing above ground sewage pump station, sitework and piping for owner furnished 100,000 gallon above ground glass lined fused sewage equalization tank, extensive site piping including several large force main tie-ins, new 12'-0" x 10' deep suction wetwell, installation of new generator, relocation and piping of fuel tanks. Extensive clearing and sitework.

**Owner:** St. Johns County Utility Dept.  
1205 State Road 16  
St. Augustine, FL. 32084  
Mr. Scott Trigg, P.E.  
(904) 209-2622

**Engineer:** CDM  
2301 Maitland Center Pkwy.,  
Suite 300  
Maitland, FL. 32751  
Mr. Pat Costello  
(407) 660-6424

Original Contract Amount: \$531,900  
Final Contract Amount: \$662,334  
Final Completion Date: 4/2009  
Original Contract Time: 330 days  
Final Contract Time: 405 days

BID NO.: 12-31

ATTACHMENT "H"

**CERTIFICATE OF COMPLIANCE  
WITH FDEP GENERIC PERMIT REQUIREMENTS**

Bidder acknowledges that he is solely responsible for complying with all requirements of the Florida Department of Environmental Protection (FDEP) National Pollutant Discharge Elimination System (NPDES) Generic Permit. These requirements are further described in Section 01571 - NPDES PERMIT CONFORMANCE. Bidder further acknowledges that included in the various items of the proposal and in the Total Bid Prices are all costs for complying with the FDEP NPDES Generic Permit.

Company Name: Sawcross, Inc.

Authorized Representative:   
(Signature) Mark Hickinbotham, President

Date: January 18, 2012



BID NO.: 12-31

BID BOND

STATE OF FLORIDA  
COUNTY OF ST. JOHNS

KNOW ALL MEN BY THESE PRESENTS, that Sawcross, Inc. as Principal, and Western Surety Company as Surety, are held and firmly bound unto St. Johns County, Florida, in the penal sum of Five Percent of \* Dollars (\$5.0%) lawful money of the United States, we bind ourselves, our heirs, executors, administrators, and successors, jointly and severally, firmly by these presents. \* Bid Amount

THE CONDITION OF THIS OBLIGATIONS IS SUCH, that whereas the Principal has submitted the accompanying Bid, dated January 18, 2012.

For  
**Innlet Beach Water Treatment Plant High Service Pumps Upgrade**  
St. Johns County, Florida

NOW THEREFORE,

- (a) If the Principal shall not withdraw said Bid within sixty (60) days after Bid Award date, and shall within ten (10) days after prescribed forms are presented to him for signature, enter into a written Contract with the County in accordance with the Bid as accepted, and give Bond with good and sufficient Surety or Sureties, as may be required, for the faithful performance and proper fulfillment of such Contract, then the above obligations shall be void and of no effect, otherwise to remain in full force and virtue.
- (b) In the event of the withdrawal of said Bid within the period specified, or the failure to enter into such Contract and give such Bond within the time specified, if the Principal shall pay the County the difference between the amount specified, in said Bid and the amount for which the County may procure the required Work and supplies, if the latter amount be in excess of the former, then the above obligations shall be void and of no effect, otherwise to remain in full force and virtue.


IN WITNESS WHEREOF, the above bounded parties have executed this instrument under their several seals, this 16th day of January A.D., 2012, the name and corporate seal of each corporate party being hereto affixed and these presents duly signed by its undersigned representative, pursuant to authority of its governing body.

BID NO.: 12-31

WITNESSES:


(If Sole Ownership or Partnership two (2) Witnesses required).  
(If Corporation, Secretary only will attest and affix seal).

WITNESSES:

  
Frances Hickinbotham, Secretary

Sawcross, Inc.  
PRINCIPAL:

Sawcross, Inc.  
NAME OF FIRM:

  
SIGNATURE OF AUTHORIZED OFFICER (AFFIX SEAL)


Mark Hickinbotham, President  
TITLE

10970 New Berlin Road  
BUSINESS ADDRESS

Jacksonville, FL  
CITY STATE

Western Surety Company  
SURETY:


Western Surety Company  
CORPORATE SURETY

  
ATTORNEY-IN-FACT (AFFIX SEAL) James J. Pedoulas  
101 Century 21 Drive, Ste. 200  
BUSINESS ADDRESS

Jacksonville, FL  
CITY STATE

TD Insurance, Inc.  
NAME OF LOCAL INSURANCE AGENCY

WITNESS:

  
Michelle O'Steen

END OF SECTION

# Western Surety Company

## POWER OF ATTORNEY APPOINTING INDIVIDUAL ATTORNEY-IN-FACT

Know All Men By These Presents, That WESTERN SURETY COMPANY, a South Dakota corporation, is a duly organized and existing corporation having its principal office in the City of Sioux Falls, and State of South Dakota, and that it does by virtue of the signature and seal herein affixed hereby make, constitute and appoint

**David L Cain, Juanita W Bowditch, Raynor E Bowditch, James J Pedoulas, Michelle Bartlett O Steen, Individually**

of Jacksonville, FL, its true and lawful Attorney(s)-in-Fact with full power and authority hereby conferred to sign, seal and execute for and on its behalf bonds, undertakings and other obligatory instruments of similar nature

**- In Unlimited Amounts -**

and to bind it thereby as fully and to the same extent as if such instruments were signed by a duly authorized officer of the corporation and all the acts of said Attorney, pursuant to the authority hereby given, are hereby ratified and confirmed.

This Power of Attorney is made and executed pursuant to and by authority of the By-Law printed on the reverse hereof, duly adopted, as indicated, by the shareholders of the corporation.

In Witness Whereof, WESTERN SURETY COMPANY has caused these presents to be signed by its Senior Vice President and its corporate seal to be hereto affixed on this 15th day of December, 2011.




WESTERN SURETY COMPANY

Paul T. Bruflat  
Paul T. Bruflat, Senior Vice President

State of South Dakota }  
County of Minnehaha } ss

On this 15th day of December, 2011, before me personally came Paul T. Bruflat, to me known, who, being by me duly sworn, did depose and say: that he resides in the City of Sioux Falls, State of South Dakota; that he is the Senior Vice President of WESTERN SURETY COMPANY described in and which executed the above instrument; that he knows the seal of said corporation; that the seal affixed to the said instrument is such corporate seal; that it was so affixed pursuant to authority given by the Board of Directors of said corporation and that he signed his name thereto pursuant to like authority, and acknowledges same to be the act and deed of said corporation.

My commission expires  
November 30, 2012



D. Krell  
D. Krell, Notary Public

### CERTIFICATE

I, L. Nelson, Assistant Secretary of WESTERN SURETY COMPANY do hereby certify that the Power of Attorney hereinabove set forth is still in force, and further certify that the By-Law of the corporation printed on the reverse hereof is still in force. In testimony whereof I have hereunto subscribed my name and affixed the seal of the said corporation this 16th day of January, 2012.



WESTERN SURETY COMPANY

L. Nelson  
L. Nelson, Assistant Secretary



# CERTIFICATE OF LIABILITY INSURANCE

OP ID: BM

DATE (MM/DD/YYYY)

01/17/12

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

**IMPORTANT:** If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER TD Insurance, Inc. 101 Century 21 Dr Ste 200 Jacksonville, FL 32216 David L. Cain	904-855-0744	CONTACT NAME: Michelle O'Steen	
	904-855-0828	PHONE (A/C, No, Ext): 904-450-4716	FAX (A/C, No): 904-855-0828
		E-MAIL ADDRESS: Michelle.OSteen@tdinsure.com	
		PRODUCER CUSTOMER ID #: SAWCR-1	
		INSURER(S) AFFORDING COVERAGE	
INSURED Sawcross, Inc. 10970 New Berlin Road Jacksonville, FL 32226	INSURER A: Bituminous Insurance Companies		NAIC # 20095
	INSURER B:		
	INSURER C:		
	INSURER D:		
	INSURER E:		
	INSURER F:		

**COVERAGES**

CERTIFICATE NUMBER:

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	GENERAL LIABILITY		CLP3564012	01/01/12	01/01/13	EACH OCCURRENCE \$ 1,000,000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY					DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 150,000
	<input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR					MED EXP (Any one person) \$ 10,000
	Blanket Add'l Ins					PERSONAL & ADV INJURY \$ 1,000,000
	Blanket Waiver					GENERAL AGGREGATE \$ 2,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:					PRODUCTS - COMP/OP AGG \$ 2,000,000
	<input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PROJECT <input type="checkbox"/> LOC					\$
A	AUTOMOBILE LIABILITY		CAP3564013	01/01/12	01/01/13	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000
	<input checked="" type="checkbox"/> ANY AUTO					BODILY INJURY (Per person) \$
	ALL OWNED AUTOS					BODILY INJURY (Per accident) \$
A	<input checked="" type="checkbox"/> SCHEDULED AUTOS		CAP3564013	01/01/12	01/01/13	PROPERTY DAMAGE (Per accident) \$
A	<input checked="" type="checkbox"/> HIRED AUTOS		CAP3564013	01/01/12	01/01/13	\$
A	<input checked="" type="checkbox"/> NON-OWNED AUTOS		CAP3564013	01/01/12	01/01/13	\$
A	<input checked="" type="checkbox"/> Contractual Liab					\$
A	UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR		CUP2588688	01/01/12	01/01/13	EACH OCCURRENCE \$ 4,000,000
	EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE					AGGREGATE \$ 4,000,000
	DEDUCTIBLE					\$
	<input checked="" type="checkbox"/> RETENTION \$ 10,000					\$
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY		WC3564011	01/01/12	01/01/13	<input checked="" type="checkbox"/> WC STATUTORY LIMITS <input type="checkbox"/> OTHER
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH)	<input type="checkbox"/> Y/N				E.L. EACH ACCIDENT \$ 500,000
	If yes, describe under DESCRIPTION OF OPERATIONS below	N/A				E.L. DISEASE - EA EMPLOYEE \$ 500,000
						E.L. DISEASE - POLICY LIMIT \$ 500,000
A	Pollution		CLP3564012	01/01/12	01/01/13	Ltd. Liab 1,000,000
A	Lease/Rent Eqmnt		CLP3564012	01/01/12	01/01/13	Per Item 250,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)  
 Project: Inlet Beach WTP High Service Pumps Upgrade Project No: 12-31  
 St Johns County to be given Additional Insured status as it applies per written contract and is subject to each policy terms and conditions

**CERTIFICATE HOLDER****CANCELLATION**

St Johns County  
 Utility Dept.  
 2446 Dobbs Road  
 St. Augustine, FL 32086

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

© 1988-2009 ACORD CORPORATION. All rights reserved.

- 5) There is not a clear specification for the harness flange adapter couplings on this project. Will SJCUD accept EBBA Iron megaflanges for the HFAC restraint?

*The EBAA Iron MegaFlange is not considered an equal to HFAC. MegaFlanges are not rated for surge and vibration. Contractor shall provide Smith Blair 931 Flange Coupling Adapter, or equal.*

**Drawings:**

- 1) Drawing M-2 calls for 8-inch fillers on the connection between pump volute and existing discharge piping. Engineer would like to clarify that the bidders should include either flange fillers or spool pieces as required to make the connection between pump volute and existing discharge piping.

**THE BID DUE DATE IS CURRENTLY Wednesday, January 18, 2012 by 2:00 P.M.**

Acknowledgment

Signature and Date

1/11/12

Sincerely,

**Sharon L. Haluska**  
Contract Administrator  
Purchasing Department

Mark Hickinbotham, President  
Printed Name and Title

Sawcross, Inc.  
Company Name (Print)

**Attachments:**

1. APPENDIX 1 - Pump Cut Sheet – PDF file (2 pages)
2. APPENDIX 2 - DCR Engineering Services Instrumentation & Controls and Telemetry System Scope of Work – WORD File (2 pages)

**END OF ADDENDUM #1**
