RESOLUTION NO. 2022-121

A RESOLUTION BY THE BOARD OF COUNTY COMMISSIONERS OF ST. JOHNS COUNTY, FLORIDA, AUTHORIZING THE COUNTY ADMINISTRATOR, OR DESIGNEE, TO ISSUE AND EXECUTE TASK ORDER NO: 39 TO THOMAS MAY CONSTRUCTION COMPANY UNDER RFQ NO. 18-05 (MASTER CONTRACT NO: 18-MCC-THO-09215) FOR MUSSALLEM BEACH PARK PHASE II – PARKING LOT CONSTRICTION.

RECITALS

WHEREAS, On March 10, 2022, the County entered into a task order based continuing services contract with Thomas May Construction Company, and

WHEREAS, the Engineering Division of Public Works requires assistance with performing parking lot construction services for Mussallem Beach Park Phase II; and

WHEREAS, the scope of services will be including, but are not limited to, providing paving of the parking lot extension, curbing and sidewalks, rough grading, irrigation chases, compaction testing, stripping and signage, and temporary fencing, in accordance with Task Order No. 39; and

WHEREAS, the County has reviewed the terms, provisions, conditions and requirements of the proposed task order (attached hereto, and incorporated herein) and find that executing the task order to complete the services serves a public purpose; and

WHEREAS, the task order will be in substantial conformance with the attached draft.

NOW, THEREFORE BE IT RESOLVED BY THE BOARD OF COUNTY COMMISSIONERS OF ST. JOHNS COUNTY, FLORIDA, as follows:

- Section 1. The above Recitals are incorporated by reference into the body of this Resolution and such Recitals are adopted as finds of fact.
- Section 2. The County Administrator, or designee, is hereby authorized to issue a task order to Thomas May Construction Company to provide the services set forth therein.
- Section 3. The County Administrator, or designee, is further authorized to execute the task order in substantially the same form as the attached draft on behalf of the County to provide the scope of services as specifically provided in Task Order No. 39.
- Section 4. To the extent that there are typographical and/or administrative errors that do not change the tone, tenor, or concept of this Resolution, then this Resolution may be revised without subsequent approval by the Board of County Commissioners.

PASSED AND ADOPTED by the Board of County Commissioners of St. Johns County, Florida, on this 19th day of April, 2022.

BOARD OF COUNTY COMMISSIONERS OF

ATTEST: Brandon J. Patty, Clerk of the Circuit Court & Comptroller

Deputy Clerk

Christian Whitehurst, Vice-chair

ST. JOHNS COUNTY. FLORIDA

Rendition Date 4/21/22



St. Johns County Board of County Commissioners

Purchasing Division

CONTRACT TASK ORDER NO: 39

RFQ No: 18-05; As Needed, Small Scale Construction, Renovation & Repair Services
Master Contract No: 18-MCC-THO-09215

Contractor:

Thomas May Construction Company

310 College Dr.

Orange Park, FL 32065

Date:

March 11, 2022

Project:

Mussallem Beach Park Phase II - Parking Lot Construction

SCOPE OF WORK:

Task Order #39 is hereby issued to authorize Thomas May Construction Company ("Contractor"), to construct a parking lot at Mussallem Beach Park located at 3315/3350 Coastal Highway A1A, St. Augustine, FL 32084. Work shall include paving of the parking lot extension in two (2) separate and equal lifts of asphalt, all curbing and sidewalks with Contractor providing expansion joints at abutments of concrete and any structure, rough grading of future locations for restroom and pavilion with silt fencing required to be installed along the cleaning limits, two (2) irrigation chases (north and south), compaction testing using a third party testing laboratory, stripping and signage applied in accordance with Florida Department of Transportation (FDOT) Roadway and Traffic Design Standard, Latest Edition, temporary fencing of construction area and construction bond. Engineering plans dated 01/27/22 from Gulfstream Design Group, LLC shall be used for construction of this project, as proposed in the Contractor's proposal dated March 10, 2022, and attached hereto.

PAYMENT TERMS:

The County shall compensate the Contractor, under Task Order #39, a lump sum amount of two hundred thousand dollars (\$200,000.00), for work satisfactorily completed in accordance with the provisions of this task order, and with the Master Contract dated March 29, 2018.

SCHEDULE:

The Contractor shall commence work upon receipt of a fully executed Task Order. The Effective Date of this Task Order shall be the date of signature by an authorized St. Johns County Representative. Work shall be completed within ninety (90) consecutive calendar days from the Effective Date of this Task Order. Any work performed prior to full execution of this Task Order shall be at the Consultant's Own Risk.

Receipt of a fully executed copy of this Task Order shall serve as the Notice to Proceed for this project.

Thomas May Construction Company	St. Johns County	, Fiorida
Representative Signature:	Representative Signature:	
Printed Name & Title:	Printed Name & Title:	Leigh A. Daniels, CPPB Purchasing Manager
Date:	Date:	

All terms and conditions of the above-referenced Master Contract dated 03/29/18 remain in full force and effect. All invoices <u>must</u> reference Task Order #39. By approving this task order, the SJC Dept is certifying the availability of funds for this. Do not approve/process this task order until funds are available in the appropriate line item.



310 College Drive Orange Park, Florida 32065 (904) 272-4808 Fax (904) 272-4957

GENERAL CONTRACTOR CGC1530508 **ROOFING CONTRACTOR** CCC057770

March 10, 2022

St. Johns County Construction Services Attn: Scott Augustine 2750 Industry Center Dr St. Augustine, FL 32084

Re: SJC Mussallem Beachfront Park Parking Lot Phase 2

Mussallem Beachfront Parking Phase 2

For the Sum of: \$200,000.00

Inclusions: All materials, labor and equipment to construct phase 2 of the parking lot as designed in provided plans by Gulfstream Design Group dated 01-27-2022, page 5 (see attached plans). This includes paving the parking lot extension, curbs, sidewalk, rough grading of future locations for restroom and pavilion, (2) irrigation chases (north and south), compaction testing, stripping, signage, temporary fencing of construction area and construction bond.

Exclusions: Any permits, surveys, relocation of any obstructions or utilities interfering with construction, export of any material including brush or trees, landscaping, irrigation, sod, seeding, MOT and any work or cost not directly associated with the listed items above.

Thomas May Construction may withdraw this proposal if not accepted within 30 days. Acceptance Date Please feel free to contact me if you have any questions regarding this proposal. Sincerely,

Scott Chandler Scott Chandler

Project Manager, TMC

ENGINEERING PLANS

FOR

MUSSALLEM BEACH PARK PHASE II

ST. JOHNS COUNTY, FLORIDA

PROJECT TEAM

SURVEYOR SURY VETOR:
ST. JOHNS COUNTY LAND MANAGEMENT
SURVEYING AND MAPPING DIVISION
SOS AN SERSTIAN VIEW
8T. AUGUSTINE FL. 37084
PHONE: 609.200.0704
FAX: 604.200.0707
CONTACT CAULI CUIVER: PLS

DEVELOPER/APPLICANT

CIVIL ENGINEER:

PRIVATE UTILITY COMPANIES

TV CABLE

TELEPHONE

TECO PEOPLES GAS P.O.BOX 31318 TAMPA FL 33631 PHONE 904-477-6908 CONTACT: MICHAEL SUN

ST. JOHNS COUNTY DEVELOPMENT SERVICES

PUBLIC UTILITY PROVIDERS

REGULATORY AGENCY

FDEP - WATER & SEWER

ST. JOHNS RIVER WATER MANAGEMENT DISTRICT

GENERAL NOTES:

- IT IS THE RESPONSIBILITY OF THE CONTRACTOR TO REVIEW ALL THE DRAWINGS AND SPECIFICATIONS ASSOCIATED WITH THE SPRINGET WORK SCODE PRIOR TO THE MINITARION OF CONSTRUCTION, SHOULD THE CONTRACTOR FROM A CONFLICT WHITH THE CONTRACTOR FROM A CONFLICT RESPONSIBILITY TO WITH THE PROJECT EXAMELS OF RECORD IN WRITING FROM THE CONFLICT WAS RESPONSIBILITY TO WITH THE PROJECT EXAMELS OF RECORD IN WRITING FROM THE CONTRACTOR RESPONSIBILITY TO WITH THE CONTRACTOR OF THE RESPONSIBILITY OF THE CONTRACTOR OF COMPLETE THE SECORE OF THE WORK AS DEFINED BY THE REPROMISED AND FULL CONFIDENCE WITH CONTRACTOR OF THE CONTRACTOR OF CONTRACTOR OF THE CONTRACTOR
- APPLICABLE LAND DEVELOPMENT CODES.
 ALL ELEVATIONS SIXMAN HERREN ARE REFERENCED TO NORTH AMERICAN GEODETIC VERTICAL DATUM 1998 (NAVO 88).
 HORIZONTAL, PROJECTION FOR THIS PLAN SET IS BASED ON NAOBS FLORIDA STATE PLANES, EAST ZONE. US FOOT.
 LEGAL DESCRIPTION: SEE SURVEY.

LOCATION OF SITE

3315/3350 COASTAL HIGHWAY A1A PARCEL ID # 142660 0000



LOCATION MAP

PREPARED FOR

ST. JOHNS COUNTY

500 SAN SEBASTIAN VIEW ST. AUGUSTINE, FL 32084 PHONE: (904) 209-0192 CONTACT: SCOTT AUGUSTINE

PREPARED BY



@GDG 2021 2225 A1A S, SUITE A2 ST. AUGUSTINE, FLORIDA 32080 Phone: (904) 794-4231 www.gulfstreamdesign.com

ENGINEERING PLANS

SHEET NUMBER	SHEET TITLE
1	COVER SHEET
2	GENERAL NOTES
3	SWPPP
4	AS-BUILT SURVEY
5	SITE PLAN
6	GRADING & DRAINAGE PLAN
7	LANDSCAPE PLAN
8	IRRIGATION PLAN
9	CONSTRUCTION DETAILS

SHEET INDEX



 \equiv SE

PHA!

MUSSALLEM BEACH PARK
COVER SHEET
ST. LOINES COUNT. FLORIDA

ENGINEERING PLANFOR

GULFSTREAM

REVISION REVISION DATE

Name and American programme and

CHECKED BY:

P.E. FLE 7139

FLOOD ZONE

ENGINEERING PLANS BASED ON

COMPANY NAME

PLAN TYPE

THE SUBJECT PROPERTY IS LOCATED IN THE FLOOD ZONE "X" PER FLOOD INSURANCE RATE MAP COMMUNITY PANEL NUMBER 1210900376H, DATED SEPTEMBER 2,2004

Matthew H. Lahs, FL PEst 71385 has digitally signed this document on January 28, 2022. This digital asynature encompasses pages 1-9 of this document. Printed versions of this document are not considered spinal and

CLEARING/DEMO AND EROSION CONTROL NOTES: THE TOTAL SECURITY OF OWN AN ADMINISTRATION OF THE ADMINISTRATION THE STATE OF THE SECONDARY OF THE STATE OF THE STATE OF THE SECONDARY OF THE STATE OF THE SECONDARY OF THE S AREAS ADJACENT TO THE PROJECT AREA ARE TO BE PROTECTED AND LEFT UNDISTURBED UNLESS WOTE THE CONSTRUCTION DOCUMENTS. THE INFORMER OF RECORDS NOT RESPONSING FOR MAY HAVING DAMAGES REQUESTED FROM THE CONTRACTORS FAURE TO USE OF COULT WORK IN STRET, ACCORDANCE MAY THE APPROPRIE PLANE, IT HE CONTRACTOR MARCH COMBET MAY TO BUT ON CONTRACTOR THE STREET OF RECORDANCE HAS PROPRIED FOR MAY FOR THE OTHER TO APPLY TO STREAM, IT RESIDANCE AND FOOD THE SUBBRIED OF RECORD PARKETS OF ALL NAMES AND DAMAGES THAT THE SUBBRIEF HAS SHEED AND FOOD THE SUBBRIEF OF RECORD PARKETS OF ALL NAMES AND DAMAGES THAT THE SUBBRIEF HAS SHEED AND FOOD THE SUBBRIEF OF RECORD PARKETS OF ALL NAMES AND DAMAGES THAT THE THE USE OF THE WORD 'S CRITEN' WITHIN THIS ENGINEERING PLAN SET, MAPLES AN EXPRESSION OF PROFESSIONAL OPHION ESCHOLARS FEED AUGUSTUS OF CONTROL ECURION FEED AUGUSTUS OF CONTROL EXPRESSED ON ARMERS, AUG THE CONTRACTOR SHALL BE REPORTING FOR OBTAINING ALL NECESSARY PERMITS, INGURANCES, AND LICENSES PERTAINING TO THE WORK A LLUSTRATED IN THIS PLAN SET. ALL MATERIALS AND LABOR ASSOCIATED THEIR MET TO BE WARRANTED BY THE CONTRACTOR FOR A TIME PERIOD OF ONE INCALEDARY FURNITION THE ASSOCIATIONS OF THE PROJECT BY THE OWNER AND ALL APPLICABLE CONTRINUENT AGRICLES. THE CONTRACTOR SHALL PROMIE ASSAUL SUMMY, RECURRAGE BESTIMMES, DO DAMES AS REQUIRED WITE SHALL SUMMY. SHALL THE CONTRACTOR SHALL CONTACT THE APPLICABLE FRANCHISE UTILITY COMPANY (RE ATAT, TECO GAS, FPBL, ETC. AS APPLICABLE) AND COORDINATE ANY CONSTRUCTION IN ADVANCE OF COMPIENDING CONSTRUCTION. PRIOR TO THE AMADO OF THE CONTRACT, THE COMTRACTOR SHALL RECOME ACQUARTED WITH THE RESERVENCE WITH ALL SITE CAMPIFERS BOTH AND OF AND RELOCATION OF GROUND. THE CONTRACTOR SHALL DESIGNED ADMITTANT AND THE RESERVENCE THE AND THE THE PROPERTY OF THE AMERICAN AND RESERVED AND THE RESERVED THE ALS SHATHAN THE PARAMEDIA WITH ALL PROPERTY OF THE PROPERTY READ TO THE COMMENCEMENT OF MAY COMMENT, TO MAINTHEE, ME CONTINUTORS, TO OWNER MAINTHAN HAVE NO MAINTH AND THE COMMENT AND THE ALL ELEVATIONS ARE BASED ON HORTH AMERICAN VERTICAL DATUM 1989 (MAYD 98) AND SHOWN IN FEET, BENCHMARK A Elevation being 7.20: ERETHIG JEHRYT HICHMETEN PROJECT DE ST. JOHNE COLINTY LINE MANUFERT SYSTEME INDHING HEI DEREY DANDEN HOLTEN MER STEIL LEN HEIGHEN TON HICHMETEN DE PLAN SETT MAKE BEIT MAKETO OF OF THE AROVE ATSFERDICE SUMMEY THE DAGNIFER OF HEIGHD ASSIMES HOR RESPONDBILLTY FOR THE ACQUIRACY OF LICET THEREOY. THE CONTRACTOR IS REPORTED TO ECOMPANY OF THE CONTRACTOR SET THE THING THE ASSET IN ECONTRACTOR IN THE CONTRACTOR SET THE CONTR ANY TREE THAT IS DAMAGED DURING THE TIME OF CONSTRUCTION BHALL BE CONSIDERED MEJACHED AND SHALL BE REPLACED BY THE CONTRACTOR WITH NO COST TO THE CHAMPER. ONLY SUPPORTURE LANDSCAPING ELEMENTS MAY BE ATTACHED TO PRESERVED ON PLANTED TREES, NO SIGNAGE PREMITS, AND ON STACES MAY BE ATTACHED TO A TREE ON THE SUBJECT PROPERTY. ALL ADJACENT PROPERTY CHARGES AND BUSINESSES ARE TO BE PROVIDED ACCESS TO THOR STEES AT ALL YIMES THROUGHOUT THE DURATION OF CONSTRUCTION ACTIVITIES. ALL DISTURBED AREAS WITHEN THE ST. JOHNS COUNTY RICHT-OF-WAY WILL BE RESTORED TO DIREGIMAL OR BITTER CONDITION BY GRADING AND SOIDING THE AREAS DISTURBED (BERMAIDA BLITIKAL CIXTIPEDE IN UTILITY STRIPS). ANY POTENTIAL DISCREPANCIES WITHIN THIS PLAN SET THAT THE CONTRACTOR PRIOS SHALL BE INFOLMED TO THE ATTEMPTOR OF THE ENGINEER OF RECORD IN MEDIATELY IN WRITING. N, Mª (PRINT THAT MEDIFECTED ARCHEOLOGICA, RECOMPLES ARE DECLARITARIO DURANG GALOHO DISTRIBRIG ACTIVITES. ALL MORK SHALL HALT AND THE DIGINERS OF RECORDS DOPICE SHALL BE CONTACTED MANERIATES Y MRITING. PRIOR TO FMAL ACCEPTANCE, THE CONTRACTOR SHALL PERFORM SITE CLEANUJP OPERATION FOR REMOVAL AND DISPOSAL OF ALL TRASH, DESIRIS, PIPE, EXCESS MATERIAL AND SOLIPMENT OFFSITE. ALL MORE WITHIN THE ST. JOHN'S COUNTY RESIT-OF-WAY MUST CONFIGH[®] OF \$1.50 CURRENT LAND DEVELOPMENT CODE I STANDARDS AND SPECIFICATIONS. CONSTRUCTION SHALL BE IN ACCORDINGE WITH THE ST. JOHNS COUNTY LIND DEVELOPMENT CODE OR THE HANDIA OF UNIFORM TRAFFIC CONTROL DEVICES INJECTS WHICHEVER IS MORE RESTRICTIVE. THE BURNESS OF RECORD AND THE CHARTER ASSUME NOT REPORTABLET IN THE SUFFRANCIAL OF AND FICTION OF THE WARR MARKARED IN THE EXECUTION OF THE COMMENT BE CHOST COMMENTED TO BESIDE. TO THE CHARTER THE AND FILE THE CHARTER AND FILE THE REMOVAL OF ALL VEGETATION AND TOPSON, ON THE PUTURE ROMONAY, PARKING AND BUILDING LOT AREAS IS REQUIRED TO BE COMPLETED PRIOR TO THE PLACEMENT OF FILL ON THESE AREAS, THE TOPSON, MAY BE TEMPORARIX. ATTOR SHALL REPORTED FOR CONTROL AND VERFEAR ON, UNITER 3 FOR A BIT FROM BOT THE ATTOR AND THE ATTOR ANY MATERIAL OR DEBITS CHAFTE IS PROHIBITED. SHALL SHALL SHEEMEN SHALL SHAL SITE LAYOUT NOTES: 1. ALD IMPRISONS ARE TO THE EDGES OF PAVEHENT UNLESS OTHERWISE HOTED. PAVING, GRADING, AND DRAINAGE NOTES: ADA GUIDANCE TO CONTRACTOR: La considera en la contra contra contra en la contra en l'El 1.1. La contra en la contra contra en la contra contra en l'El 1.1. La contra en la contra en la contra contra contra en la contra en la contra en l'el 1.1. La contra en la SIDEWALKS ADJACENT TO PAVEMENT SURFACES ARE TO BE THICKENED ÉDICE SUDDWALKS, ALL TYPE TO CURBAIO SHALL HAVE À THREE (1) POOT TRANSITION AT ALL TERMANS LOCAT GRADE. ALL PAL MATERIALS LOCATED REMEATH STRUCTURES AND PAREMENT SMALL COMEST OF HEW CLEAN GRANDLAR SAND FREE FROM ORIGANICS AND SMALAR MATERIAL THAT COLID DECOMPOSE. WHERE RETURNING WALLS (AMETHERS OR NOT THEY MEET THE AUTOCOCTOMAL OLEMITON), HE DESITTED ON FAMS. ELEVATIONS CONTROL HE FOR THE LESCOOD PORTION OF THE WALL, WALL CONTROLOGOUGH TOWN LEWATORS ARE NOT INSTITUTED HERE HE AND ALL OF THE CENTRE OF THE CONTROL OF THE AL BROKBUCHACHED DRAYDWAYS AUST BE FULLY REGISTED AND BEHACED. THE COMMAL RESEACE OF GROUNDWATER BROULD BE ANTEWATED THE CONTRACTORS BID BROULD WILLIES THE ANTEWATED COST OF BREETER. SI, T FONCE SHALL BE NISTALLED ALONG THE CLEARING LIMITS. GRAINHOLL REPRESENTATION OF CLEARING LIMITS AND SILT FONCE IS EXAGGRATED FOR PICTORIAL PURPORES ONLY. THE CONTRACTOR IS REQUIRED TO USE THE RECOMMENDATIONS FROM THE CROTECHNICAL ENGARER ON THE PROJECT FOR FINAL PILL COMMETION AND DENSITY SPECIFICATIONS THROUGHOUT THE PROJECT. ALL ELISTRAD CATCH MARKS ADJACENT TO THE STEE SHALL BE CONTRED WITH FRITES YARRE TO PREVIOUS SEGMENT PROMISHERMENT THE STREAL THE FRITES MARKE SHALL BE REPECTED AND MARTIANED DIALY THROUGHOUT THE COMMITTING OF CHROSTROCTON. P AVVINIGITARIE MATRINIE DESCONTRED. IT SMIL IR RECOMBOTO DE RESCONDAD REPLICID MET SITTARIE MATRIMI, TMAT REPORTRY DECRETICED COMPACTO AND TRETEU SPAG AUSTICO I IR ROOMINGO PIOTECTON METHOD AND ATTRE DIRECTION OF THE ACOTICHANCE UNIMERE OF RECOND. FIL MATERIAL IS TO BE PLACED IN ONE FOOT LIFTS AND COMPACTED TO THE APPROPRIATE DENSITY UNDER SUPERVISIO OF A LICENSED DEOTECHNICAL ENDINEER. ALL PARABOT RETONN AND SHALL BE INFLAMED TO THE EDGE OF PAREADIT SUBFACE UNITES OTHERWAS HOTED DTICH DOTTOWAND CONTROL STRUCTURE BLET GAATES SHALL BE SUATED PROPERTY. FARE OF FETT OF SCOIN REQUIRED AREASON ALL DETCH ROTTOW WILETS, MANIMALES, HALDWALLE, TIC. ALL NON-PAYED DISTURBED AREAS TO BE SOCIOED AND STABILIZED WITHIN SEVEN (7) DAYS OF THE DISTURBANCE UNLESS OTHERWISE WOTED. CONTRACTOR MUST CONTRIBUTE CARE MAN PRICIPIEM WHO RECONSTRUCTION AND ACCESSIBLE COMPONENTS OF THE PRISE MERCHANISH AS PERSONAND TO MERCHAN ACT TO MESS COMPONENTS MUST CARE WAY WITH THE CORREST ADA. STRUMANDES AT THE TIME OF THA APPROVAL. THESE TRUES INCLIDER WIT ARE NOT LIMITED TO 1.1. AVAILABLE PLATES AND ALKELY. 1.1. SOME SHALL WITH EXCERCITION CAN IN ANY ORDERTICAN. ada Alaw's shali be'nista leo at ali sob'nalegune nitersetions ali ada Raup's shali cantonin to detar s Korts and deterrations from the fidot obsernannal latest editich nodix no das anetts 1 through 8. Appleare. THE CONTRACTOR SHALL COORDWATE MAY OF R-SITE IMPROVEMENTS WITH ST. JOHNS COUNTY 7 DAYS PRIOR TO CONSTRUCTION. ALL AMERICANS WITH OSSANLTIES ACT JADAI RAMPS TO METT CURRENT ADA CHITERIA AND INCLUS A DETECTANLE WANNING, COLOR SELECTICA FOR DETECTANLE MARRIAGI TO BE COCKIDIANTED WITH COMMEN PRICE TO DISCENAND PALICEMENT. ALL TYPE "D" CLIXIBNO SHALL HAVE A ONE (1) FOOT TRANSTION AT ALL TERMINUS LOCATIONS WHEN TYNO BACK TO GRADE ALL EXISTING CURB AND OUTTER AND SIDEWALK SHOWN TO BE REMOVED, WILL BE REMOVED AND REPLACED JOINT TO JOINT, CONTRACTOR BUST REFER TO STORMWATER POLLUTION PREVENTION PLANCH SHEET # SWEEP AND ABOURT ALL CONDITIONS. -where walch of other dolume wateral is removed it shall be replaced by dood dultity wateral wateral wateral contact and the dollars of the downers of beautified by the downers of beautified of the downers of beautified by the downers of beautified STOCKMED AND USED AS TOPSON, OVER PROPOSED GREEN AREAS SUCH AS PLANT BEDS, BODDED AREAS AND WHERE TREES ARE TO BE INSTALLED OR RELOCATED. WHOPAST OR FIQUAL SHALL REUSED WHERE HOTED AND SHALL ACCOMMODATE THE PREJECTION AND ANGLES HOTED. SHOWLD THE PRESIDENT REARLETO BE ACCOMMODATED, THEN A TIPE TO HALT SHALL BE SUBSTITUTED AT SALD JOSEDOWN, CHARGET TO THE OWNERS THE CONTRACTOR IS TO COORDINATE THE COSMICT POINTS AT UTILITY WITRIFACES AROUND THE SITE. CLEANANCES SMOULD BE MET AN ACCORDANCE WITH FORM BULES AND MER THE ST. JOHNS COUNTY: STANDARDS NOTED IN THIS PLAN SIT. METRICA DE SICTORS SANT COMPONATO FOCH ROCK RAIS-QUI, METRICA (ROCK) SICTORS IN POURS SANT COMPONATO FOCH ROCK RAIS-OUT DICTRIDITION MICTIS SANT CONFORM TO FOCH MOCK RAIS-KST. STONM MAMPOLIS SANT COMPONATO FOCH ROCK RAIS-ROIT IT IS ENCOURAGED THAT THE CONTRACTOR REVIEW THE INTENDED CONSTRUCTION WITH THE LOCAL BUILDING CODES AND PRECIOD AFTER STAGING AND BEFORE COMMENCEMENT OF CONSTRUCTION. CONTRACTOR MUST VERBY SLOPES PRIOR TO COMMERCING ARY CONSTRUCTION ACTIVITIES. IF THERE ARE ARY NOW, COMPORISMMES THAT EXIST, THE CONTRACTOR MUST NOTIFY THE ENGINEER OF RECORD IN WRITING INMEDIATELY the contemptor shall be responsible for verification of all betraces and/or existing easembits before Scorming Construction. tidan structum pres that exceld the schol for the Consts, at 10 be constructed with alternate soft data with Managam dameters to accommodate pre size and/of fire ameles fir foot 1800 for 23 50 and 23 801. Fire E Dettom. E CONTRACTOR SHALL LAYOUT SACH AREA OF WORK TO CHEEK DIMENSIONED PRICE TO CONSTRUCTION AND DORDHANT WITH OFFIER BRICKIN HEEK SOLULD ANY DOKENBANCHES KERN, THE CONTRACTOR IS TO HOTEY, IN WRITHING, E OWNERS REPRESENTATIVE AND THE ENQUREER OF RECORD DAMEDWITELY. OGDIN CONTRIQ, AND REDINENTATION CONTRICL TRYMESS SHALL RE IN PLACE PRICE TO REGINNING CONSTRUCTION. TO SHALL RE REPLACE DAY DAY DAYD MAN DE THROUGHOUT THE COURSE OF CONSTRUCTION, AS STRUCTIONES AND INCHES SEE ADORST OT THE PROJECT SITE, STAKE OUT MUST BE PERFORMED UNDER MIPPENSION OF A LEDINGED NOTION AS THE STATE OF FLORIDA. BHOLDS PERIOR TO CLEANS, THE CONTRACTOR IS RESPONMENTED BY ANALYSIS AND PLAS SHOTTED OF CONTRACTOR OF CHARACTERS OF THE MANAGEMENT AND PLAST CONTRACTOR OF CONTRACTOR SHALL PROVIDE A COMP OF THESE DOCUMENTS OF THE MANAGEMENT OF T SIGNAGE AND PAVEMENT MARKINGS NOTES: OVERALL TESTING NOTES: ALL SIGNAGE AND PAYEMENT MATISHOS SHALL BE IN ACCORDANCE WITH FOOT ROADWAY AND TRAFFIC DESIGN STU-LATEST EDITION. , PAY SAMP ES SYCULO RE EXAMAND NA "SYKKATSYN-TROM" PRA THE STANDANDS OF THE GEOTECHNICAL BROWLER OF RECHO, THANKLAY CONCENT WALL IE REMONRED AT THE CONTRACTORS EXPENSE ONTE THE EXPEL OF "ALTEXATOR'S BASE". SOFICIAL OF MAJO CASTRICITOR HERMAD SHA, BE A FOLLOWS 1.1. SOFFICE SHA WE TESTE SHALL BY THE FRANCH OF MAJO CHECH SET THE TAIL OF THE THAT HERMAD OF MAJO SHA MAJO CHECH SET. 2.1. MAJO SHATIN THE TEACH HAS ESPACESSON FROM NOT THAN MOD INSEAS FEET. ALL TESTING SHALL BE TAKEN HAS ESPACESSON PATTERN HITHER THE ESPAC OF PARENDER BOANDARY. THE CONTRACTOR SHALL TRILET HE SERVESS OF A THEIR MARY TESTED LANDACTORY TO CONSULT ALL REQUIRENT TO MAY RECOVER AND ANALYSE AREA TO MAY RECOVER AND ANALYSE ANALYSE AND ANALYSE AND ANALYSE AND ANALYSE AND ANALYSE AND ANALYSE ANALYSE AND ANALYSE AND ANALYSE AND ANALYSE AND ANALYSE AND ANALYSE ANALYSE ANALYSE AND ANALYSE ANALY SION PLACEMENT BHOWN IN FLANG IS APPROXIMATE. FINAL LOCATION SHALL BE AS DIRECTED BY ENGINEER OF RECORD \$449ECTOR(5) AND CAMER, ALL PARTEINET MARBAIS TO BE NACCORDANCE WITH FOOT NOTE NO. 71-401, THE CONTRACTOR WILL BE RESPONSIBLE ORN MALERIEMPHON TEMPORATE PARTEINET MARBAIGS (MITL THE PINAL SURFACE COURSE NAS CURED (MINICIAL PHINT) (20) DAYS AFTER FINAL SURFACE COURSE PARKEISH). KOM SIGN DETALS REFER TO THE MANUAL ON UNIFORM TRAFFIC CONFROL DEVICES PUBLISHED BY U.S. DEPARTMENT OF TRANSPORTATION, FEDERAL HIGHWAY ADMINISTRATICM, LATEST EDITICM, ALL PAVEMENT MARRHOUS ARE TO BE PAINTED WITH THERMOPLASTIC PAINT IN ACCORDANCE WITH FOOT STANDARDS Unit Ess otherwise hoted on the plays. ALL GROUND MOUNTED STOP: YELD, MRONG WAY, DO HOT ENTER SIGN FACES SHALL BE FABRICATED ENTIRELY WITH TYPE TO REFLECTIVE SHEETING. THE CONTRACTOR SOLL, HE RESTORMENT FOR CORDINALISMS THE REQUIRED SET TEMPORATION OF GEOTER CONTRACT, REQUIRED, MISS OF ELORIED HE ACCOUNTED HE RESTORMENT FOR SCHOOLS HAVE SHOWN ON THE SET THOM CONTRACTOR OF THE COUNTE STATES OF THE COUNTED HE COUNTED HAVE SHOWN IN STATES OF THE COUNTED HAVE COUNTED HAVE SHOWN IN STATES OF THE COUNTED HAVE C THE CONTRACTOR IS TO SUBMIT A PROPOSED XXMETMA PATTERN TO THE OWINER AND GEOTECHNICAL ENGINEER OF RECORD FOR APPROVAL PRIOR TO PLACEMENT OF ANY CONCRETE PAYSMENT. PAVEMENT SHALL BE PLACED AN TWO EQUAL LIFTS. THE SECOND LET SHOULD BE PLACED AFTER THE SHAL CERTIFICATE OF OCCUPANCY UNLESS THE OWNER AND THE ENGINEER OF RECORD REQUESTS OTHERWISE IN VARTING. THE CONTRACTOR SHALL PROVIDE EXPANSION JOINTS AT ABUTIMENTS OF CONCRETE AND ARY STRUCTURE UNIFFEREN DEDIGH GEORY (C.C. WAR REVIEW OF THE EMPOSPHET I CTOMAS PERIONEO TO INTRODUCE DESIGNATION OF THE CONTROL PROPERTY OF nil defurbed area tha't will be diposed for more t driven and 'n wid blown sediment LL EXISTING CURB AND CLITTER AND SIDENINLE SHOWN TO BE REMOVED, WILL BE REMOVED AND REPLACED FROM JOINT O JOINT. dom, of disting parenty materias shall be accompised using the "modellast" hethigo if this Cees damesescent parenty then the parenty that, be nalled and rediringed the liters cotton I standards and recordantias. IO PANTENENT MARKINGS SMALL 44 ION WITH EXISTING PANTENENT MARKINGS AT PANTENENT MARKING LIMITS OF JOTICIN. Mary I Decision | Annual Property | Annual Prope In the control of the SCHEDULE OF TESTING astructural paragraphic astructural paragraphic see ET MICH. SCHOOL SEALO BONDO. SCHOOL SHOPPER SCHOOL SHOPPER STANDARD. AND CONTROL OF THE CONTROL OF T



62



GENERAL NOTES ST. JOHNS COUNTY, FLORIDA

REVISIONS DESCRIPTION

AUSTRACTOR IT NO. CR O CHOCK CAN'T

CONTRACTOR IN THE

Control of the Contro Let Symbolish and the symbolis

GENERAL NOTES

STRANDAMS. ALL CONTRACTORS AND SUBCONTRACTORS WAS SAVEN TO SUPPLY ASSESSMENT AND SUBCONTRACTORS AND SUBCONTR

SEQUENCE OF MAJOR EVENTS

THE ORDER OF A CRITICAL WALL HE ALFOLOUS PROPERTY OF THE ALFOLOUS PROPE

TIMING OF CONTROLS / MEASURES

A RECORD OF THE STOCKE OF THE OWNER AND THE STEPPING AND THINGTHE BLOCK THANKED, CONTINUEND AND THE STREAM OF THE STANDARD CONTINUEND AND THE STANDARD OF THE

CONTROLS

IT IS THE CONTRACTORS RESPONSIBILITY TO IMPLEMENT THE EROSION AND TURBIDITY CONTROLS AS SHOWN ON THE CLEARING AN EROSION CONTROL PLAN. IT IS ALSO THE CONTRACTORS RESPONSIBILITY TO ENSURE THESE CONTROLS ARE PROPERLY INSTALLED INEC AND FUNCTIONING PROPERLY TO PREVENT TURBLO OR POLILITED WHITE 7 FROM LEAVING THE FIRE ACTOR WILL ADJUST THE EROSCION AND TURBEDTY CONTROLS SECKION ON THE CLEARING AND EROSCION OUTDOMAL CONTROL MEASURES, AS REQUIRED TO ENSURE THE SITE MEETS ALL FEDERAL STATE AND INTY CONTROL REQUIREMENTS. THE BEST MANAGEMENT PRACTICES WILL BE MAP LIBENTED BY THE CO

ROSION AND SEDIMENT CONTROLS STABILIZATION PRACTICES:

SYNTHETIC BALE BARRIER. SYNTHETIC BALE BARRIERS CAN BE USED BELOW DISTURBED AREAS SUBJECT TO SHEET AND EROSSON WITH THE FOXLOWING UNITATIONS:

A. WHERE THE MAXIMUM SLOPE BEHIND THE BARRIER IS 33 PERCENT.

B. HIMON SIMLES OR DITCH LINES WHERE THE MAXIMUM CONTRIBUTING DRAINAGE AREA IS NO GREATER THAN 2 ACRES REFER TO THE OFFASTE FABRIC BARRIER.

SNIT FENCE SHALL BE INSTALLED AROUND PERINETER OF SITE TO LIMIT THE AREA OF DISTURBANCE

STOCKPRING MATERIAL IN O EXCAVATED MATERIAL SHALL BE STOCKPRED IN SUCH A MAMMER AS TO DIRECT RUNOFF DIRECT OFF THE PROJECT SITE INTO MAY ADJACENT WATER BODY OR STORM WATER COLLECTION FACILITY. MAY EXCAVATED MATERIA MUST REMAIN ON THE PROJECT SITE.

EXPOSED AREA UNITATION. THE SURFACE AREA OF OPEN PAIN ERGORNE SOIL EXPOSED BY CLEARING AND ORUBBING OPERATIONS OR EXCAVATION AND FILLING OPERATIONS SHALL NOT EXCEED 10 ACRES, URLESS APPROVED BY THE ENGIR

NUET PROTECTION: NUETS AND CATCH BASINS WHICH OSCINANCE ORECTLY OFF-SITE SHALL BE PROTECTED FROM SEGMENT-LADEN STORM RUNOFF UNTIL THE COMPLETION OF ALL CONSTRUCTION OPERATIONS THAT MAY CONTRIBUTE SEGMENT TO THE RULET.

TEMPORARY SEEDING, AREAS OPPOSED BY CONSTRUCTION OPERATIONS AND THAT ARE NOT AN TOPPATED TO BE RELECTIVATED OF THE PROPERTY OF

TEMPURARY SECONG AND MULCHING. SLOPES STEPPER THAN 6 I THAT FALL WITHIN THE CATEGORY ESTABLISHED IN PARAGRAPH 8 ABOVE SHALL ADDITIONALLY RECENS MULCHING OF APPROXIMATELY 2 MORTES LOOSE MEASURE OF MULCHING ON APPROXIMATELY 2 MORTES LOOSE MEASURE OF MULCHING AND ADMILLOR. MATCHING LOT NOT THE SCELO PARA ADEQUATE TO PREVIENT MOVEMBER OF SEED AND MULCH.

MAINTENANCE, ALL FEATURES OF THE PROJECT DESIGNED AND CONSTRUCTED TO PREVENT EROSION AND SEDNERT SHALL BE MANTANED DURING THE LIFE OF THE CONSTRUCTION SO AS TO FUNCTION AS THEY WERE CREMANLY OBSERVED AND CONSTRUCTED.

PERMANENT EROSION CONTROL. THE EROSION CONTROL FACILITIES OF THE PROJECT SHOULD BE DESIGNED TO MINIMIZE THI IMPACT ON THE OF FETTE FACILITIES.

STRUCTURAL PRACTICES:

TEMPORARY DIVERSION DIVE TEMPORARY DIVERSION DIVES MAY BE USED TO DIVERT RUNOFF THROUGH A SEDIMENT-T FACILITY AND IT SHALL BE CONSTRUCTED IN ACCORDANCE WITH THE DETAILS.

TEMPORARY SEDIMENT TRAP A SECOMENT TRAP SHALL BE INSTALLED IN 1 JM BANGE WAY AT A STORM DRAIN INLET OR AT CHIER POWTS OF DISCHARGE FROM A DISTURBED AREA. REFER TO DETARS.

OUTLET PROTECTION: APPLICABLE TO THE OUTLETS OF ALL PIPES AND PAVED CHANNEL SECTIONS WHERE THE FLOW COLLC CAUSE BROSKON AND SEPOMENT PROBLEM TO THE RECENTION WATER BODY. SILT FENCES AND SYNTHETIC BALES ARE TO BE INSTALLED IMMEDIATELY DOWNSTREAM OF THE DISCHARGING STRUCTURE AS SOCKOM ON THE OUTLET PROTECTION DETAIL.

DEFINITION DESIGNATION TO CONSTRUCTIONS OF THE OBSERVATIONS OF THE CONTROL OF THE COURT OF THE C

WASTE DISPOSAL

WASTE DISPOSAL

WASTE MATERIALS:

WASTE MATERI

ACATRODUS WASTE:

ALL HAZARDOUS WASTE MATERIALS WAL BE DEPOSED OF IN THE MAINER SPECIFIC BY LOCAL OR STATE REQUIATION OR BY THE MAMPLACTURES FRACTURES AND THE MET SUPERIFICATION THE ROMOZUMA WHO MAMPLACTURES THE FRACTURES AND LIKE HIS SUPERIFICATION THE ROMOZUMA WHO MAMPLACE DAY TO-GAY OPERATIONS WALL BE RESPONSIBLE FOR SCEND THAT THISSE PRACTICES ARE FOLLOWED.

WASTE DISPOSAL

WASTE DISPOSAL:

SANITARY WASTE: ALL SANTARY WASTE WILL BE COLLECTED FROM THE PORTABLE UNITS AS WEDDED TO PREVENT POSSIBLE SPRLAGE. TH WASTE WILL BE COLLECTED AND DEPOSED OF IN ACCORDANCE WITH STATE AND LOCAL WASTE DISPOSAL RECREATIVES FOR GANIFIARY DEVELOP OR SPETIC, NOTFILE.

OFFSITE VEHICLE TRACKING: A STARZED CONSTRUCTION PRIMARE WALLE PROVIDED TO HELP REDUCE VIPICE TRACKING OF SEDIMENTS. THE ASTARZED CONSTRUCTION PRIMARE WALLE PROVIDED TO HELP REDUCE VIPICE TRACKING AND DESCRIPTION PROVIDED PROVIDED THE TIME TOWN PROCESS HAVE MORE AND RETRAIN TO RESONATION THE WALLE CONSTRUCTION THE WALLE OFF CONSTRUCTION THE

MAINTENANCE / INSPECTION PROCEDURES

EROSION AND SEDIMENT CONTROL INSPECTIONS AND MAINTENANCE PRACTICES.

ALL CONTROL MEASURES WILL BE HISPECTED BY THE SUPERNITENDENT, THE PERSON RESPONSISLE FOR THE DAY-TO SITE OPERATION OR SOMEONE APPOINTED BY THE SUPERNITENDENT, AT LEAST ONCE A WEEK AND FOLLOWING ANY S EVENT OF D.S ONCES OR GREATER

SET FENCE WALL BE INSPECTED FOR DEPTH OF SEDIMENT, TEARS, TO SEE IF THE FABRIC IS SECURELY ATTACHED TO THE FENCE POSTS. AND TO SEE THAT THE FENCE POSTS ARE FIRMLY IN THE GROUND.

THE SEDMENT BASINS WILL BE INSPECTED FOR THE DEPTH OF SEDMENT, AND BUILT UP SEDMENT WAL BE REMOV WARRY IT REACHES TO PERCENT OF THE DESIGN CAPACITY OR AT THE END OF THE JOB, WHICHEVER COMES FIRST.

OWERSION DIKESISWALES WILL BE INSPECTED AND ANY BREACHES PROMPTLY REPAIRED

THE REPORTS WAS BE EXEPT ON SITE DURING CONSTRUCTION MAD AWARABLE UPON RECURST TO THE OWNER, BUGNES OF MAY FEBRUAL STATE OR LOCAL AGENCY APPROXING SEQUENTI AND FROGEN PLANS, OR STOM WATER MANAGED PLANS. THE REPORTS SHALL BE SHOWN AD REPORTS FOR THE STOM WATER REQUITION REPORTS FOR ALL FLANT AND REPORTS MAD A PROXING A PROVINCE OF THE STOM WATER REQUITION REPORTS FOR ALL FLANT THESE YEARS FROM THE DATE THAT THE STIFL STATE PROVINCE OF THE MAD A PROXING THE MOTER OF TERMINATION IS SUBJECTED THE REPORTS SHALL BERNING WAY RECORDED TO ONLOCOMPLANCE.

THE SITE SUPERINTENDENT WILL SELECT UP TO THREE INDIVIDUALS WHO WILL BE RESPONSIBLE FOR INSPECTIONS, MAINTENANCE AND REPAIR ACTIVITIES, AND FALING OUT THE INSPECTION AND MAINTENANCE REPORT.

PERSONNEL SELECTED FOR INSPECTION AND MAINTENANCE RESPONSIBILITIES WILL RECEIVE TRAINING FROM THE SITE SUPERINTENDENT. THEY WALL BE TRAINED IN ALL THE INSPECTION AND MAINTENANCE PRACTICES NECESSARY FOR VESEBOAD DATE EXPONSIVE AND SECONSIST AND OLDER OF A COMMITTEN OF A COMMIT

T IS EXPECTED THAT THE FOLLOWING NON-STORM WATER DISCHARGES WILL OCCUR FROM THE SITE DURING THE CONSTRUCTION PERIOD

WATER FROM WATER (INE FLUSHING.

PAVEMENT WASH WATERS MAHERE NO SPILLS OF LEAKS OF TOXIC OF HAZARDOUS MATERIALS HAVE OCCU

UNICONTAMBIATED GROUNDMATER (FROM DEMATERING EXCAVATION).

ION-SYGMM WIATER DISCHARGES WALL BE DIRECTED TO THE SEDIMENT BASIN PRIOR TO DESCHARGE. ALL SUC HARGES SHALL MEET STATE WATER CUALITY STANDARDS AND ALL NECESSARY PERMITS SHALL BE OBTAINED.

POLLUTION PREVENTION PLAN CERTIFICATION

MATTHEWH, LAHTE P.E. PROFESSIONAL ENGINEER GULFSTREAM DESIGN GROUP, LLC

CONTRACTOR'S CERTIFICATION

LIST THE 24 HOUR CONTACT NUMBER AND PERSON(S) BELOW

	1
	1

SPILL PREVENTION

MATERIAL MANAGEMENT PRACTICES:

AN EFFORT WILL BE MADE TO STORE ONLY ENOUGH PRODUCT REQUIRED TO DO THE JOB

ALL MATERIALS STORED ONSITE WALL BE STORED IN A HEAT, ORDERLY MANINER IN THEIR APPROISE POSSIBLE LINDER A ROOF OR OTHER ENCYOSURE.

PRODUCTS WILL BE KEPT IN THEIR ORIGINAL CONTAINERS WITH THE ORIGINAL MANUFACTURER'S LABEL SUBSTANCES WILL NOT BE MUSED WITH ONE ANOTHER UNLESS BECOMMENDED BY THE MANUENCINGER

WHENEVER POSSIBLE ALL OF A PRODUCT WILL BE USED UP BEFORE DISPOSING OF THE CONTAINER. MANUFACTURER'S RECOMMENDATIONS FOR PROPER USE AND DISPOSAL WILL BE FOLLOWED.

THE SITE SUPERINTENDENT WILL INSPECT DAILY TO ENSURE MATERIALS CHISITE RECEIVE PROPER USE AND DISPOSAL.

HESE PRACTICES ARE USED TO REDUCE THE RISKS ASSOCIATED WITH HAZARDOUS MATERIALS, PRODUCTS WILL BE KEPT IN ORIGINAL CONTAINERS UNLESS THEY ARE NOT RESEALABLE.

RODUCT SPECIFIC PRACTICES:

HE FOLLOWING PRODUCT SPECIFIC PRACTICES WILL BE FOLLOWED ONSITE

ETROLEUM PRODUCTS:

AL CHIEF VERGLEE MALLE MONITORED FOR LEAKS AND RECEIVE REGULAR PREVENTATIVE MANTIDIANCE
THE CHANCE OF LEAKAGE, PETROLEUM PRODUCTS WALLE BY STORED IN TENHTLY STALED CONTINUES WHICH
CLEANY L'ABELLD. MY ASHALT SUBSTANCES USED CHIEFE WILL BE APPLIED ACCORDING TO THE MANUFA
RECOMMENDATIONS.

POST (OPTIONS 2's4" OR 2 1/2" MN. DM. WOOD STEEL 1.33LBJFT, MN.)

ONCRETE TRUCKS: CONCRETE TRUCKS SHALL BE ALLOWED TO WASH OUT OR DISCHARGE SURPLUS CONCRETE OR DRUM WASH WATER ONLY AT DESCHARGE POINT PROMOTO. NO OFFSITE DISCHARGE WALL BE PERMITTED. SHILL CONTROL BRACTICES:

IN ADDITION TO GOOD HOUSEKEEPING AND MATERIAL MANAGEMENT PRACTICES DISCUSSED IN THE PREVIOUS SEC THIS PLAN. THE FOLLOWING PRACTICES WILL BE FOLLOWED FOR SMILL PREVENTION AND CLEANUP

MANUFACTURER'S RECOMMENDED METHODS FOR SPILL CLEANUP WILL BE CLEARLY POSTED ON SITE AND SITE PERSONNEL WALL BE MADE AWARE OF THE PROCEDURES AND THE LOCATION OF THE INFORMATION AND CLEANUP SUPPLIES.

THE SPILL AREA WALL SE KEPT WELL VENTRATED AND PERSONNEL WILL WEAR APPROPRIATE PROTECTIVE CLOTHING TO PREVENT MUNITY FROM CONTACT WITH A HAZARDOUS SUBSTANCE.

SPRIL OF TOXIC OR HAZARDOUS MATERIAL WALL BE REPORTED TO THE APPROPRIATE STATE OR LOCAL GOVERNMENT OF THE SPRIL.

SECTION

THE SPILL PREVENTION PLAN WILL BE ADJUSTED TO INCLUDE MEASURES TO PREVENT THIS TYPE OF SPILL FROM REOCCUP AND HOW TO CLEAN UP THE SPILL IF THERE IS ANOTHER ONE. A DESCRIPTION OF THE SPILL, WHAT CAUSED IT, AND THE CLEANUP MEASURES WILL ASO BE RECLUDED. THE SITE SUPERATEMENT RESPONSED FOR THE DAYLO AN SITE OF PRATTON A WALL BE THE SPILL PREVENTION AND CLEANUP COORDINATION. HIGHLAND AND CLEANUP COORDINATION. HIGHLAND AND CLEANUP COORDINATION. HIGHLAND AND CLEANUP TRANSING, THE REPORTION AND CLEANUP TRANSING, THESE ROMBOULDS WILL HOLD HE CONSTRUCTIONS HE FOR A PROPERTY OF THE ROMBOULD AND LICENT HE CONSTRUCTION AND CLEANUP. THE MANES OF RESPONSED SPILL PERSONNEL WILL BE POSTED IN THE MATERIAL STORAGE, MORE PAPILLARIE, AN THE OFFICE TRANSIC HOUSET.

TYPE MISET FENCE DETAIL N.T.S.

SYNTHETIC BALE DROP INLET SEDMENT FILTER


CHOPE WEOMER

E-TELEVISION FOR E ME


SILT FENCE CONSTRUCTION

SECOMENT BARRIER

TELLETE ADECIANDA 4 A REMOLESCIO MONO PERSONAP



CATCH BASIN SEDIMENT PROTECTION DETAIL N.T.S.



MODES

INSTALLATION TO BE COMPLETED IN ACCOMMENCE WITH WANGFACTURER'S SPECIFICATIONS.

3. SECURE ROLLED RECORD CONTROL PRODUCT OF GROWN OF LOCAL ROLLED RECORD CONTROL PRODUCT OF SECURE AND DESPOSE OF SECURE AND DESPOSE OF SECURE AND DESPOSE OF SECURE RECORD REC) DEBRIS. TER: 20 LONG WATTLE ROLLS FOR STANDARD CIRCULAR DRAMAGE STRUCTURES, LL ARQUING THE STRUCTURE AND JOIN THE ENDS TOGETHER WITH HOG RINGS OR WARE, AND GEN WEDGES TO HOLD DOWN WATTLE ROLLS.

ROLLED EROSION AND SEDIMENTATION CONTROL PRODUCTS



106 ECE - LEE P DISSORTE STEEP BY COOK - LEED OF MACED ON THE STITTE MAKE STANK AND OF STANK GENERAL WARE - LEE OFFRET WERF MONEY ON DIVERTING TO MISCORD TOUCH IN MALE SHOULD BE FRED KINDS THE THOMAS I. IT FERSON IN PRACTICE I.

= 1111111111


Ш \mathbf{S} PHA! \mathbf{x} ENGINEERING PLAN ~ PA BEACH I SWPPF JOHNS COUNTY. SALLEMI








HECKED BY


* 30

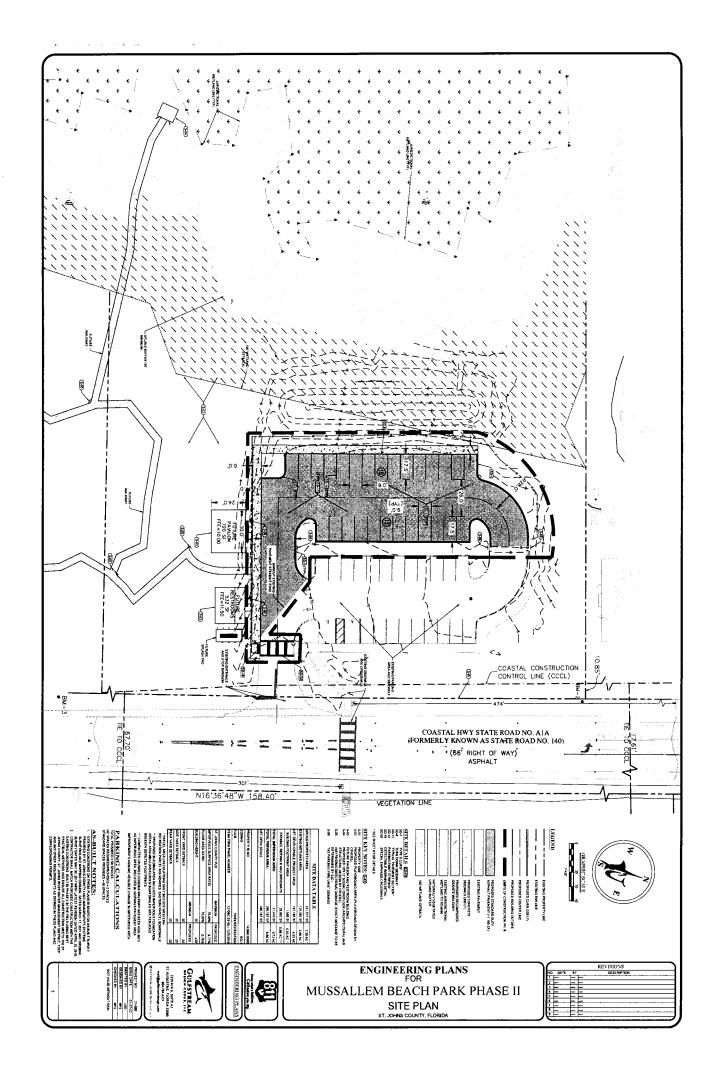

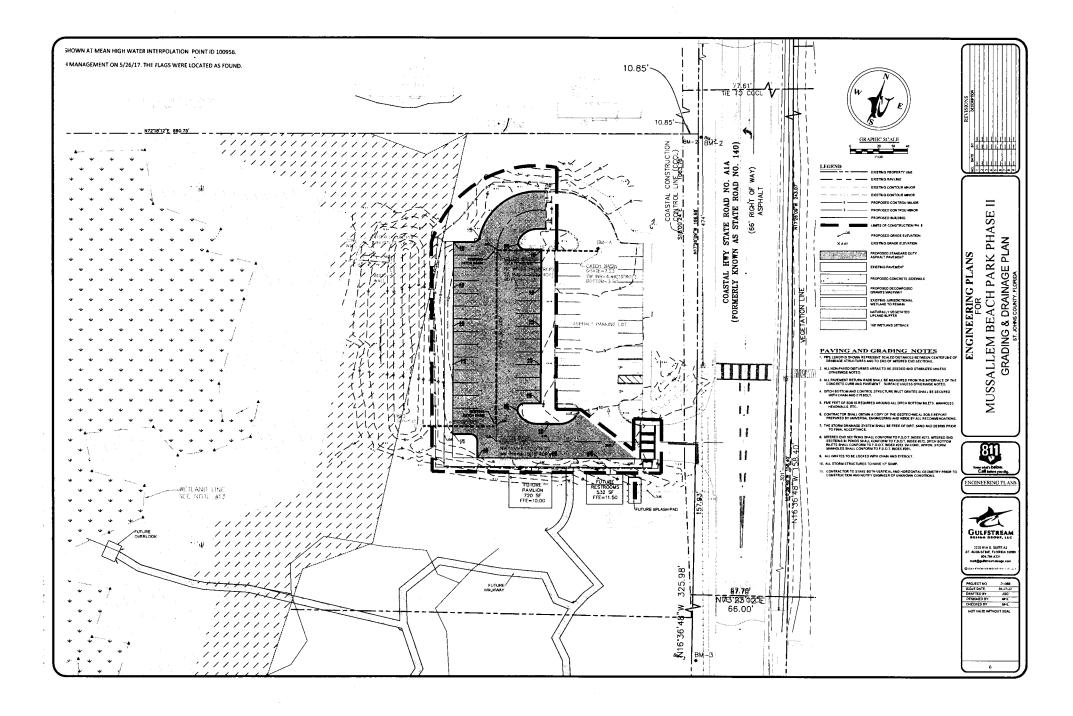

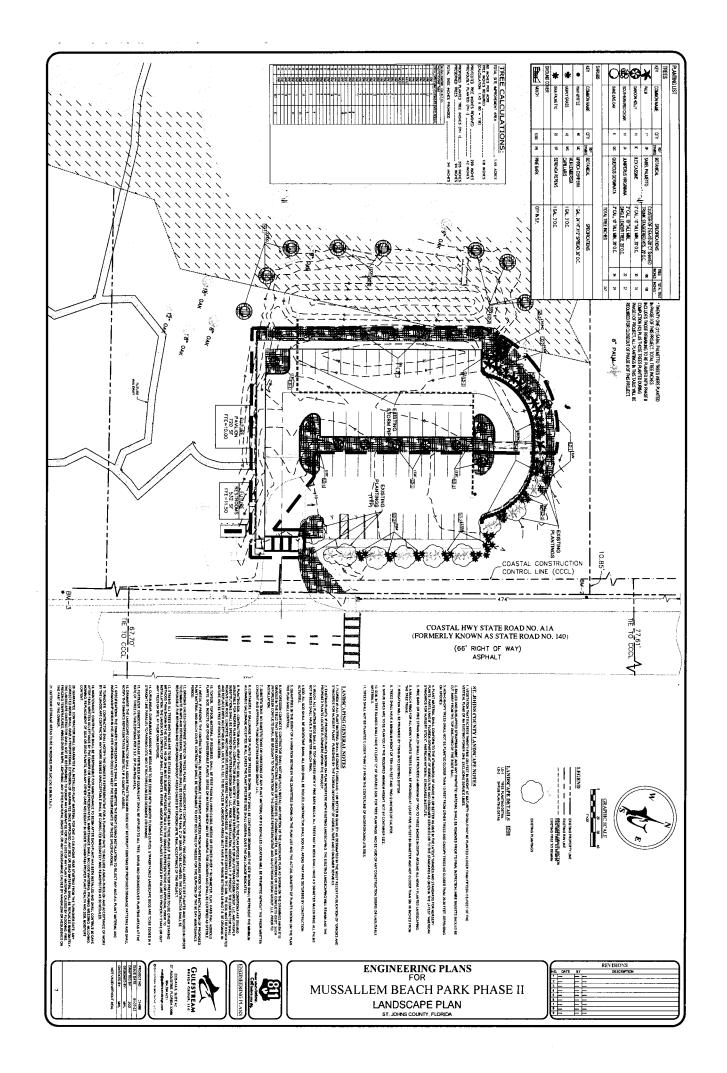

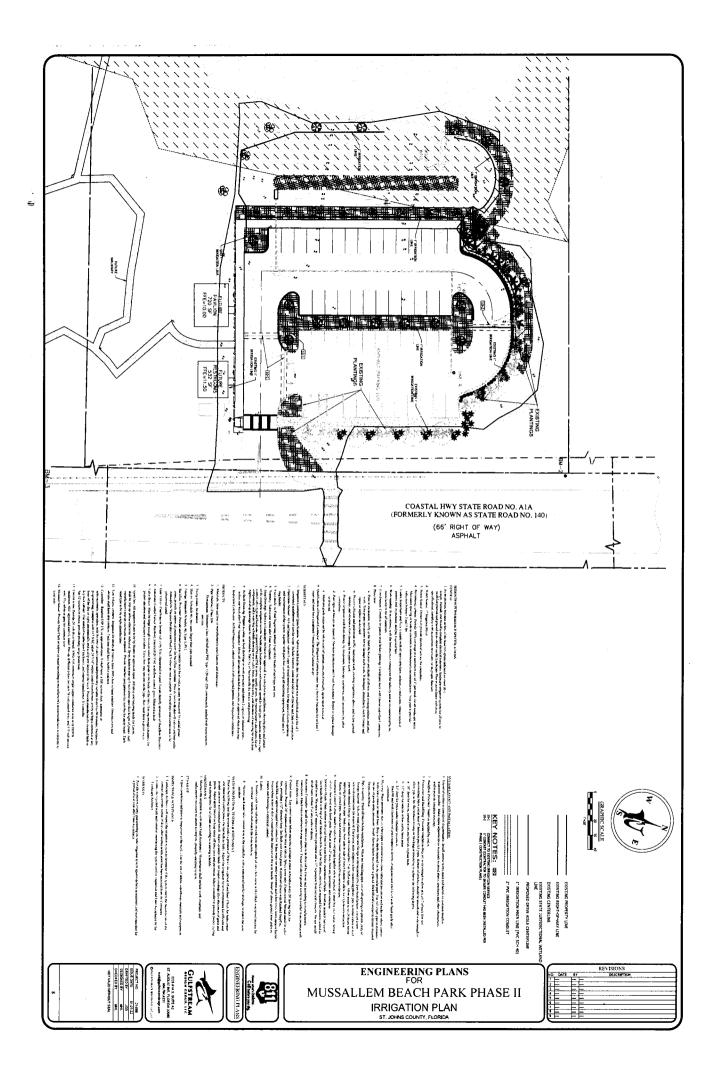

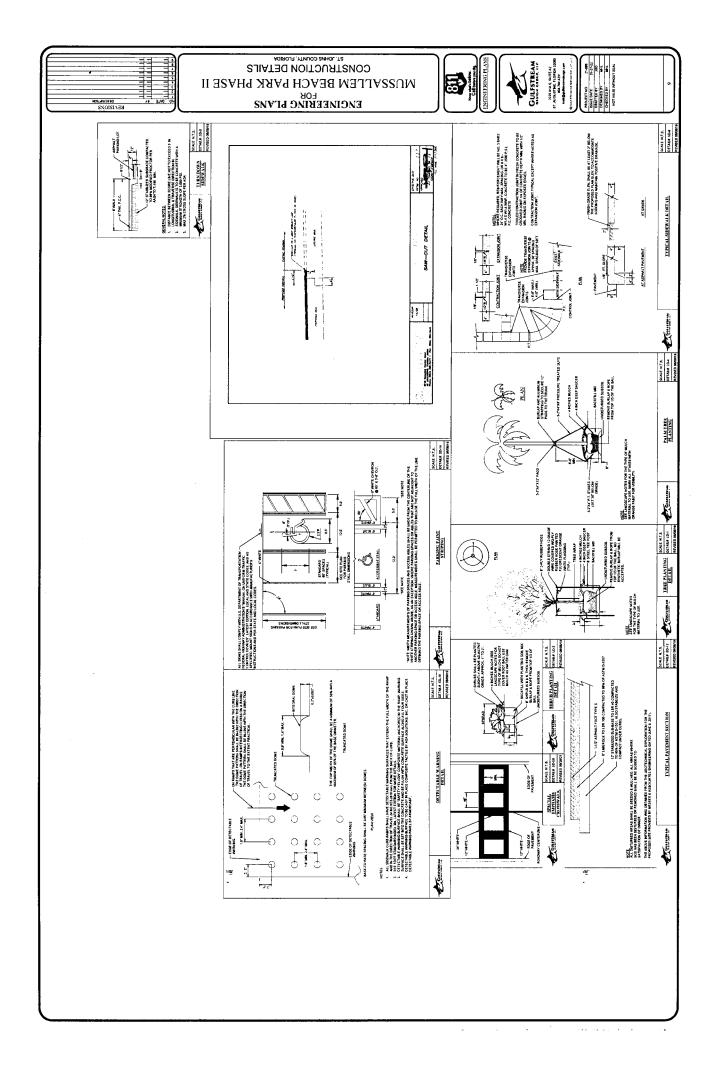

en de la companya de la co



CONTINUING CONSTRUCTION CONTRACT AGREEMENT BETWEEN COUNTY AND CONTRACTOR

(2012 EDITION)

MASTER CONTRACT #: 18-MCC-THO-09215

ARTICLE I – THE CONTRACT AND THE CONTRACT DOCUMENTS

- 1.1 The Contract and Contract Documents
- 1.1.1 The Contract between the County and the Contractor, of which this Agreement is a part, shall consist of the Contract Documents.
- 1.1.2 The Contract Documents shall consist of: (1) this Agreement together with all exhibits, attachments, and duly executed amendments; (2) all RFQ No: 18-05 documents together with all addenda thereto; (3) all Specifications; (4) all duly executed Amendments, Task Orders, Change Orders and Field Orders issued after the Effective Date of the Contract; and (5) FEMA Public Assistance Program Required Contract Clauses (Exhibit B). Documents not enumerated in this Article are not Contract Documents and do not form part of the Contract.
- 1.2 Contract Term and Extension
- 1.2.1 Unless terminated or extended in accordance with other provisions contained herein, the initial term of the Contract shall begin on the date of signature by the County ("Effective Date"), and shall remain in effect for a period of three (3) calendar years.
- 1.2.2 The term of the Contract may be renewed for up to one (1) additional two (2) year period, contingent upon satisfactory performance by the Contractor, mutual written agreement by both parties, and the availability of funds. While the Contract may be renewed as provided herein, it is expressly noted that the County is under no obligation to renew or extend the Contract. It is further expressly noted that the option of renewing the Contract is exercisable only by the County, and only upon the County's determination that the Contractor has satisfactorily performed under the terms of the Contract. The County reserves the right to further extend the Contract, as necessary, to complete any ongoing projects, or as best serves the needs of the County.
- 1.3 Entire Agreement
- 1.3.1 The Contract, together with the Contractor's Public Construction Bond(s) (as applicable), and Certificates of Insurance constitutes the entire agreement between the County and the Contractor with reference to RFP No: 18-22; Utility Rehabilitation/Construction Services. Specifically, but without limitation, the Contract supersedes any RFP Document not listed among the Contract Documents described herein and all prior written and/or oral communications, representations and negotiations, if any, between County and Contractor.
- 1.4 No Privity with Others
- 1.4.1 Nothing contained in the Contract shall create, or be interpreted to create privity or any other contractual agreement between County and any person or entity other than the Contractor.
- 1.5 Intent and Interpretation
- 1.5.1 The intent of the Contract is to require complete, correct and timely execution of the Work. Any work that may be required, implied, or inferred by the Contract Documents, or any one or more of them, as necessary to produce the intended result shall be provided by the Contractor for the Project Price as provided by Task Order.
- 1.5.2 The Contract is intended to be an integral whole and shall be interpreted as internally consistent. What is required by any one Contract Document shall be considered as required by the Contract.

- 1.5.3 When a word, term or phrase is used in the Contract, it shall be interpreted or construed, first, as defined herein; second, if not defined, according to its generally accepted meaning in the construction industry; and third, if there is no generally accepted meaning in the construction industry, according to its common and customary usage.
- 1.5.4 The words "include," "includes" or "including," as used in the Contract, shall be deemed to be followed by the phrase "without limitation."
- 1.5.5 The specification herein of any act, failure, refusal, omission, event, occurrence, or condition as constituting a material breach of the Contract shall not imply that any other, non-specified act, failure, refusal, omission, event, occurrence, or condition shall be deemed not to constitute a material breach of the Contract.
- 1.5.6 Words or terms used as nouns in the Contract shall be inclusive of their singular and plural forms, unless the context of their usage clearly requires a contrary meaning.
- 1.5.7 The headings, titles and captions contained herein are inserted for convenience only and in no way are intended to interpret, define, or limit the scope, extent, or intent of the Contract or any provision thereof.
- 1.5.8 The Contractor shall have a continuing duty to read, carefully study and compare each of the Contract Documents, the Shop Drawings and the Product Data and shall give written notice to the County of any inconsistency, ambiguity, error or omission which the Contractor may discover with respect to these documents before proceeding with the affected Work. The issuance or the express or implied approval by the County of the Contract Documents, Shop Drawings, or Product Data shall not relieve Contractor of the continuing duty set forth in this paragraph. The County has requested that the Project Manager only oversee preparation of documents for the Work, including the Drawings and Specifications for the Work, which are accurate, adequate, consistent, coordinated, and sufficient for construction. HOWEVER, THE COUNTY MAKES NO REPRESENTATION OR WARRANTY OF ANY NATURE WHATSOEVER TO THE CONTRACTOR CONCERNING SUCH DOCUMENTS. By the execution hereof, the Contractor acknowledges and represents that it has received, reviewed and carefully examined such documents, has found them to be complete, accurate, adequate, consistent, coordinated and sufficient for construction. The Contractor further acknowledges that it has not, does not, and shall not rely upon any representation or warranties by the County concerning such documents as no such representation or warranties have been or are hereby made.
- 1.5.9 As between numbers and scaled measurements on the Drawings and in the Design, the numbers shall govern; as between larger scale and smaller scale drawings, the larger scale shall govern.
- 1.5.10 Neither the organization of any of the Contract Documents into divisions, sections, paragraphs, articles, (or other categories), nor the organization or arrangement of the Design, shall control the Contractor in dividing the Work or in establishing the extent or Scope of Work to be performed by Subcontractors.
- 1.6 Ownership of Contract Documents
- 1.6.1 The Contract Documents, and each of them, shall remain the property of the County. The Contractor shall have the right to keep one record set of the Contract Documents upon completion of the Work; provided, however, that in no event shall the Contractor use, or permit to be used, any or all of such Contract Documents on other projects without County's prior written authorization.

ARTICLE II - THE WORK

- 2.1 The Contractor shall perform all of the Work required, implied, or reasonably inferable from the Contract.
- The term "Work" shall mean whatever is done by or required of the Contractor to perform and complete its duties under the Contract, including the following: construction of the whole or a designated part of a project as set forth each Task Order; furnishing of any required Surety Bonds and insurance; and the provision or furnishing of labor, supervision, services, materials, supplies, equipment, fixtures, appliances, facilities, tools, transportation, storage, power, permits and licenses required of the Contractor, fuel, heat, light, cooling and all other utilities as required by the Contract. The Work to be performed by the Contractor on each project shall be specifically described in, and authorized by Task Order issued by the County. Each Task Order issued by the County under the Contract shall further specify the amount of time permitted for completion of the Work ("Project Time") and the amount to be paid as compensation for completion of Work ("Project Price").

ARTICLE III - PROJECT TIME

3.1 Time and Liquidated Damages

- 3.1.1 The Contractor shall commence the Work for each project upon receipt of a Notice to Proceed, or as stated on the fully executed Task Order, issued by the County, and shall reach Substantial and Final Completion of all Work as specified by Task Order.
 - For each project, the number of calendar days from the date on which the Work is permitted to proceed through the date set forth in the Task Order for Final Completion shall constitute the "Project Time."
- 3.1.2 For each project, the Contractor shall pay the County the sum of nine hundred fifty eight dollars (\$958.00), based on the current FDOT Table for Liquidated Damages, for each and every calendar day of unexcused delay in achieving Substantial Completion of the Work beyond the date specified by Task Order for Substantial Completion of the Work. Any sums due and payable hereunder by the Contractor shall be payable, not as a penalty, but as liquidated damages representing an estimate of delay damages likely to be sustained by the County, estimated at or before the time of issuing the Task Order. When the County reasonably believes that Substantial Completion shall be inexcusably delayed the County shall be entitled, but not required, to withhold from any amounts otherwise due the Contractor an amount then believed by the County to be adequate to recover liquidated damages applicable to such delays. If and when the Contractor overcomes the delay in achieving Substantial Completion, or any part thereof, for which the County has withheld payment, the County shall promptly release to the Contractor those funds withheld, but no longer applicable, as liquidated damages.
- 3.2 Substantial Completion
- 3.2.1 "Substantial Completion" shall mean that stage in the progression of the Work when the Work is sufficiently complete as provided by Task Order that the County can enjoy beneficial use or occupancy of the Work and can utilize the Work for its intended purpose.
- 3.3 Time is of the Essence
- 3.3.1 All limitations of time set forth in the Contract Documents are of the essence of this Contract.

ARTICLE IV - PROJECT PRICE

- 4.1 The Project Price
- 4.1.1 The County shall pay, and the Contractor shall accept, as full and complete payment for all Work required by each Task Order, the amount specified and authorized by each Task Order upon satisfactory completion of the Work for each project. The amount set forth in each Task Order shall not exceed two hundred thousand dollars (\$200,000), without prior written authorization by the Board of County Commissioners.

ARTICLE V – PAYMENT OF THE PROJECT PRICE

- 5.1 Schedule of Values
- 5.1.1 Upon request by the County, the Contractor shall submit a Schedule of Values allocating the Project Price to the various portions of the Work included in the Task Order for each project. The Contractor's Schedule of Values shall be prepared in such form, with such detail, and supported by such data as the County may require, in order to substantiate its accuracy. The Contractor shall not imbalance its Schedule of Values, nor artificially inflate any element thereof. The violation of this provision by the Contractor shall constitute a material breach of the Contract. The Schedule of Values shall be used only as a basis for the Contractor's Requests for Payment and shall only constitute such basis after it has been agreed upon in writing by the County.
- 5.2 Payment Procedure
- 5.2.1 The County shall pay the Project Price to the Contractor as provided below.
- Progress Payments Based upon the Contractor's Requests for Payment submitted to the County and upon Certificates for Payment subsequently issued to the County by the Project Manager, the County shall make progress payments to the Contractor on account of the Project Price. Retainage in the amount of ten percent (10%) will be withheld=from each progress payment until County has issued Final Acceptance of the Work. Progress payments for each project shall be provided by Task Order.
- 5.2.3 On or before the fifteenth (15th) day of each month after commencement of the Work for each project, the Contractor shall submit an Application for Payment for the period ending the thirtieth (30th) day of the previous month to the Project Manager in such form and manner, and with such supporting data and content, as the Project Manager may require. Therein, the Contractor may request payment for ninety percent (90%) of that portion of

the Project Price properly incorporated in the Work less the total amount of previous payments received from the County.

Such Application for Payment shall be signed by the Contractor and shall constitute the Contractor's representation that the Work has progressed to the level for which payment is requested, that the Work has been properly installed or performed in full accordance with the Contract Documents, and that the Contractor knows of no reason why payment should not be made as requested. Thereafter, the Project Manager (and Engineer if applicable) shall review the Application for Payment and may also review the Work at the project site or elsewhere to determine whether the quantity and quality of the Work is as represented in the Application for Payment and is as required by the Contract Documents. The Project Manager shall determine and certify to the County the amount properly owing to the Contractor. The County shall make partial payments on accounts of the Project Price within thirty (30) days following the Project Manager's receipt of each Application for Payment. The amount of each partial payment shall be the amount certified for payment by the Project Manager less such amounts, if any, otherwise owing by the Contractor to the County or which the County shall have the right to withhold as authorized by the Contract. The Project Manager's certification of the Contractor's Application for Payment shall not preclude the County from the exercise of any of its rights as set forth in Paragraph 5.3 herein below.

- 5.2.4 The Contractor warrants that title to all Work covered by an Application shall pass to the County no later than time of payment. The Contractor further warrants that upon submittal of an Application for Payment, all Work for which payments have been received from the County shall be free and clear of liens, claims, security interest or other encumbrances in favor of the Contractor or any other person or entity whatsoever.
- 5.2.5 The Contractor shall promptly pay each Subcontractor out of the amount paid to the Contractor on account of such Subcontractor's Work, the amount to which such Subcontractor is entitled. In the event the County becomes informed that the Contractor has not paid a Subcontractor as herein provided, the County shall have the right, but not the duty or obligation, to issue future checks in payment to the Contractor of amounts otherwise due hereunder naming the Contractor and such Subcontractor as joint payees. Such joint check procedure, if employed by the County, shall create no rights in favor of any person or entity beyond the right of the named payees to payment of the check and shall not be deemed to commit the County to repeat the procedure in the future.
- 5.2.6 No progress payment, nor any use or occupancy of any project by the County, shall be interpreted to constitute an acceptance of any Work not in strict accordance with the Contract Documents.
- 5.3 Withheld Payment
- 5.3.1 County may decline to make payment, may withhold funds and, if necessary, may demand the return of some or all of the amounts previously paid to the Contractor, to protect the County from loss because of:
 - (1) defective Work not remedied by the Contractor and, in the opinion of the County, not likely to be remedied by the Contractor;
 - (2) claims of third parties against the County or the County's property;
 - (3) failure by the Contractor to pay Subcontractors or others in a prompt and proper fashion;
 - (4) evidence that the balance of the Work cannot be completed in accordance with the Task Order for unpaid balance of the Project Price;
 - (5) evidence that the Work shall not be completed in the time required for Substantial or Final Completion of the Work;
 - (6) repeated failure (two or more times) to carry out the Work as specified by Task Order;
 - (7) damage to the County or a third party to whom the County is, or may be, liable;
 - (8) failure by the Contractor to timely pay, any, and all, applicable taxes, fees (including permit or use fees), costs, or expenses, associated with the Project.

In the event that the County makes written demand upon the Contractor for amounts previously paid by the County as contemplated in this Subparagraph 5.3.1, the Contractor shall promptly comply with such demand.

- 5.4 Unexcused Failure to Pay
- 5.4.1 If within ten (10) days after the date established by Task Order for payment to the Contractor by the County, the County, without cause or basis hereunder, fails to pay the Contractor any amount due and payable to the Contractor, then the Contractor may after seven (7) additional days, written notice to the County and the Project Manager, and without prejudice to any other available rights or remedies it may have, stop the Work until

payment of those amounts due from the County have been received. Any payment not made within ten (10) days after the date due shall bear interest at the rate of twelve percent (12%) per annum.

5.5 Substantial Completion

5.5.1 When the Contractor believes the Work required by Task Order for each project is Substantially Complete, the Contractor shall submit to the Project Manager a list of items to be completed or corrected. When the Project Manager on the basis of an inspection determines that the Work is in fact Substantially Complete, the Project Manager shall prepare a Certificate of Substantial Completion which shall establish the date of Substantial Completion of the Work, shall state the responsibilities of the County and the Contractor for project security, maintenance, heat, utilities, damage to the Work, and insurance, and shall fix the time within which the Contractor shall complete the items listed therein. Guarantees required by the Contract Documents shall commence on the date of Substantial Completion of the Work. The Certificate of Substantial Completion shall be submitted to the County and the Contractor for their written acceptance of the responsibilities assigned to them in such certificate.

Until Final Completion and acceptance of the Work by the County, the County shall pay the Contractor an amount equal to ninety percent (90%) of the Project Price. Ten Percent (10%) of the Project Price shall be retained until Final Completion, acceptance of the Work by the County and Final Payment to the Contractor.

- 5.6 Final Completion and Final Payment
- 5.6.1 When all the Work required by Task Order for each project is finally complete and the Contractor is ready for a Final Inspection, it shall notify the County and the Project Manager thereof in writing. Thereupon, the Project Manager shall make Final Inspection of the Work and, if the Work is complete in full accordance with the project Task Order and the Task Order has been fully performed, the Project Manager shall promptly issue a Final Certificate for Payment for the project and if required to repeat its Final Inspection of the Work, the Contractor shall bear the cost of such repetition of the Work, the Contractor shall bear the cost of such repeat Final Inspection(s) which cost may be deducted by the County and all other Authorities having jurisdiction under Florida Laws or regulations.
- 5.6.1.1 If the Contractor fails to achieve Final Completion within the time fixed in the Certificate of Substantial Completion, the Contractor shall pay the County liquidated damages at the sum shown in Paragraph 3.1.2. per day for each and every calendar day of unexcused delay in achieving Final Completion beyond the date set forth for Final Completion of the Work. Any sums due and payable hereunder by the Contractor shall be payable, not as penalty, but as liquidated damages representing an estimate of delay damages likely to be sustained by the County, estimated at or before the time of issuance of the Task Order. When the County reasonably believes that Final Completion shall be inexcusably delayed, the County shall be entitled, but not required, to withhold from any amounts otherwise due the Contractor an amount then believed by the County to be adequate to recover liquidated damages applicable to such delays. If and when the Contractor overcomes the delay in achieving Final Completion, or any part thereof, for which the County has withheld payment, the County shall promptly release to the Contractor those funds withheld, but no longer applicable, as liquidated damages.
- 5.6.2 The Contractor shall not be entitled to Final Payment unless and until it submits to the Project Manager its affidavit that all payrolls, invoices for materials and equipment, and other liabilities connected with the Work on each project for which the County, or the County's property might be responsible, have been fully paid or otherwise satisfied; releases and waivers of claims and lien from all Subcontractors of the Contractor and of any and all other parties required by the County; consent of Surety, if any, to Final Payment. If any third party fails or refuses to provide a release of claim or waiver of a lien as required by County the Contractor shall furnish a bond satisfactory to the County to discharge any such lien or indemnify the County from liability.
- 5.6.3 The County shall make Final Payment of all sums, due the Contractor within thirty (30) days of the Project Manager's execution of a Final Certificate for Payment.
- 5.6.4. Acceptance of Final Payment shall constitute a waiver of all claims against the County by the Contractor except for those claims previously made in writing against the County by the Contractor, pending at the time of Final Payment, and identified in writing by the Contractor as unsettled at the time of its request for Final Payment.

ARTICLE VI - THE COUNTY

6.1 Information, Services and Things Required from County

- 6.1.1 The County shall furnish to the Contractor, at the time of issuing each Task Order, any and all written and tangible material in its possession concerning conditions below ground at the site of the project. Such written and tangible material is furnished to the Contractor only in order to make complete disclosure of such material and for no other purpose. By furnishing such material, the County does not represent, warrant, or guarantee its accuracy either in whole, in part, implicitly, or at all, and shall have no liability therefore. The County shall also furnish surveys, legal limitations and utility locations (if known), and a legal description of the project site. Copies may be provided instead of originals.
- 6.1.2 Excluding permits and fees normally the responsibility of the Contractor, the County shall obtain all approvals, easements, and the like required for construction.
- 6.1.3 The County shall furnish the Contractor, free of charge, three (3) copies of the Contract Documents for execution of the Work. The Contractor shall be charged, and shall pay the actual cost of reproduction per additional set of Contract Documents which it may require.
- 6.2 Right to Stop Work
- 6.2.1 If the Contractor persistently fails or refuses to perform Work in accordance with any Task Order, the County may order the Contractor to stop the Work, or any described portion thereof, until the cause for stoppage has been corrected, no longer exists, or the County orders that Work be resumed. In such event, the Contractor shall immediately obey such order. Further, the Contractor shall not be paid for, nor make any claim for payment for, any Work done in connection with the Project, during the period of Work stoppage.
- 6.3 County's Right to Perform Work
- 6.3.1 If the Contractor's Work is stopped by the County under Paragraph 6.2, and the Contractor fails within seven (7) days of such stoppage to provide adequate assurance to the County that the cause of such stoppage shall be eliminated or corrected, the County may, without prejudice to any other rights or remedies the County may have against the Contractor, proceed to carry out the subject Work.
 - In such a situation, an appropriate Change Order shall be issued by the County deducting from the Project Price the cost of correcting the subject deficiencies, and compensation for the County's additional services and expenses necessitated thereby, if any. If the unpaid portion of the Project Price is insufficient to cover the amount due the County, the Contractor shall pay the difference to the County.

ARTICLE VII – THE CONTRACTOR

- 7.1 The Contractor is again reminded of its continuing duty set forth in Subparagraph 1.5.7. The Contractor shall perform no part of the Work at any time without adequate Contract Documents or, as appropriate, approved Shop Drawings, Product Data or Samples for such portion of the Work. If the Contractor performs any of the Work where Contractor knows or should know such Work involves a recognized error, inconsistency or omission in the Contract Documents without such notice to the Project Manager and the County, the Contractor shall bear responsibility for such performance and shall bear the cost of correction.
- 7.2 The Contractor shall perform the Work for each project strictly in accordance with the Contract Documents.
- 7.3 The Contractor shall supervise and direct the Work for each project using the Contractor's best skill, effort and attention. The Contractor shall be responsible to the County for any and all acts or omissions of the Contractor, its employees and other engaged in the Work on behalf of the Contractor.
- 7.4. Warranty
- 7.4.1 The Contractor warrants to the County that all labor furnished to progress the Work under the Contract shall be competent to perform the tasks undertaken, that the product of such labor shall meet or exceed acceptable industry standards, that materials and equipment furnished shall be of good quality, free from faults and defects and in strict conformance with the Contract. This warranty shall survive termination of the Contract and shall not be affected by Final Payment for any project hereunder. All Work not conforming to these requirements may be considered defective.
- 7.5 Contractor shall obtain and pay for all permits, fees and licenses necessary and ordinary for the Work. The Contractor shall comply with all lawful requirements applicable to the Work and shall give and maintain any and all notices required by applicable law pertaining to the Work.

- 7.6 Supervision
- 7.6.1 The Contractor shall employ and maintain at each project site only competent supervisory personnel. Absent written instruction from the Contractor to the contrary, the superintendent shall be deemed the Contractor's authorized representative at the site and shall be authorized to receive and accept any and all communications from the County or Assignees.
- 7.6.2 Key supervisory personnel assigned by the Contractor to projects under the Contract are as follows:

Name	Function
DALMA KENT HITER	SUPERVISION
JEFFREY HITER	SUPERVISION
BEN ROBERTS	SUPERVISION
NOLAN HORN	SUPERVISION
CHRISTOPHER PAUL NIFLIS	SUPERVISION
MELVIN D. DURDEN	Supervision - Roofing

So long as the individuals named above remain actively employed or retained by the Contractor, they shall perform the functions indicated next to their names unless the County agrees to the contrary in writing. In the event one or more individuals not listed above subsequently assume one or more of those functions listed above, the Contractor shall be bound by the provisions of this Subparagraph 7.6.2 as though such individuals have been listed above.

- 7.7 The Contractor, prior to commencing the Work for each project, shall submit to the Project Manager for his information, the Contractor's schedule for completing the Work. The Contractor's schedule shall be revised no less frequently than monthly (unless the parties otherwise agree in writing) and shall be revised to reflect conditions encountered from time to time and shall be related to each entire project. Each sum revision shall be furnished to the Project Manager. Failure by the Contractor to strictly comply with the provisions of this Paragraph 7.7 shall constitute a material breach of the Contract.
- 7.8 The Contractor shall continuously maintain at the project site, for the benefit of the Project Manager, one record copy of the Contract and the project Task Order marked to record on a current basis changes, selections and modifications made during construction. Additionally, the Contractor shall maintain at the project site for the Project Manager the approved Product Data, Samples and other similar required submittals. For each project, upon Final Completion of the Work, such record documents shall be delivered to the County.
- 7.9 Product Data and Samples
- 7.9.1 Product Data, Samples and other submittals from the Contractor do not constitute Contract Documents. Their purpose is merely to demonstrate the manner in which the Contractor intends to implement the Work for each project in conformance with the information received from the Contract Documents. All Product Data, Samples and other submittals shall belong to the County and shall be delivered, or returned to County, as applicable, prior to Submittals shall belong to County and shall be delivered, or returned to County, as applicable, prior to Substantial Completion.
- 7.10 Cleaning the Site and the Project
- 7.10.1 The Contractor shall keep each project site reasonably clean during performance of the Work. Upon Final Completion of the Work, the Contractor shall clean the site and the project and remove all waste, together with all of the Contractor's property there from.
- 7.11 Access to Work
- 7.11.1 The County and the Project Manager shall have access to the Work at all times from commencement of the Work through Final Completion. The Contractor shall take whatever steps necessary to provide access when requested.
- 7.12 Indemnity
- 7.12.1 To the fullest extent permitted by law, for each project, the Contractor shall indemnify and hold harmless the County, its officers and employees from, and against, any, and all, administrative/legal/equitable liability, claims, damages, losses and expenses, including attorneys' fees, arising out of or resulting from performance of the Work noted in the Contract Documents, that are referenced and considered a part of the Contract. It is specifically noted that such liability, claims, damages, loss or expense includes any of those referenced instances attributable to

bodily injury, sickness, disease, or death, or to injury to, or destruction of, personal and/or real property, including the loss of use resulting there from or incident to, connected with, associated with or growing out of direct and/or indirect negligent or intentional acts or omissions by the Contractor, a Subcontractor, or anyone directly, or indirectly employed by them, or anyone for whose acts the Contractor or Subcontractor may be liable, regardless of whether or not such liability, claim, damage, loss or expense is caused in part by a party indemnified hereunder.

- 7.12.2 In claims against any person or entity indemnified under this Paragraph 7.12 by an employee of the Contractor, a Subcontractor, any one directly or indirectly employed by them or anyone for whose acts they may be liable, the indemnification obligation under this Paragraph 7.12 shall not be limited by a limitation on amount or type of damages, compensation or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefits acts or other employee benefit acts.
- 7.13 Safety
- 7.13.1 The Contractor shall be responsible for supervising all safety precautions, including initiating and maintaining such programs in connection with performance of the Contract and for adequate maintenance of traffic.
- 7.13.2 The Contractor shall designate a member of the on-site construction team for each Project, whose duty shall be the prevention of accidents. Unless notified otherwise in writing by the Contractor to the County (and the Engineer if applicable), this person shall be the Contractor's Superintendent.

ARTICLE VIII - CONTRACT ADMINISTRATION

- 8.1 Project Manager
- 8.1.1 The Project Manager, unless otherwise directed by the County shall perform those duties and discharge those responsibilities allocated to the Project Manager as set forth in the Contract. The Project Manager shall be the County's representative for the entire Term of the Contract. The Project Manager shall be authorized to act on behalf of the County only to the extent provided in the Contract.
- 8.1.2 The County and the Contractor shall communicate with each other in the first instance through the Project Manager.
- 8.1.3 The Project Manager shall be the initial interpreter of the requirements of the drawings and specifications and the judge of the performance thereunder by the Contractor. The Project Manager shall render written or graphic interpretations as necessary for the proper execution or progress of the Work with reasonable promptness on request of the Contractor.
- 8.1.4 The Project Manager shall review the Contractor's Applications for Payment and shall certify to the County for payment to the Contractor, those amounts then due to the Contractor as provided in the Contract Documents.
- 8.1.5 The Project Manager shall have authority to reject Work, which is defective or does not conform to the requirements of the Contract Documents. If the Project Manager deems it necessary or advisable, the Project Manager shall have authority to require additional inspection or testing of the Work for compliance with Contract requirements at Contractor's expense.
- 8.1.6 The Project Manager shall review and approve, or take other appropriate action as necessary, concerning the Contractor's submittals including Product Data and Samples. Such review, approval or other action shall be for the sole purpose of determining conformance with the design concept and information given through the Contract Documents.
- 8.1.7 The Project Manager shall prepare Change Orders for processing by the Purchasing Department and may authorize minor changes in the Work by Field Order as provided elsewhere herein.
- 8.1.8 The Project Manager shall, upon written request from the Contractor, conduct inspections to determine the date of Substantial Completion and the date of Final Completion, shall receive and forward to the County for the County's review and records, written warranties and related documents required by the Contract and shall issue a Final Certificate for Payment upon compliance with the requirements of the Contract Documents.
- 8.1.9 The Project Manager's decision in matters relating to visual quality shall be final if consistent with the applicable provisions of the Contract Documents.

- 8.2 Claims by the Contractor
- 8.2.1 All Contractor claims shall be initiated by written notice and claim to the Project Manager. Such written notice and claims must be furnished within seven (7) days after occurrence of the event, or the first appearance of the condition, giving rise to the claim.
- 8.2.2 Pending final resolution of any claim of the Contractor, the Contractor shall diligently proceed with performance of the Work and the County shall continue to make payments to the Contractor in accordance with each Task Order. The resolution of any claim under this Paragraph 8.2 shall be reflected by a Change Order executed by the Project Manager and the Contractor.
- 8.2.3 Claims for Concealed and Unknown Conditions. Should concealed and unknown conditions encountered in the performance of the Work (a) below the surface of the ground or (b) in an existing structure be at variance with the conditions indicated by Task Order, or should unknown conditions of an usual nature differing materially from those ordinarily encountered in the area and generally recognized as inherent in Work of the character provided for in the Task Order, be encountered, wherein the Contract Documents or Standard Construction industry practices have not placed the responsibility of discovering such concealed and unknown conditions upon the Contractor prior to the Contractor submitting his Pricing Proposal for the Work, the Project Price shall be equitably adjusted by Change Order upon the written notice and claim by either party made within seven (7) days after the first observance of the condition. As a condition precedent to the County having any liability to the Contractor for concealed or unknown conditions, the Contractor must give the Project Manager written notice of, and an opportunity to observe, the condition prior to disturbing it. The failure by the Contractor to make the written notice and claim as provided in this Subparagraph shall constitute a waiver by the Contractor of any claim arising out of or relating to such concealed or unknown condition.
- 8.2.4 Claims for Additional Costs. If the Contractor wishes to make a claim for an increase in the Project Price, as a condition precedent to any liability of the County therefore, the Contractor shall give the Project Manager written notice of such claim within seven (7) days after the occurrence of the event, or the first appearance of the condition, giving arise to such claim. Such notice shall be given by the Contractor before proceeding to execute any additional or changed Work. The failure by the Contractor to give such notice prior to executing the Work shall constitute a waiver of any claim for additional compensation.
- 8.2.4.1 In connection with any claim by the Contractor against the County for compensation in excess of the Project Price, any liability of the County for the Contractor's costs shall be strictly limited to direct costs incurred by the Contractor and shall in no event include indirect costs or consequential damages of the Contractor.
 - The County shall not be liable to the Contractor for claims of third parties, including Subcontractors, unless and until liability of the Contractor has been established therefore in a court of competent jurisdiction.
- 8.2.5 Claims for Additional Time. If the Contractor is delayed in progressing any Work which at the time of the delay is then critical or which during the delay becomes critical, as the sole result of any act or neglect to act by the County or someone acting on the County's behalf, or by changes ordered in the Work, unusual delay in transportation, unusually adverse weather conditions not reasonably anticipated, fire or any causes beyond the Contractor's control, then the date for achieving Substantial Completion of the Work shall be extended upon the written notice and claim of the Contractor to the Project Manager, for such reasonable time as the Project Manager may determine.
 - Any notice and claims for an extension of time by the Contractor shall be made not more than seven (7) days after the occurrence of the event or the first appearance of the condition giving the rise to the claim and shall set forth in detail the Contractor's basis for requiring additional time in which to complete the project. In the event the delay to the Contractor is a continuing one, only one notice and claim for additional time shall be necessary. If the Contractor fails to make such claim for an extension of time as provided herein, then such claim shall be waived. This paragraph shall not be deemed to waive any damages for delay that are covered by insurance.
- 8.2.5.1 Delays and Extensions of Time. An extension of Project Time shall not be given due to weather conditions unless such weather conditions are more severe than average and have caused a delay. In requesting an extension of time for weather conditions, Contractor shall present complete records and such requests shall document how weather conditions delayed progress of the Work.

- 8.3 Field Orders
- 8.3.1 For each Project, the Project Manager shall have authority to order minor changes in the Work not involving a change in the Project Price or in Project Time and not inconsistent with the intent of the Contract. Such changes shall be effected by Field Order and shall be binding upon the Contractor. The Contractor shall carry out such Field Orders promptly.

ARTICLE IX - SUBCONTRACTORS

- 9.1 Definition
- 9.1.1 A Subcontractor is an entity, which has a direct Contract with the Contractor to perform a portion of the Work.
- 9.2 Award of Subcontracts
- 9.2.1 Prior to commencing the Work for each project, the Contractor shall furnish the Project Manager, in writing, the names of persons or entities proposed by the Contractor to act as a Subcontractor on the project. The Project Manager shall reply within seven (7) business days to the Contractor, in writing, stating any objections the Project Manager may have to such proposed Subcontractor. The Contractor shall not enter into a Subcontract with a proposed Subcontractor with reference to whom the Project Manager has made a timely objection.
- 9.2.2 All subcontracts shall afford the Contractor rights against the Subcontractor, which correspond to those rights afforded to the County by Subparagraph 12.2.1 below.

ARTICLE X - CHANGES IN THE WORK

- 10.1 Changes Permitted
- 10.1.1 Changes in the Work within the general scope of each Task Order, consisting of additions, deletions, revisions, or any combination thereof, may be ordered without invalidating the Contract by properly executed Change or Field Order.
- 10.1.2 Changes in the Work for each project shall be performed under applicable provisions of the Contract and the Contractor shall proceed promptly with such changes.
- 10.2 Change Order Defined
- 10.2.1 The term "Change Order" shall mean a written order to the Contractor executed by the County Administrator, or authorized designee, issued after execution of the Contract, authorizing and directing a change in the Work or an adjustment in the Project Price or the Project Time, or any combination thereof. Only a duly executed Change Order may change the Scope of Work, Project Price and/or the Project Time.
- 10.3 Changes in the Project Price
- 10.3.1 Any change in the Project Price resulting from a Change Order shall be determined as follows: (a) by mutual agreement between the County and the Contractor as evidenced by (1) the change in the Project Price being set forth in the Change Order, (2) such change in the Project Price, together with any conditions or requirements related thereto, being initialed by both parties and (3) the Contractor's execution of the Change Order, or (b) if no mutual agreement occurs between the County and the Contractor, then, as provided in Subparagraph 10.3.2 below.
- 10.3.2 If no mutual agreement occurs between the County and the Contractor as contemplated in Subparagraph 10.3.1 above, the change in the Project Price, if any, shall than be determined by the Project Manager on the basis of the reasonable expenditures or savings of those performing, deleting or revising the Work attributable to the change, including, in the case of an increase or decrease in the Project Price, a reasonable allowance for direct project site overhead and profit. In such case, the Contractor shall present, in such form and with such content as the County or the Project Manager requires, an itemized accounting of such expenditures or savings shall be limited to the following: reasonable costs of materials, supplies, or equipment including delivery costs, reasonable costs of labor, including social security, old age and unemployment insurance, fringe benefits required by a pre-existing agreement or by custom, and workers' compensation insurance, reasonable costs of premiums for all Bonds and insurance, permit fees, and sales, use or other taxes related to the Work and paid by the Contractor, and reasonable costs of directly attributable to the change. In no event shall any expenditure or savings associated with the Contractor's home office or other non-project site overhead expenses be included in any change in the

- Project Price. Pending final determination of reasonable expenditures or savings to the County, payments on account shall be made to the Contractor on the County's Certificate of Payment.
- 10.3.3 If Unit Prices are provided in a Task Order, and if the quantities contemplated are so changed by proposed Change Order that application of such Unit Prices to the quantities of Work proposed shall cause substantial inequity to the County or to the Contractor, then the applicable Unit Prices shall be equitable adjusted.
- 10.4 Minor Changes
- 10.4.1 The Project Manager shall have authority to order minor changes in the Work for each project not involving a change in the Project Price or an extension of the Project Time and not inconsistent with the intent of the Contract. Such minor changes shall be made by written Field Order, and shall be binding upon the County and the Contractor. The Contractor shall promptly carry out such written Field Orders.
- 10.5 Effect of Executed Change Order
- 10.5.1 For each project, the execution of any Change Order by the Contractor shall constitute conclusive evidence of the Contractor's agreement to the ordered changes in the Work, the Contract Documents as thus amended, the Project Price and the Project Time. The Contractor, by executing a Change Order, waives and forever releases any claim against the County for additional time or compensation for matters relating to or arising out of or resulting from the Work included within or affected by the executed Change Order.
- 10.6 Notice to Surety; Consent
- 10.6.1 The Contractor shall notify and obtain the timely consent and approval of the Contractor's surety with reference to all Change Orders if such notice, consent or approval is required by the Contractor's surety or by law. The Contractor's warranty to the County that the surety has been notified of and consents to, such Change Order and the surety shall be conclusively deemed to have been notified of such Change Order and to have expressly consented thereto.

ARTICLE XI – UNCOVERING AND CORRECTING WORK

- 11.1 Uncovering Work
- 11.1.1 If any of the Work for a project is covered contrary to the Project Manager's request or to any provision of the Contract Documents, it shall, if required by the Project Manager, be uncovered for the Project Manager's inspection and shall be properly replaced at the Contractor's expense without change to the Project Time as provided in the Task Order.
- 11.1.2 If any of the Work for a project is covered in a manner not described in Subparagraph 11.1.1 above, it shall, if required by the by the Project Manager or County, be uncovered for the Project Manager's inspection. If such Work conforms strictly to the Contract Documents, costs of uncovering and proper replacement shall by Change Order be charged to the County. If such Work does not strictly conform to the Contract Documents, the Contractor shall pay the costs of uncovering and proper replacement.
- 11.2 Correcting Work
- 11.2.1 The Contractor shall immediately proceed to correct Work rejected by the Project Manager as defective or failing to conform to the Contract Documents. The Contractor shall pay all costs and expenses associated with correcting such rejected Work, including any additional testing and inspections, and reimbursement to the County for the Project Manager's services and expenses made necessary thereby.
- 11.2.2 For each project, if within one (1) year after Substantial Completion of the Work, any of the Work is found to be defective or not in accordance with the Contract Documents, the Contractor shall correct the Work within seven (7) days at the Contractor's expense upon receipt of written notice from the County. This obligation shall survive Final Payment by the County and termination of the Contract. With respect to Work first performed and completed after Substantial Completion of the project, this one (1) year obligation to specifically correct defective and nonconforming Work shall be extended by the period of time which elapses between Substantial Completion and completion of the subject Work.
- 11.2.3 Nothing contained in this Paragraph 11.2 shall establish any period of limitation with respect to other obligations, which the Contractor has under the Contract. Establishment of the one (1) year time period in Subparagraph 11.2.2 relates only to the duty of the Contractor to specifically correct Work for each project, and has no

- relationship to the time which the obligation to comply with the Contract Documents may be sought to be enforced.
- 11.3 County May Accept Defective or Nonconforming Work
- 11.3.1 If the County chooses to accept any defective or nonconforming Work, the County may do so. In such events, the Project Price shall be reduced by the greater of (a) the reasonable cost of removing and correcting the defective or nonconforming Work, and (b) the difference between the fair market value of the project had it not been constructed in such manner as to include defective or nonconforming Work. If the remaining portion of the unpaid Project Price, if any, is insufficient to compensate the County for its acceptance or defective or nonconforming Work, the Contractor shall, upon written demand from the County, pay the County such remaining compensation for accepting defective or nonconforming Work.

ARTICLE XII - CONTRACT TERMINATION

- 12.1 Termination by the Contractor
- 12.1.1 For each project, if the Work is stopped for a period of ninety (90) days by an order of any court or as a result of an act of the Government, through no fault of the Contractor or any person or entity working directly or indirectly for the Contractor, the Contractor may, upon ten (10) days written notice to the County, terminate performance under the Contract and recover from the County payment for the actual reasonable expenditures of the Contractor (as limited in Subparagraph 10.3.2 above) for all Work executed and for materials, equipment, tools, construction equipment and machinery actually purchased or rented solely for the Work, less any salvage value of any such items.
- 12.1.2 For each project, if the County shall persistently or repeatedly fail to perform any material obligation to the Contractor for a period of fifteen (15) days after receiving written notice from the Contractor of its intent to terminate if such failure is not substantially corrected within fifteen (15) days, the Contractor may terminate performance under the Contract by written notice to the Project Manager. In such event, the Contractor shall be entitled to recover from the County as though the County had terminated the Contractor's performance under the Contract for convenience pursuant to Subparagraph 12.2.1 hereunder.
- 12.2 Termination by the County
- 12.2.1 For Convenience
- 12.2.1.1The County may terminate the Contract for convenience. In such instance, the County shall provide written notice of such termination to the Contractor specifying when termination shall become effective.
- 12.2.1.2The Contractor shall incur no further obligations in connection with the Work and the Contractor shall stop Work when such termination becomes effective. The Contractor shall also terminate outstanding orders and subcontracts. The Contractor shall settle liabilities and claims arising out of the termination of subcontracts and orders. The County may direct the Contractor to assign the Contractor's right, title and interest under terminated orders or subcontracts to the County or its designee.
- 12.2.1.3The Contractor shall transfer title and deliver to the County for such completed or partially completed Work and materials, equipment, parts, fixtures, information and Contract rights as the Contractor has in either its possession or control.
- 12.2.1.4 (a) The Contractor shall submit a termination claim to the Project Manager specifying the amounts due because of the termination for convenience together with costs, pricing or other data required by the Project Manager. If the Contractor fails to file a termination claim within one (1) year from the effective date of termination of the Contract, the County shall pay the Contractor, an amount derived in accordance with subparagraph (c) below.
 - (b) The County and the Contractor may agree to compensation, if any, due to the Contractor hereunder.
 - (c) Absent an agreement as to the amount due to the Contractor, the County shall pay the Contractor the following amounts:
 - (i) Project Prices for labor, materials, equipment, and other services accepted under the Contract;
 - (ii) Reasonable costs incurred in preparing to perform and in performing a portion of the Work prior to termination and not included in (i) or (ii), and in terminating the Contractor's performance, plus a fair

and reasonable allowance for overhead and profit thereon (such profit shall not include anticipated profit or consequential damages); provided, however, that if it appears that the Contractor would have not profited or would have sustained a loss if the entire Contract had been completed, no profit shall be allowed or included and the amount of compensation shall be reduced to reflect the anticipated rate of loss, if any;

(iii) Reasonable costs of settling and paying claims arising out of the termination of Subcontracts or orders pursuant to Subparagraph 12.2.1.2 of this Paragraph. These costs shall not include amounts paid in accordance with other provisions hereof.

The total sum to be paid the Contractor under this Subparagraph 12.2.1 shall not exceed the total Project Price, as properly adjusted, reduced by the amount of payments otherwise made, and shall in no event include duplication of payment.

12.2.2 For Cause

- 12.2.2.1If the Contractor persistently or repeatedly refuses or fails to perform the Work in a timely manner, supply enough properly skilled Workers, supervisory personnel or proper equipment or materials to complete the Work, or fails to make prompt payment to Subcontractors, or for materials or labor, or persistently disregards laws, ordinances, rules, regulations or orders of any public authority having jurisdiction, or otherwise substantially violates a material provision of the Contract as determined by the County, then the County may, by written notice to the Contractor, without prejudice to any other right or remedy, terminate the Contract and take possession of the project site and of all materials, equipment, tools, construction equipment and machinery thereon owned by the Contractor and may finish the Work by whatever methods it may deem expedient. In such case, the termination of the Contract is effective as of the time that notice of termination is delivered to an authorized representative of the Contractor, or as of the date and time, specified in the notice of termination (whichever is applicable). In such case, the Contractor shall not be entitled to receive any further payment until the Work is completed.
- 12.2.2.2If the unpaid balance of the Project Price less any liquidated damages due under the Contract, exceeds the cost of finishing the Work, including compensation for the Project Manager's additional services and expenses made necessary thereby, such exceed the unpaid balance, the Contractor shall pay the difference to the County. This obligation for payment shall survive the termination of the Contract.
- 12.2.2.3In the event the Contract is terminated by the County for cause pursuant to Subparagraph 12.2.2 and it is subsequently determined by a Court of competent jurisdiction that such termination was without cause, such termination shall thereupon be deemed a Termination for Convenience under Subparagraph 12.2.1 and the provisions of Subparagraph 12.2.1 shall apply.

ARTICLE XIII - INSURANCE

- 13.1 Contractor's Insurance
- 13.1.1 The Contractor shall not commence work under this Contract until he/she has obtained all insurance required under this section and such insurance has been approved by the County. All insurance policies shall be issued by companies authorized to do business under the laws of the State of Florida. The Contractor shall furnish proof of Insurance to the County prior to the commencement of operations. The Certificate(s) shall clearly indicate the Contractor has obtained insurance of the type, amount, and classification as required by contract and that no material change or cancellation of the insurance shall be effective without thirty (30) days prior written notice to the County. Certificates shall specifically include the County as Additional Insured for all lines of coverage except Workers' Compensation and Professional Liability. A copy of the endorsement must accompany the certificate. Compliance with the foregoing requirements shall not relieve the Contractor of its liability and obligations under this Contract.

Certificate Holder Address:

St. Johns County, a political subdivision of the State of Florida

500 San Sebastian View

St. Augustine, FL 32084

13.1.1.1The Contractor shall maintain throughout the life of this Contract, Comprehensive General Liability Insurance with minimum limits of \$1,000,000 per occurrence, \$2,000,000 aggregate to protect the Contractor from claims for damages for bodily injury, including wrongful death, as well as from claims of property damages which may arise from any operations under this Contract, whether such operations be by the Contractor or by anyone directly employed by or contracting with the Contractor.

- 13.1.1.2The Contractor shall maintain during the life of the contract, Professional Liability or Errors and Omissions Insurance with minimum limits of \$1,000,000, if applicable.
- 13.1.1.3The Contractor shall maintain during the life of this Contract, Comprehensive Automobile Liability Insurance with minimum limits of \$2,000,000 combined single limit for bodily injury and property damage liability to protect the Contractor from claims for damages for bodily injury, including the ownership, use, or maintenance of owned and nonowned automobiles, including rented/hired automobiles whether such operations be by the Contractor or by anyone directly or indirectly employed by a Contractor.
- 13.1.1.4The Contractor shall maintain Umbrella or Excess Liability Insurance covering workers compensation, commercial general liability and business auto liability with minimum limits of liability of \$1,000,000.
- 13.1.1.5The Contractor shall maintain during the life of this Contract, adequate Workers' Compensation Insurance in at least such amounts as are required by the law for all of its per Florida Statute 440.02.
- 13.1.1.6In the event of unusual circumstances, the County Administrator, or his designee, may adjust these insurance requirements.
- 13.1.1.7Contractor shall provide the County at least thirty (30) days prior notice of any cancellation of or modification to any insurance coverage required under the Contract.
- 13.1.1.8It is the responsibility of the Contractor to insure that all subcontractors comply with all insurance requirements provided in the Contract.
- 13.1.1.9It is expressly noted that the insurance requirements contained herein are minimum requirements, subject to modification by the County in response to high hazard operations.

ARTICLE XIV - EQUAL EMPLOYMENT OPPORTUNITY

- 14.1 Contractor's Employment Opportunity
- 14.1.1 The Contractor and all Subcontractors shall not discriminate against any employee or applicant for employment because of race, religion, color, sex, national origin or age.
 - The Contractor shall take affirmative measures to insure that applicants are employed, and that employees are treated during employment without regard to their race, religion, color, sex, national origin or age. Such action shall include, but not be limited to, the following: employment, upgrading, demotion or transfer, recruitment or recruitment advertisement, layoff or termination, rates of pay or other forms of compensation, and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices setting forth the policies of non-discrimination.
- 14.1.2 The Contractor and all Subcontractors shall, in all solicitations or advertisements for employees placed by them or on their behalf, state that all qualified applicants shall receive consideration for employment without regard to race, religion, color, sex, national origin or age.

ARTICLE XV – APPRENTICESHIP LAW REQUIREMENTS

- 15.1 Apprenticeship Law (Chapter 446, Florida Statutes)
- 15.1.1 In accordance with applicable Florida law, the Contractor shall make a diligent effort to hire for performance of the Contract a number of apprentices in each occupation which bears to the average number of journeyman in that occupation to be employed in the performance of the Contract, the ratio of at least one (1) apprentice or trainee to every five (5) journeymen.
- 15.1.2 The Contractor shall, when feasible and except when the number of apprentices or trainees to be hired is fewer than four (4), assure that twenty-five (25) percent of such apprentices or trainees are in their first year of training. Feasibility here involves a consideration of the availability of training opportunities for first year apprentices or trainees, the hazardous nature of the Work for beginning workers, and excessive unemployment of apprentices or rainees in their second or subsequent years of training.
- 15.1.3 The Contractor, during the performance of the Contract, shall make diligent efforts to employ the number of apprentices or trainees necessary to meet requirements of Subparagraphs a. and b. However, on-the-job training programs shall only be established in non-apprenticable trades or occupations to meet the requirements of this section.

- 15.1.4 The Contractor agrees to return records of employment, by trade, of the number of apprentices or trainees by first year of training, and the number of journeymen and the wages paid, and hours of work, of such persons on a form as prescribed by the Bureau of Apprenticeship of the Division of Labor at three (3) month intervals. Submission of duplicate copies of forms submitted to the United States Department of Labor shall be sufficient compliance with the provisions of the section.
- 15.1.5 The Contractor agrees to supply the Bureau of Apprenticeship of the Division of Labor, at three (3) months intervals, a statement describing steps taken toward making diligent effort and containing a breakdown by craft or hours worked and wages paid for first year apprentices or trainees, other apprentices or trainees and journeymen.
- 15.1.6 The Contractor agrees to insert in any Subcontract under the Contract the requirements contained in this section. "The term Contractor" as used in such clauses and any Subcontract shall mean the Subcontractor.
- 15.1.7 Anything herein to the Contrary notwithstanding, Contractor agrees to comply with all of the provisions of Florida Statutes 446 and all regulations prescribed by the Bureau of Apprenticeship of the Division of Labor.

ARTICLE XVI – PUBLIC RECORDS

- 16.1 Public Records (Chapter 119, Florida Statues)
- 16.1.1 The cost of reproduction, access to, disclosure, non-disclosure, or exemption of records, data, documents, and/or materials, associated with this Agreement shall be subject to the applicable provisions of the Florida Public Records Law (Chapter 119, Florida Statutes), and other applicable State and Federal provisions. Access to such public records, may not be blocked, thwarted, and/or hindered by placing the public records in the possession of a third party, or an unaffiliated party.
- 16.1.2 In accordance with Florida law, to the extent that Contractor's performance under this Contract constitutes an act on behalf of the County, Contractor shall comply with all requirements of Florida's public records law. Specifically, if Contractor is expressly authorized, and acts on behalf of the County under this Agreement, Contractor shall:
 - (1) Keep and maintain public records that ordinarily and necessarily would be required by the County in order to perform the Services;
 - (2) Upon request from the County's custodian of public records, provide the County with a copy of the requested records or allow the records to be inspected or copied within a reasonable time at a cost that does not exceed the cost as provided in Chapter 119, Florida Statutes, or as otherwise provided by law;
 - (3) Ensure that public records related to this Agreement that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by applicable law for the duration of this Agreement and following completion of this Agreement if the Contractor does not transfer the records to the County; and
 - (4) Upon completion of this Agreement, transfer, at no cost, to the County all public records in possession of the Contractor or keep and maintain public records required by the County to perform the Services.
- 16.1.3 If the Contractor transfers all public records to the County upon completion of this Agreement, the Contractor shall destroy any duplicate public records that are exempt or confidential and exempt from public records disclosure requirements. If the Contractor keeps and maintains public records upon completion of this Agreement, the Contractor shall meet all applicable requirements for retaining public records. All records stored electronically must be provided to the County, upon request from the County's custodian of public records, in a format that is compatible with the County's information technology systems.
- 16.1.4 Failure by the Contractor to comply with the requirements of this section shall be grounds for immediate, unilateral termination of this Agreement by the County.

IF THE CONTRACTOR HAS QUESTIONS REGARDING THE APPLICATION OF CHAPTER 119, FLORIDA STATUTES, TO ITS DUTY TO PROVIDE PUBLIC RECORDS RELATING TO THIS AGREEMENT, CONTACT THE CUSTODIAN OF PUBLIC RECORDS AT: 500 San Sebastian View, St. Augustine, FL 32084, (904) 209-0805, publicrecords@sjcfl.us

ARTICLE XVII - MISCELLANEOUS

- 17.1 Governing Law and Venue
- 17.1.1 The Contract shall be governed by the laws of the State of Florida. Venue for any administrative and/or legal action arising under the Contract shall be St. Johns County, Florida.
- 17.2 Successors and Assigns
- 17.2.1 The County and Contractor bind themselves, their successors, assigns and legal representatives to the other party hereto and to successors, assigns and legal representatives of such other party in respect to covenants, agreements and obligations contained in the Contract. In light of the scope and rationale for the Contract, the Contractor shall not assign the Contract without prior express written consent of the County. However, the County shall not unreasonably deny such written consent, when the interests of the County are not negatively affected. Should the Contractor assign this Contract without securing the prior express written consent of the County, then the County may pursue any legal option available to the County, including, but not limited to, termination of the Contract.
- 17.3 Surety Bonds
- 17.3.1 For each project totaling \$100,000, or more, the Contractor shall furnish a separate Public Construction Bond to the County. Each Bond shall set forth a penal sum in an amount not less than the Project Price. Each Bond furnished by the Contractor shall incorporate by reference the terms of the Contract as fully as though they were set forth verbatim in such Bonds. Each Public Construction Bond shall provide that in the event the Project Price is adjusted by Change Order executed by the Contractor, the Contractor shall obtain a an Amended Public Construction Bond, or a New Public Construction Bond which reflects the adjusted Project Price. Such Amended or New Public Construction Bond shall be provided to the County within ten (10) days of the Change Order being approved to adjust the Project Price. The Public Construction Bond furnished by the Contractor shall be in form suitable to the County and shall be executed by a Surety, or Sureties, reasonably suitable to the County.
- 17.4. Safety of Persons and Property
- 17.4.1 When existing utility lines shown on the Drawings are to be removed or relocated, the Contractor shall notify the Engineer in ample time for taking measures for prevention of the interruption of any required services prior to the beginning of operations. In the event that the Contractor damages any existing utility lines not shown on the Drawings, the location of which is not known to the Contractor, report thereof shall be made immediately to the Engineer.
- 17.4.2 Locations of existing utility lines shown on the Drawings are based upon the best information available to the Engineer, but shall not be considered exact either as to location or number of such lines.
- 17.4.3 Contractor shall protect utility lines constructed pursuant to terms of the Contract and those discovered or shown on Drawings to be existing. Damage occurring to utility lines due to Contractor's operations shall be repaired at no cost to the County.
- 17.5 Amendments
 - It is expressly understood that any change, amendment, modification, revision, or extension of the Contract (other than termination, as noted elsewhere in the Contract) shall be in writing, and shall be executed by duly authorized representatives of both the County and the Contractor.
- 17.6 Compliance with Local, State, and Federal Rules, Regulations, and Laws
 - In performance of the Contract, both the County and the Contractor shall abide by, and comply with, all applicable laws, rules, regulations, orders, and policies, of the Local, State, and Federal governments.
- 17.7 Effect of Failure to Insist on Strict Compliance with Conditions
 - The failure of either party hereto to insist upon strict performance of any term, condition, provision, and/or requirement of the Contract, shall not be construed as a waiver of such term, condition, provision, and/or requirement on any subsequent occasion.
- 17.8 Severability
 - If any word, phrase, sentence, part, subsection, section, or other portion of the Contract, or any application thereof, to any person, or circumstance is declared void, unconstitutional, or invalid for any reason, then such word, phrase, sentence, part, subsection, other portion, or the proscribed application thereof, shall be severable,

and the remaining portions of the Contact, and all applications thereof, not having been declared void, unconstitutional, or invalid shall remain in full force, and effect.

17.9 Execution in Counterparts

The Contract may be executed in counterparts, each of which shall be deemed to be an original, but all of which, taken together, shall constitute one and the same agreement.

17.10 Authority to Execute

Each party covenants to the other party hereto that it has the lawful authority to enter into the Contract and has authorized the execution of the Contract by the party's authorized representative.

17.11 Notice Regarding Public Entity Crimes

Section 287.133(3)(a), Florida Statutes requires the County to notify the Contractor of the provisions of Section 287.133(2)(a), Florida Statutes.

Section 287.133(2)(a), Florida Statutes prohibits a person or affiliate who has been placed on the convicted vendor list maintained by the Florida Department of Management Services, following a conviction from a public entity crime from:

- (a) Contracting to provide goods or services to a public entity;
- (b) Submitting a bid on a contract for construction or repair of a public building or public work;
- (c) Submitting bids on leases of real property to a public entity;
- (d) Being awarded or perform work as a contractor, supplier, subcontractor, or consultant under a contract with any public entity in excess of \$10,000.00.

The prohibitions listed above apply for a period of thirty-six (36) months from the date a person or affiliate is placed on the convicted vendor list.

17.12. Termination Under Section 287.135, Florida Statutes

Notwithstanding any other provision in the Contract to the contrary, the County will have the option, in the exercise of its sole discretion, to immediately terminate the Contract if the Contractor is found to have submitted a false certification under Section 287.135(5), Florida Statutes, or has been placed on the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector List, as described in Section 287.135, Florida Statutes.

17.13. Royalties and Payments

The Contractor hereby certifies that to the best of the Contractor's information, neither the Contractor, nor any process employed by the Contractor, infringes upon any trademark, patent, or other intellectual property rights of another party. Moreover, the Contractor agrees to pay (where required and/or applicable) any, and all, applicable royalties, and or license fees that are associated with any aspect of this Project.

17.14. Permits and Licenses.

To the extent required, the Contractor (at its sole expense) shall secure, obtain, acquire, and maintain permits, approvals, certificates, and/or licenses, in order to perform the Work referenced in the Contract, the Contractor shall be responsible or securing, obtaining, acquiring and maintaining at the Contactor's sole expense, and cost, any, and all, permits, licenses, certificates, and/or approvals required by Federal, State, and/or Local law, rule, regulation, or ordinance.

17.15. Completion of All Required Forms

Throughout the duration of the Contract, the Contractor has an on-going duty to timely complete all forms required by Federal, State, or local law, rule, regulation, or ordinance, and where required, timely submit the required form to the applicable entity/person.

17.16. No Third Party Beneficiaries

Both the County and the Contractor explicitly agree, and the Contract explicitly states that no third party beneficiary status or interest is conferred to, or inferred to, any other person or entity.

17.17. E-Verify

The Contractor agrees that it will enroll and participate in the federal E-verify Program for Employment Verification. The Contractor further agrees to comply with, and abide by, any, and all, applicable rules and provisions associated with the federal E-verify Program for Employment Verification.

17.18. Survival.

It is explicitly noted that the following provisions identified by numbered caption and contained herein shall survive any suspension, termination, cancellation, revocation, expiration and/or non-renewal of the Contract, and therefore shall be both applicable and enforceable beyond any suspension, termination, cancellation, revocation, expiration and/or non-renewal: (1) Article 1.5 (Intent and Interpretation); (2) Article 1.6 Ownership of Contract Documents; (3) Article 7.4 (Warranty); (4) Article 7.12 (Indemnity); (5) Article 11 (Uncovering and Correcting Work); and (6) Article 12.2.2 (Termination for Cause).

IN WITNESS WHEREOF, the Board of County Commissioners of St. Johns County, Florida has made and executed this Contract on behalf of the County and Contractor has hereunto set his/her hand the day and year above written.

COUNTY	CONTRACTOR
St. Johns County, FL (Seal)	Thomas May Construction Company (Seal)
By: Johne Hollean	By: Just March
(County Representative Signature)	/ (Contractor Representative Signature)
Jaime T. Locklear, MPA, CPPB, FCCM	KEITH R. WARD
(Printed Name)	(Printed Name)
Dividence Manager	PRESIDENT
Purchasing Manager (Printed Title)	(Printed Title)
3/29/18	03/26/2018
(Date of Execution)	(Date of Execution)
ATTEST:	ST JOHNS COUNTY
St. Johns County, FL Clerk of Courts	MAR 29 118
By: Rolling L. Place + Deputy Clerk	PURCHASING
Date of Execution	
LEGALLY SUFFICIENT:	
Deputy County Attorney	
4/3/18	
Date of Execution	

RFQ No: 18-05; AS NEEDED SMALL SCALE CONSTRUCTION, RENOVATION & REPAIR SERVICES MASTER CONTRACT # <u>18-MCC-THO-C9-21-5</u> EXHIBIT "A"

The following clauses shall apply to any projects authorized under this Contract, that are funded by, or eligible for reimbursement through, the FEMA Public Assistance Grant Program, or any other state or federal funding source, where the provisions below apply.

FEMA PUBLIC ASSISTANCE PROGRAM REQUIRED CONTRACT CLAUSES

1. Equal Employment Opportunity.

If this contract meets the definition of a "federally assisted construction contract" as provided in 41 C.F.R. § 60-1.3, the following shall apply to the contractor's performance under this contract:

- a. The contractor will not discriminate against any employee or applicant for employment because of race, color, religion, sex, or national origin. The contractor will take affirmative action to ensure that applicants are employed, and that employees are treated during employment without regard to their race, color, religion, sex, or national origin. Such action shall include, but not be limited to the following: Employment, upgrading, demotion, or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices to be provided setting forth the provisions of this nondiscrimination clause.
- b. The contractor will, in all solicitations or advertisements for employees placed by or on behalf of the contractor, state that all qualified applicants will receive considerations for employment without regard to race, color, religion, sex, or national origin.
- c. The contractor will send to each labor union or representative of workers with which he has a collective bargaining agreement or other contract or understanding, a notice to be provided advising the said labor union or workers' representatives of the contractor's commitments under this section, and shall post copies of the notice in conspicuous places available to employees and applicants for employment.
- d. The contractor will comply with all provisions of Executive Order 11246 of September 24, 1965, and of the rules, regulations, and relevant orders of the Secretary of Labor.
- e. The contractor will furnish all information and reports required by Executive Order 11246 of September 24, 1965, and by rules, regulations, and orders of the Secretary of Labor, or pursuant thereto, and will permit access to his books, records, and accounts by the administering agency and the Secretary of Labor for purposes of investigation to ascertain compliance with such rules, regulations, and orders.
- f. In the event of the contractor's noncompliance with the nondiscrimination clauses of this contract or with any of the said rules, regulations, or orders, this contract may be canceled, terminated, or suspended in whole or in part and the contractor may be declared ineligible for further Government contracts or federally assisted construction contracts in accordance with procedures authorized in Executive Order 11246 of September 24, 1965, and such other sanctions as may be imposed and remedies invoked as provided in Executive Order 11246 of September 24, 1965, or by rule, regulation, or order of the Secretary of Labor, or as otherwise provided by law.
- g. The contractor will include the portion of the sentence immediately preceding paragraph (a) and the provisions of paragraphs (a) through (g) in every subcontract or purchase order unless exempted by rules, regulations, or orders of the Secretary of Labor issued pursuant to section 204 of Executive Order 11246 of September 24, 1965, so that such provisions will be binding upon each subcontractor or vendor. The contractor will take such action with respect to any subcontract or purchase order as the administering agency may direct as a means of enforcing such provisions, including sanctions for noncompliance: Provided, however, That in the event a contractor becomes involved in, or is threatened with, litigation with a subcontractor or vendor as a result of such direction by the administering agency the contractor may request the United States to enter into such litigation to protect the interests of the United States."

For the purposes of this section, "federally assisted construction contract" means any agreement or modification thereof between any applicant and a person for construction work which is paid for in whole or in part with funds

obtained from the Government or borrowed on the credit of the Government pursuant to any Federal program involving a grant, contract, loan, insurance, or guarantee, or undertaken pursuant to any Federal program involving such grant, contract, loan, insurance, or guarantee, or any application or modification thereof approved by the Government for a grant, contract, loan, insurance, or guarantee under which the applicant itself participates in the construction work.

For the purposes of this section, "construction work" means the construction, rehabilitation, alteration, conversion, extension, demolition or repair of buildings, highways, or other changes or improvements to real property, including facilities providing utility services. The term also includes the supervision, inspection, and other onsite functions incidental to the actual construction.

2. Contract Work Hours and Safety Standards Act.

- **a.** This section applies to all contracts in excess of \$100,000 that involve the employment of mechanics or laborers as provided in 40 U.S.C. § 3701.
- b. As provided in 40 U.S.C. § 3702, the contractor shall compute the wages of every mechanic and laborer on the basis of a standard work week of 40 hours. Work in excess of the standard work week is permissible provided that the worker is compensated at a rate of not less than one and a half times the basic rate of pay for all hours worked in excess of 40 hours in the work week.
- c. The requirements of 40 U.S.C. § 3704 shall apply to construction work and provide that no laborer or mechanic must be required to work in surroundings or under working conditions which are unsanitary, hazardous or dangerous. These requirements do not apply to the purchases of supplies or materials or articles ordinarily available on the open market, or contracts for transportation or transmission of intelligence.
- d. No contractor or subcontractor contracting for any part of the contract work which may require or involve the employment of laborers or mechanics shall require or permit any such laborer or mechanic in any workweek in which he or she is employed on such work to work in excess of forty hours in such workweek unless such laborer or mechanic receives compensation at a rate not less than one and one-half times the basic rate of pay for all hours worked in excess of forty hours in such workweek.
- e. In the event of any violation of the clause set forth in paragraph (d) of this section the contractor and any subcontractor responsible therefor shall be liable for the unpaid wages. In addition, such contractor and subcontractor shall be liable to the United States (in the case of work done under contract for the District of Columbia or a territory, to such District or to such territory), for liquidated damages. Such liquidated damages shall be computed with respect to each individual laborer or mechanic, including watchmen and guards, employed in violation of the clause set forth in paragraph (d) of this section, in the sum of \$10 for each calendar day on which such individual was required or permitted to work in excess of the standard workweek of forty hours without payment of the overtime wages required by the clause set forth in paragraph (d) of this section.
- f. The County shall upon its own action or upon written request of an authorized representative of the Department of Labor withhold or cause to be withheld, from any moneys payable on account of work performed by the contractor or subcontractor under any such contract or any other Federal contract with the same prime contractor, or any other federally-assisted contract subject to the Contract Work Hours and Safety Standards Act, which is held by the same prime contractor, such sums as may be determined to be necessary to satisfy any liabilities of such contractor or subcontractor for unpaid wages and liquidated damages as provided in the clause set forth in paragraph (e) of this section.
- g. The contractor or subcontractor shall insert in any subcontracts the clauses set forth in paragraph (c) through (f) of this section and also a clause requiring the subcontractors to include these clauses in any lower tier subcontracts. The prime contractor shall be responsible for compliance by any subcontractor or lower tier subcontractor with the clauses set forth in paragraphs (c) through (f) of this section.

3. Compliance with Clean Air Act.

a. The contractor agrees to comply with all applicable standards, orders or regulations issued pursuant to the Clean Air Act, as amended, 42 U.S.C. § 7401 et seq.

- b. The contractor agrees to report each violation to the County and understands and agrees that the County will, in turn, report each violation as required to assure notification to the state of Florida, Federal Emergency Management Agency, and the appropriate Environmental Protection Agency Regional Office.
- c. The contractor agrees to include these requirements in each subcontract exceeding \$100,000 financed in whole or in part with Federal assistance provided by FEMA.

4. Compliance with Federal Water Pollution Control Act.

- a. The contractor agrees to comply with all applicable standards, orders or regulations issued pursuant to the Federal Water Pollution Control Act, as amended, 33 U.S.C. 1251 et seq.
- b. The contractor agrees to report each violation to the County and understands and agrees that the County will, in turn, report each violation as required to assure notification to the state of Florida, Federal Emergency Management Agency, and the appropriate Environmental Protection Agency Regional Office.
- c. The contractor agrees to include these requirements in each subcontract exceeding \$100,000 financed in whole or in part with Federal assistance provided by FEMA.

5. Debarment and Suspension.

- a. This contract is a covered transaction for purposes of 2 C.F.R. pt. 180 and 2 C.F.R. pt. 3000. As such the contractor is required to verify that none of the contractor, its principals (defined at 2 C.F.R. § 180.995), or its affiliates (defined at 2 C.F.R. § 180.905) are excluded (defined at 2 C.F.R. § 180.940) or disqualified (defined at 2 C.F.R. § 180.935).
- b. The contractor must comply with 2 C.F.R. pt. 180, subpart C and 2 C.F.R. pt. 3000, subpart C and must include a requirement to comply with these regulations in any lower tier covered transaction it enters into.
- c. This certification is a material representation of fact relied upon by the County. If it is later determined that the contractor did not comply with 2 C.F.R. pt. 180, subpart C and 2 C.F.R. pt. 3000, subpart C, in addition to remedies available to the state of Florida and the County, the Federal Government may pursue available remedies, including but not limited to suspension and/or debarment.
- d. The bidder or proposer agrees to comply with the requirements of 2 C.F.R. pt. 180, subpart C and 2 C.F.R. pt. 3000, subpart C while this offer is valid and throughout the period of any contract that may arise from this offer. The bidder or proposer further agrees to include a provision requiring such compliance in its lower tier covered transactions.

6. Byrd Anti-Lobbying Amendment

Contractors who apply or bid for an award of \$100,000 or more shall file the required certification. Each tier certifies to the tier above that it will not and has not used Federal appropriated funds to pay any person or organization for influencing or attempting to influence an officer or employee of any agency, a member of Congress, officer or employee of Congress, or an employee of a member of Congress in connection with obtaining any Federal contract, grant, or any other award covered by 31 U.S.C. § 1352. Each tier shall also disclose any lobbying with non-Federal funds that takes place in connection with obtaining any Federal award. Such disclosures are forwarded from tier to tier up to the recipient.

APPENDIX A, 44 C.F.R. PART 18: CERTIFICATION REGARDING LOBBYING

Certification for Contracts, Grants, Loans, and Cooperative Agreements (To be submitted with each bid or offer exceeding \$100,000)

The undersigned [Contractor] certifies, to the best of his or her knowledge, that:

1. No Federal appropriated funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of an agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with the awarding of any Federal contract, the making of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any Federal contract, grant, loan, or cooperative agreement.

- 2. If any funds other than Federal appropriated funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form-LLL, "Disclosure Form to Report Lobbying," in accordance with its instructions.
- 3. The undersigned shall require that the language of this certification be included in the award documents for all subawards at all tiers (including subcontracts, subgrants, and contracts under grants, loans, and cooperative agreements) and that all subrecipients shall certify and disclose accordingly.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by 31, U.S.C. § 1352 (as amended by the Lobbying Disclosure Act of 1995). Any person who fails to file the required certification shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.

The Contractor, certifies or affirms the truthfulness and accuracy of each statement of its certification and disclosure, if any. In addition, the Contractor understands and agrees that the provisions of 31 U.S.C. § 3801 et seq., apply to this certification and disclosure, if any.

Signature of Contractor's Authorized Official

Name and Title of Contractor's Authorized Official

Date

7. Procurement of Recovered Materials.

- a. In the performance of this contract, the Contractor shall make maximum use of products containing recovered materials that are EPA- designated items unless the product cannot be acquired
 - i. Competitively within a timeframe providing for compliance with the contract performance schedule;
 - ii. Meeting contract performance requirements; or
 - iii. At a reasonable price.

8. DHS Seal, Logo, and Flags.

The contractor shall not use the DHS seal(s), logos, crests, or reproductions of flags or likenesses of DHS agency officials without specific FEMA pre-approval.

9. Compliance with Federal Law, Regulations, and Executive Orders.

This is an acknowledgement that FEMA financial assistance will be used to fund the contract only. The contractor will comply will all applicable federal law, regulations, executive orders, FEMA policies, procedures, and directives.

10. No Obligation by Federal Government.

The Federal Government is not a party to this contract and is not subject to any obligations or liabilities to the non-Federal entity, contractor, or any other party pertaining to any matter resulting from the contract.

11. Fraud and False or Fraudulent or Related Acts.

The contractor acknowledges that 31 U.Ş.C. Chap. 38 (Administrative Remedies for False Claims and Statements) applies to the contractor's actions pertaining to this contract.



St. Johns County Board of County Commissioners

Purchasing Division

April 4, 2018

Thomas May Construction Company 310 College Drive Orange Park, FL 32065

RE: RFQ No: 18-05 - As Needed Small Scale Construction, Renovation & Repair Services

Master Contract No: 18-MCC-THO-09215

Dear Mr. Ward:

Attached, please find a fully executed original copy of the Contract Agreement for your files.

All work under this contract will be authorized by Task Orders. No work shall be performed without an executed Task Order, issued by the SJC Purchasing Department. In the event the County requests a proposal from your firm regarding a specific project, any and all instructions for the proposal will be included in the request. Please note that any projects in excess of \$100,000.00 will require a Public Construction Bond.

If you have any questions regarding this contract, you may contact me at the information below.

Thank you for doing business with St. Johns County.

Sincerely,

St. Johns County, FL

Purchasing Department

Jaime T. Locklear, MPA, CPPB, FCCM

Purchasing Manager

(904) 209-0158 - Direct

(904) 209-0159 - Fax

(904) 209-0150 - Main

jlocklear@sjcfl.us

CC:

SJC Minutes & Records (Copy taken when attested)

SJC Purchasing RFQ 18-05- Thomas May Construction Company - Master Contract File
